

Sewer System Evaluation and Rehabilitation Program

Capacity Project

Contract Number	3813
Name	New 18-inch Force Main from Pump Station 3 to the intersection of Olive Street and Carrollton Avenue
Basin	Carrollton
Council Districts	A, B
Status:	Phase 3.
	This project is in the Preliminary Design phase.

Resources

SSERP Project Engineer MWH

Design Engineer Weston Solutions, Inc.

Contractor


Comments

3813 - New 18-inch FM from SPS 3 to the Intersection of Olive and Carrollton

Description

This force main project, in the Carrollton basin, consists of approximately 2,400 feet of 18-inch FM. The new force main will run from PS 3, along Olive St., to Carrollton Ave. and tie into the new 42-inch FM, as shown in **Figure 1**. Pump Station 3 currently discharges to gravity. Its flow is re-pumped by PS 5, then by PS A, before reaching the treatment plant. This new force main will tie PS 3 to the new force main network, allowing it to pump directly to the treatment plant.

Figure 1
Project Location

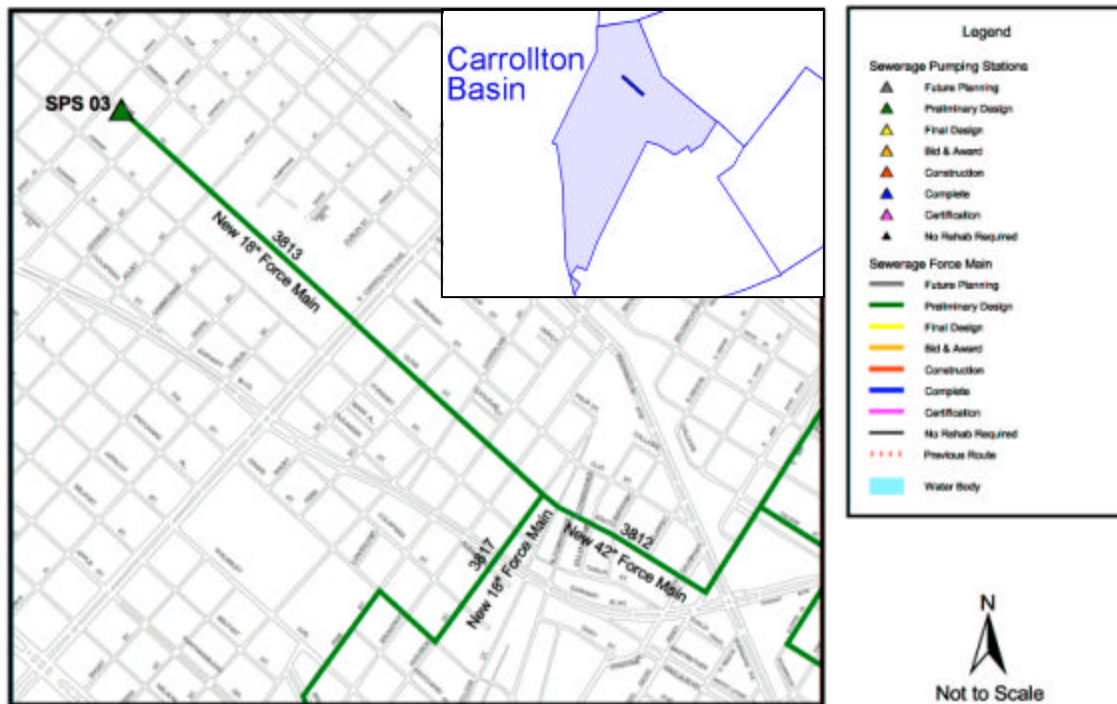

Current Capital Cost \$2,052,593

Description	Projected Start	Target Start	Projected Finish	Target Finish	%	Budgeted Cost	1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018											
							Gantt Chart Timeline											
3813 FM from SPS 3 to Carrollton at Olive																		
Pre-Design	18JUN03 A	18JUN03	16DEC03 A	16DEC03	100	0												
Preliminary Design	14JAN04 A	14JAN04	20SEP05	02FEB05	52	61,551												
Final Design	05OCT05	02FEB05	23MAY06	09JAN06	0	90,234												
Pre-Advertisement	31MAY06	18JAN06	06SEP06	12APR06	0	0												
Advertisement	13SEP06	12APR06	20OCT06	12MAY06	0	4,785												
Award	20OCT06	12MAY06	10APR07	31OCT06	0	1,595												
Construction	10APR07	31OCT06	03FEB08	27AUG07	0	1,700,000												
Field Testing	10APR07	31OCT06	04MAR08	26SEP07	0	25,500												
ESDC	10APR07	31OCT06	04MAR08	26SEP07	0	12,928												
Inspection Services	10APR07	31OCT06	04MAR08	26SEP07	0	136,000												
Construction Final	04FEB08	27AUG07	04MAR08	26SEP07	0	0												
S&WB Acceptance	18JUN08	25DEC07	18JUN08	26DEC07	0	0												
Certification	21MAR09	27SEP08	18JUN09	26DEC08	0	20,000												

Data date 01MAR05

**Sewerage & Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule**

- Early bar
- Target bar
- Progress bar
