

Sewer System Evaluation and Rehabilitation Program

Capacity Project

Contract Number 3809

Name New 42-inch Force Main from intersection of Carrollton and Palmyra to Pump Station 8

Basin Mid-City

Council Districts A, B, C, D

Status: Phase 3.

This project is in the Preliminary Design phase.

Resources

SSERP Project Engineer MWH

Design Engineer Weston Solutions


Contractor

Comments

3809 - New 42-inch FM from Carrollton and Palmyra to SPS 8

This project, in the Mid-City basin, consists of approximately 8,200 feet of 42-inch FM. This new force main will run from the intersection of Carrollton and Palmyra, along Carrollton to Orleans Ave, then along Orleans to Broad, tying in to the new 54-inch FM. **Figure 1** shows the project location. Currently, Pump Stations 1, 3, and 6 discharge to gravity and the flow is re-pumped twice before reaching the treatment plant. This new force main will allow these stations to transmit flow directly to the treatment plant.

Figure 1
Project Location

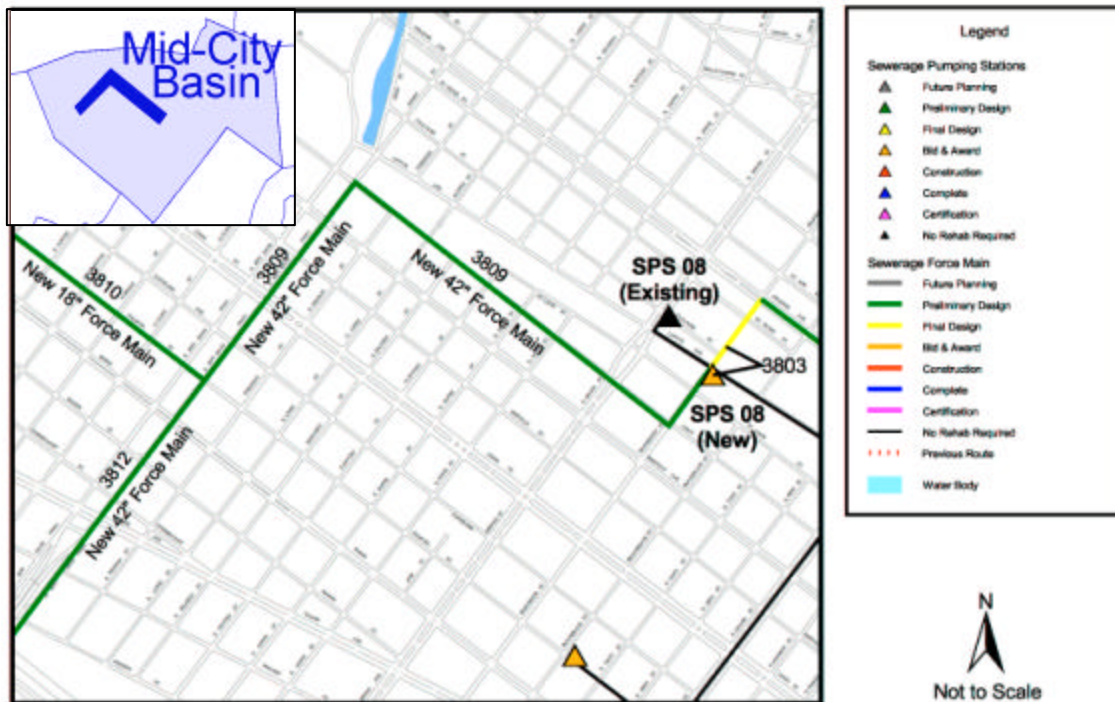

Current Capital Cost \$5,190,075

Description	Projected Start	Target Start	Projected Finish	Target Finish	%	Budgeted Cost	1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018											
							Gantt Chart Timeline											
3809 Sewer FM Carrollton at Palmyra to SPS 8																		
Pre-Design	18JUN03 A	18JUN03	16DEC03 A	16DEC03	100	0	Pre-Design											
Preliminary Design	14JAN04 A	14JAN04	17OCT05	02FEB05	53	152,190	Preliminary Design											
Final Design	18OCT05	02FEB05	05JUN06	09JAN06	0	151,619	Final Design											
Pre-Advertisement	31MAY06	22MAR06	06SEP06	14JUN06	0	0	Pre-Advertisement											
Advertisement	13SEP06	14JUN06	19OCT06	17JUL06	0	9,514	Advertisement											
Award	19OCT06	17JUL06	10APR07	04JAN07	0	3,171	Award											
Construction	10APR07	04JAN07	03FEB08	31OCT07	0	4,400,000	Construction											
Field Testing	10APR07	04JAN07	05MAR08	30NOV07	0	66,000	Field Testing											
ESDC	10APR07	04JAN07	05MAR08	30NOV07	0	35,581	ESDC											
Inspection Services	10APR07	04JAN07	05MAR08	30NOV07	0	352,000	Inspection Services											
Construction Final	04FEB08	31OCT07	05MAR08	30NOV07	0	0	Construction Final Completion											
S&WB Acceptance	18JUN08	28FEB08	18JUN08	29FEB08	0	0	S&WB Acceptance											
Certification	20MAR09	01DEC08	17JUN09	01MAR09	0	20,000	Certification											

Data date 01MAR05

**Sewerage & Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule**

- Early bar
- Target bar
- Progress bar
