

*Sewer System Evaluation and Rehabilitation Program*

**Capacity Project**

---

<b>Contract Number</b>	3845
<b>Name</b>	Redundant 24-inch Force Main from Pump Station Bullard to Pump Station Wright
<b>Basin</b>	New Orleans East
<b>Council Districts</b>	D, E
<b>Status:</b>	Phase 5.
	Preliminary Design is scheduled to begin in March 2005.

**Resources**

**SSERP Project Engineer** MWH

**Design Engineer** Digital Engineering and Imaging, Inc.

**Contractor**


**Comments**

# 3845 - Redundant 24-inch FM from SPS Bullard to SPS Wright

## Description

This project, in the New Orleans East basin, consists of approximately 2,500 feet of 24-inch FM. The proposed force main will tie into the existing 16-inch FM at the intersection of Bullard Ave. and Lake Forest Blvd, continue down Lake Forest Blvd. and then tie into the proposed 12-inch FM from PS Wright. This route is shown in **Figure 1**. This proposed force main will provide an additional discharge route for Wright and Lake Forest Pump Stations. It will also provide additional redundancy for other stations on the eastern end of the New Orleans East basin.

**Figure 1**  
**Project Location**

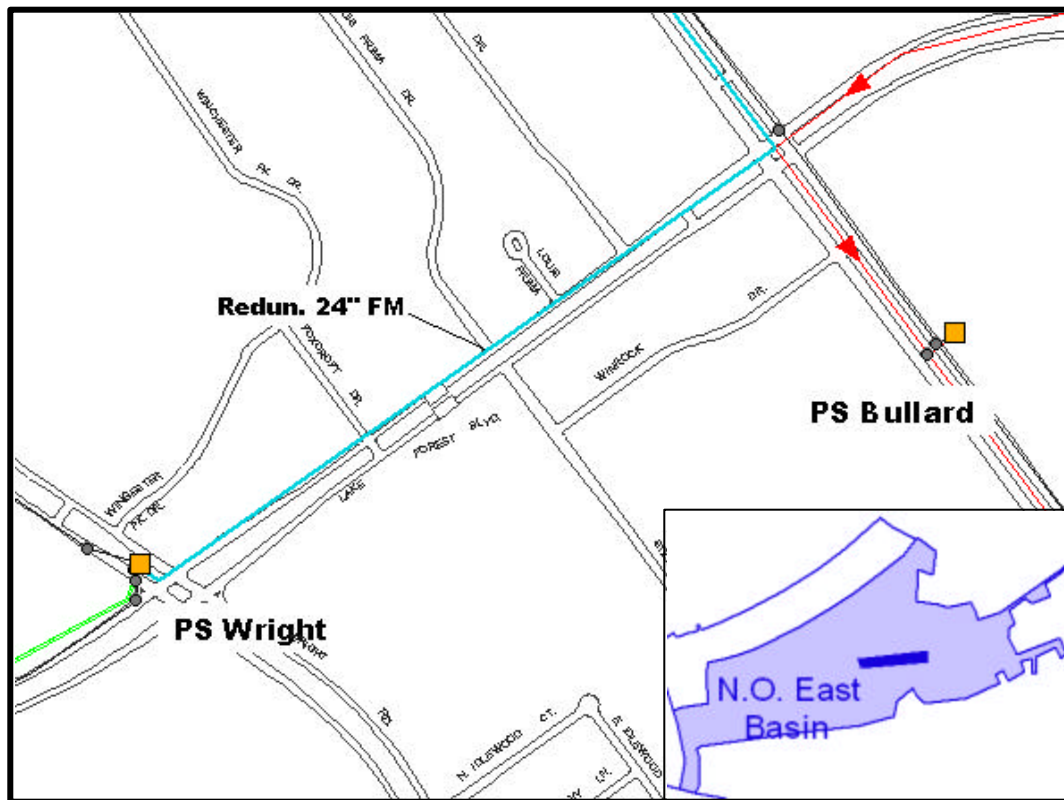

**Current Capital Cost**      \$1,206,879.

Description	Projected Start	Target Start	Projected Finish	Target Finish	%	Budgeted Cost	1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018											
							Gantt chart area with a vertical red line at 2005.											
3845 Redund. FM from SPS Bullard to SPS Wright																		
Pre-Design	22SEP04 A	18AUG04	03MAR05	11AUG05	92	0	Pre-Design											
Preliminary Design	04MAR05	12AUG05	07FEB06	18JUL06	0	51,023	Preliminary Design											
Final Design	08FEB06	19JUL06	16JAN07	25JUN07	0	68,138	Final Design											
Pre-Advertisement	25JUL07	22AUG07	07NOV07	13NOV07	0	0	Pre-Advertisement											
Advertisement	14NOV07	14NOV07	21DEC07	13DEC07	0	6,048	Advertisement											
Award	21DEC07	14DEC07	10JUN08	03JUN08	0	2,016	Award											
Construction	10JUN08	04JUN08	07SEP08	01SEP08	0	953,300	Construction											
Field Testing	10JUN08	04JUN08	07OCT08	01OCT08	0	14,300	Field Testing											
ESDC	10JUN08	04JUN08	07OCT08	01OCT08	0	15,790	ESDC											
Inspection Services	10JUN08	04JUN08	07OCT08	01OCT08	0	76,264	Inspection Services											
Construction Final	08SEP08	02SEP08	07OCT08	01OCT08	0	0	Construction Final Completion											
S&WB Acceptance	21JAN09	31DEC08	21JAN09	31DEC08	0	0	S&WB Acceptance											
Certification	23OCT09	03OCT09	20JAN10	31DEC09	0	20,000	Certification											

Data date 01MAR05

**Sewerage & Water Board of New Orleans  
Sewer System Evaluation and Rehabilitation Program  
Master Schedule**

- Early bar
- Target bar
- Progress bar
