

Sewer System Evaluation and Rehabilitation Program

Capacity Project

Contract Number 3854

Name Redundant 48-inch Force Main from Pump Station Aurora to Pump Station Blair

Basin Algiers

Council Districts C

Status: Phase 6.

Preliminary Design is scheduled to begin in 2012.

Resources

SSERP Project Engineer MWH

Design Engineer

Contractor

Comments


Attended the Aurora West Neighborhood Watch/Civic Association meeting of January 25, 2001

3854 - Redundant 48-inch FM from SPS Aurora to SPS Blair

Description


This project consists of approximately 3,650 feet of 48-inch FM. The proposed force main will extend from the existing 12-inch FM near PS Aurora to PS Blair. **Figure 1** shows the project location. Currently, PS Aurora pumps into a 12-inch FM connecting to the 48-inch FM along General De Gaulle Blvd. This proposed force main will provide redundancy for the 48-inch FM along along General De Gaulle Blvd.

Figure 1
Project Location

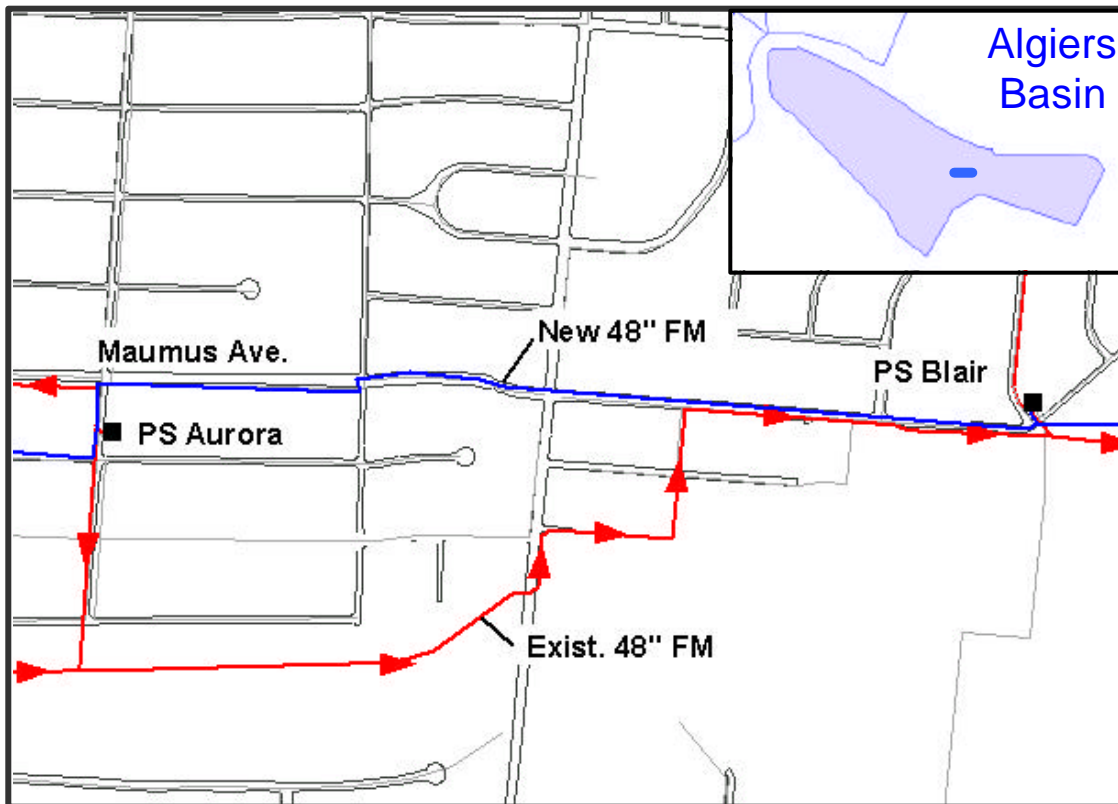

Current Capital Cost \$2,033,749.

Description	Projected Start	Baseline Start	Projected Finish	Baseline Finish	%	Budgeted Cost																												
							1997	1998	1999	2000	2001	2002	2003	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	2023	2024
3854 Red. SFM from SPS Aurora to SPS Blair																																		
Pre-Design	17AUG11	17AUG11	09AUG12	09AUG12	0	0																												
Preliminary Design	08AUG12	10AUG12	16JUL13	18JUL13	0	44,000																												
Final Design	17JUL13	19JUL13	23JUN14	25JUN14	0	131,000																												
Pre-Advertisement	25JUN14	16JUL14	01OCT14	07OCT14	0	0																												
Advertisement	08OCT14	08OCT14	21NOV14	06NOV14	0	4,400																												
Award	21NOV14	07NOV14	12MAY15	28APR15	0	17,600																												
Construction	12MAY15	29APR15	07DEC15	24NOV15	0	1,639,040																												
Field Testing	12MAY15	29APR15	06JAN16	24DEC15	0	24,586																												
ESDC	12MAY15	29APR15	06JAN16	24DEC15	0	22,000																												
Inspection Services	12MAY15	29APR15	06JAN16	24DEC15	0	131,123																												
Construction Final	08DEC15	25NOV15	06JAN16	24DEC15	0	0																												
S&WB Resolution	20APR16	24MAR16	20APR16	24MAR16	0	0																												
Certification	20JAN17	26DEC16	19APR17	25MAR17	0	20,000																												

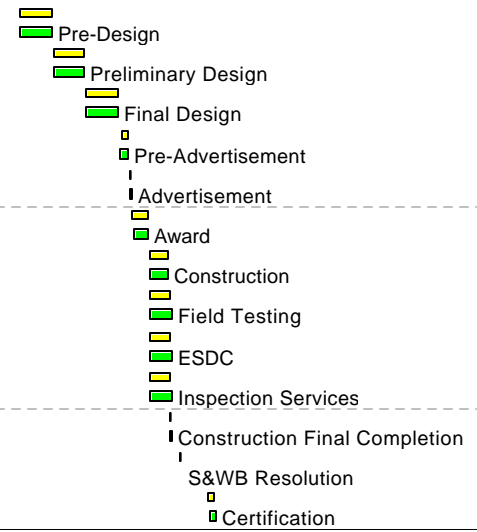

Data date	01SEP04
© Primavera Systems, Inc.	

Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule
