

Sewer System Evaluation and Rehabilitation Program

Capacity Project

Contract Number	3851
Name	Redundant 48-inch Force Main from Pump Station Blair to West Bank Waste Water Treatment Plant
Basin	Algiers
Council Districts	C
Status:	Phase 6. Preliminary Design is scheduled to begin in 2012.

Resources

SSERP Project Engineer MWH

Design Engineer

Contractor

Comments


Attended the Aurora West Neighborhood Watch/Civic Association meeting of January 25, 2001

3851 - Redundant 48-inch FM from SPS Blair to WBWWTP

Description


This project consists of approximately 7,750 feet of 48-inch FM. The proposed force main will extend from PS Blair, underneath the Intercoastal Waterway, to the existing 48-inch FM near the WBWWTP. **Figure 1** shows the project location. Currently, PS Blair pumps into a 10-inch FM connecting to the 48-inch FM crossing the Intracoastal Waterway. This proposed force main will provide redundancy for the 48-inch FM crossing the Intracoastal Waterway.

Figure 1
Project Location

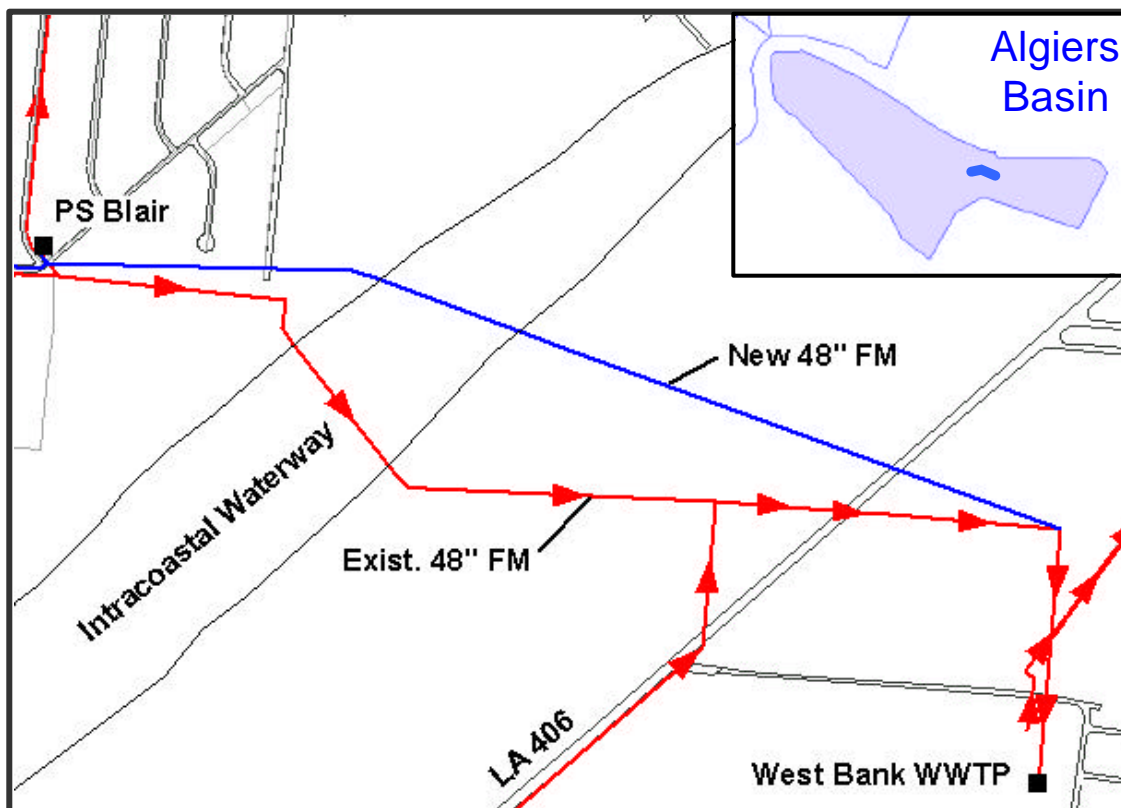

Current Capital Cost \$4,294,704.

Description	Projected Start	Baseline Start	Projected Finish	Baseline Finish	%	Budgeted Cost																												
							1997	1998	1999	2000	2001	2002	2003	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	2023	2024
3851 Red. SFM from SPS Blair to WBWWTP																																		
Pre-Design	16MAR11	16MAR11	08MAR12	08MAR12	0	0																												
Preliminary Design	07MAR12	09MAR12	12FEB13	14FEB13	0	92,000																												
Final Design	04FEB13	06FEB13	10JAN14	14JAN14	0	277,000																												
Pre-Advertisement	23DEC13	15JAN14	02APR14	08APR14	0	0																												
Advertisement	09APR14	09APR14	16MAY14	08MAY14	0	36,800																												
Award	16MAY14	09MAY14	03NOV14	27OCT14	0	9,200																												
Construction	03NOV14	28OCT14	30JUN15	24JUN15	0	3,482,834																												
Field Testing	03NOV14	28OCT14	30JUL15	24JUL15	0	52,243																												
ESDC	03NOV14	28OCT14	30JUL15	24JUL15	0	46,000																												
Inspection Services	03NOV14	28OCT14	30JUL15	24JUL15	0	278,627																												
Construction Final	01JUL15	25JUN15	30JUL15	24JUL15	0	0																												
S&WB Resolution	18NOV15	23OCT15	18NOV15	23OCT15	0	0																												
Certification	20AUG16	25JUL16	17NOV16	22OCT16	0	20,000																												

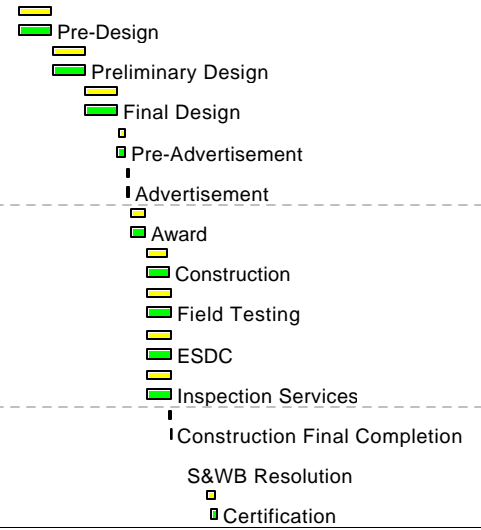

Data date 01SEP04

© Primavera Systems, Inc.

**Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule**
