

Sewer System Evaluation and Rehabilitation Program

Capacity Project

Contract Number	3856
Name	Redundant 42-inch Force Main from Pump Station Huntlee to Pump Station Eton
Basin	Algiers
Council Districts	C
Status:	Phase 6. Preliminary Design is scheduled to begin in 2014.

Resources

SSERP Project Engineer MWH

Design Engineer

Contractor

Comments


Attended the Aurora West Neighborhood Watch/Civic Association meeting of January 25, 2001

3856 - Redundant 42-inch FM from SPS Huntlee to SPS Eton

Description


This project consists of approximately 5,690 feet of 42-inch FM. The proposed force main will extend from the existing 12-inch FM near PS Huntlee to the existing 16-inch FM near PS Eton. **Figure 1** shows the project location. Currently, PS Huntlee pumps into a 12-inch FM connecting to the 48-inch FM along General De Gaulle Blvd. This proposed force main will provide redundancy for the 48-inch FM along along General De Gaulle Blvd.

Figure 1
Project Location

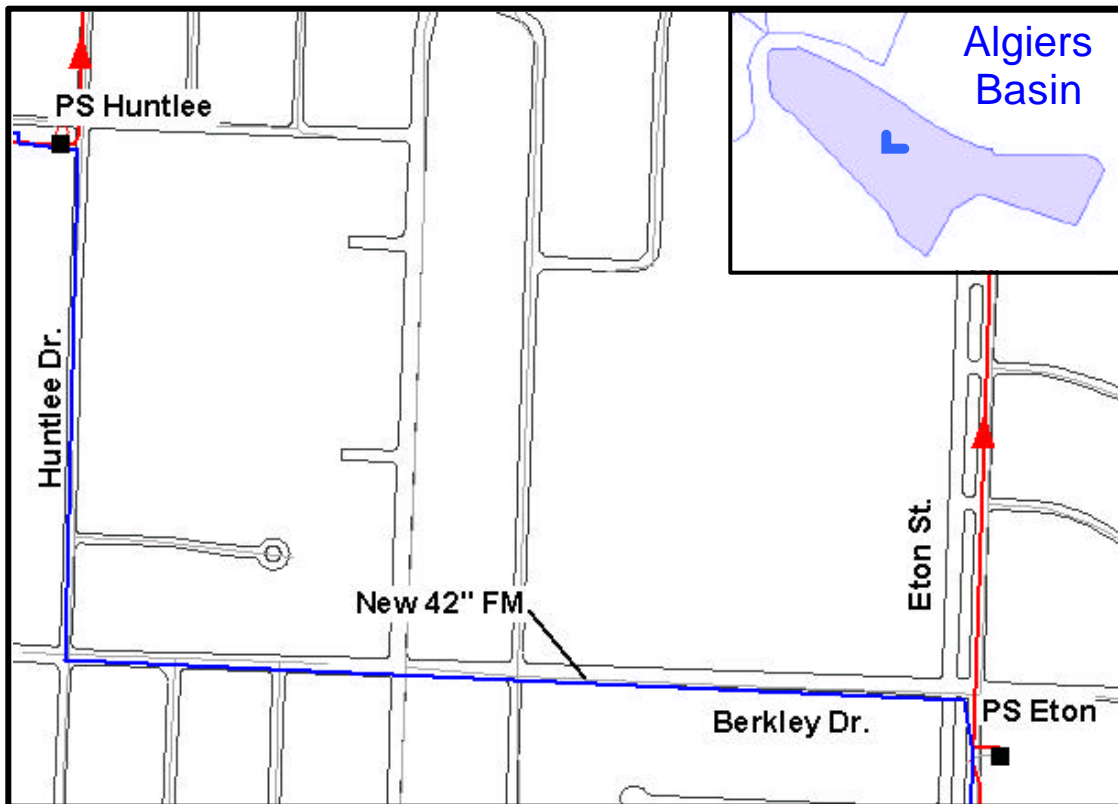

Current Capital Cost \$2,870,364.

Description	Projected Start	Baseline Start	Projected Finish	Baseline Finish	%	Budgeted Cost																												
							1997	1998	1999	2000	2001	2002	2003	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	2023	2024
3856 Red. SFM from SPS Huntlee to SPS Eton																																		
Pre-Design	17APR13	17APR13	14APR14	14APR14	0	0																												
Preliminary Design	11APR14	15APR14	19MAR15	23MAR15	0	62,000																												
Final Design	20MAR15	24MAR15	24FEB16	26FEB16	0	185,000																												
Pre-Advertisement	24FEB16	16MAR16	01JUN16	07JUN16	0	0																												
Advertisement	08JUN16	08JUN16	15JUL16	08JUL16	0	24,800																												
Award	15JUL16	11JUL16	30DEC16	26DEC16	0	6,200																												
Construction	30DEC16	27DEC16	27JUL17	24JUL17	0	2,320,881																												
Field Testing	30DEC16	27DEC16	26AUG17	23AUG17	0	34,813																												
ESDC	30DEC16	27DEC16	26AUG17	23AUG17	0	31,000																												
Inspection Services	30DEC16	27DEC16	26AUG17	23AUG17	0	185,670																												
Construction Final	28JUL17	25JUL17	26AUG17	23AUG17	0	0																												
S&WB Resolution	20DEC17	22NOV17	20DEC17	22NOV17	0	0																												
Certification	21SEP18	25AUG18	19DEC18	22NOV18	0	20,000																												

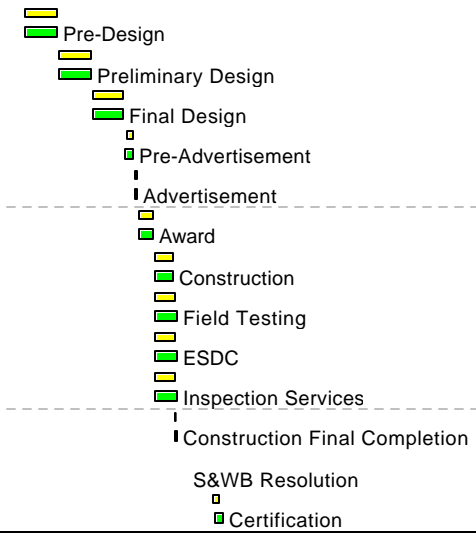

Data date 01SEP04

© Primavera Systems, Inc.

**Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule**
