

Sewer System Evaluation and Rehabilitation Program

Planning Task

Name	South Shore CSES
Basin	South Shore
Council Districts	D, E

Progress

Percent Complete	91 %
-------------------------	------

Resources

SSERP Project Engineer	MWH
Consultant	Brown and Caldwell


Comments

Notice to proceed was issued and work began on this project on February 26, 2004. The Consent Decree milestone due date for submittal of the final report to the USEPA is April 1, 2005.

Description

Study to be performed to evaluate the condition and capacity of the collection system in the Southshore basin, including all pump stations in order to determine if the condition and capacity of the collection system are sufficient to prevent unauthorized discharges.

Project Location

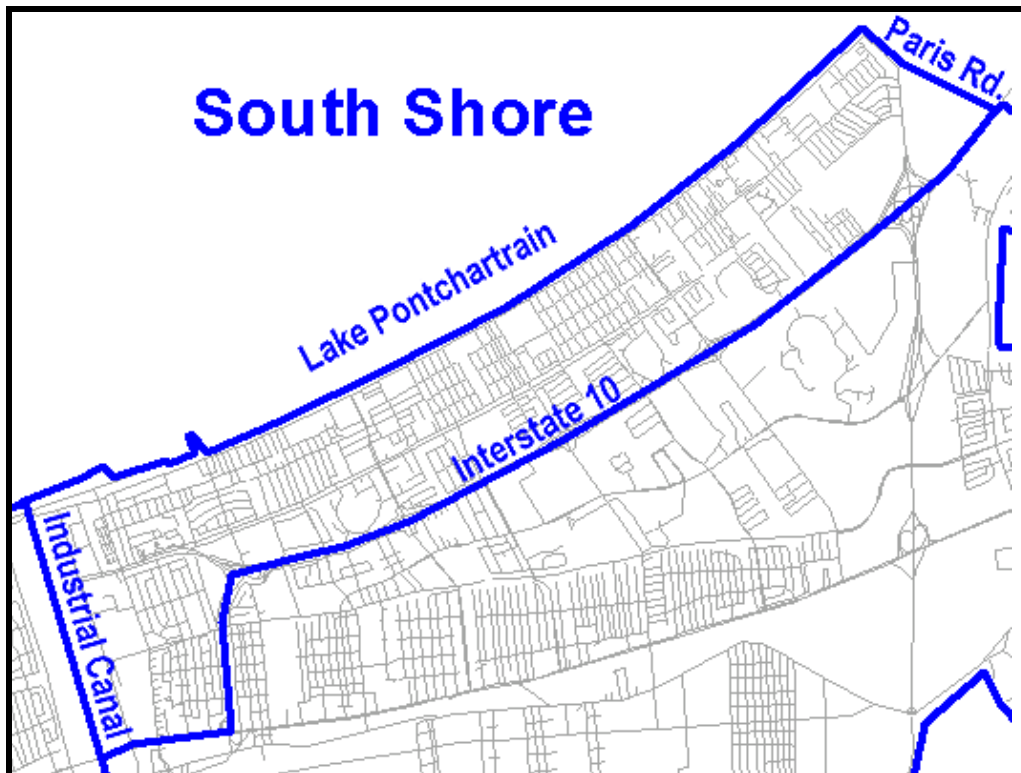

Current Capital Cost \$2,395,068

Description	Projected Start	Target Start	Projected Finish	Target Finish	%	Budgeted Cost	1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018											
							Gantt chart area with grid lines for years 1997-2018.											
South Shore CSES																		
CSES	26FEB04 A	26FEB04	23MAR05	10FEB05	91	2,395,068												

Data date 01MAR05
© Primavera Systems, Inc.

Sewerage & Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule

- Early bar
- Target bar
- Progress bar
