

*Sewer System Evaluation and Rehabilitation Program*

**Rehabilitation Project**

---

**Contract Number** 3920

**Name** CBD/FQ Area Sewer Rehabilitation Phase 2 Point Repair

**Basin** CBD/FQ

**Council Districts** B, C

**Status:** This project is in the Construction phase.

**Resources**

**SSERP Project Engineer** MWH

**Design Engineer** Camp, Dresser, & McKee, Inc.

**Contractor** Boh Bros. Construction Co., LLC

**Comments**

A Public Hearing was held for the Central Business District/French Quarter/Warehouse District basin on October 30, 2000. Attended the French Quarter Property Owners Association meeting on May 9, 2001. Attended the French Quarter Business Association meeting on April 17, 2002.


## 3920 - CBD/FQ Area Sewer Rehabilitation Phase 2 Point Repair

---

### Description

Rehabilitation consisting of 12 external main line point repairs, 125 external service or lateral line point repairs and 480 lineal feet of 8" pipe replacement.

### Project Location

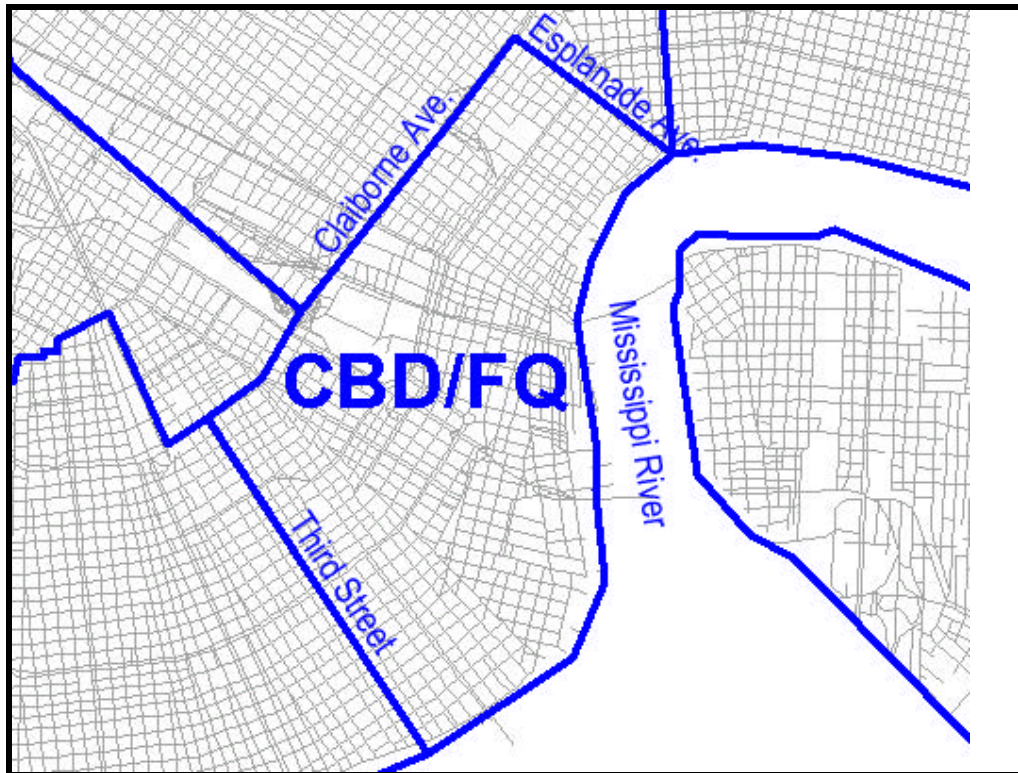

**Current Capital Cost**    \$1,499,243

Description	Projected Start	Target Start	Projected Finish	Target Finish	%	Budgeted Cost	1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018											
							Gantt Chart Timeline											
3920 CBD/FQ Sewer Rehab. Phase 2 Point Repair																		
Pre-Design	10OCT98 A	10OCT98	20NOV98 A	20NOV98	100	0												
Preliminary Design	08FEB99 A	08FEB99	25MAY99 A	25MAY99	100	29,092												
Final Design	01OCT99 A	01OCT99	01NOV01 A	01NOV01	100	61,756												
Pre-Advertisement	25MAR03 A	25MAR03	03JUL03 A	03JUL03	100	0												
Advertisement	09JUL03 A	09JUL03	15AUG03 A	15AUG03	100	8,425												
Award	15AUG03 A	15AUG03	01DEC03 A	01DEC03	100	4,637												
Construction	01DEC03 A	01DEC03	08APR05	12OCT04	92	1,208,809												
Field Testing	01DEC03 A	01DEC03	08MAY05	11NOV04	92	18,132												
ESDC	01DEC03 A	01DEC03	08MAY05	11NOV04	92	13,156												
Inspection Services	01DEC03 A	01DEC03	08MAY05	11NOV04	92	132,969												
Construction Final	09APR05	13OCT04	08MAY05	11NOV04	0	0												
S&WB Acceptance	17AUG05	10FEB05	17AUG05	10FEB05	0	0												
Certification	19MAY06	13NOV05	16AUG06	10FEB06	0	20,000												

Data date 01MAR05

**Sewerage & Water Board of New Orleans  
Sewer System Evaluation and Rehabilitation Program  
Master Schedule**

- Early bar
- Target bar
- Progress bar
