

Sewer System Evaluation and Rehabilitation Program

Rehabilitation Project

| | |
|--------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Contract Number | 3918 |
| Name | CBD/FQ Area Sewer Rehabilitation Phase 1 Manhole Rehabilitation |
| Basin | CBD/FQ |
| Council Districts | B, C |
| Status: | The Sewerage and Water Board accepted as complete all work performed under this contract at the Board meeting on March 20, 2002. Certification of this project, as required by USEPA Assistance Grant No. XP-986042-01-0, was completed February 28, 2003. |

Resources

SSERP Project Engineer MWH

Design Engineer Camp, Dresser, & McKee, Inc.

Contractor D&O Contractors, Inc.

Comments


A Public Hearing was held for the Central Business District/French Quarter/Warehouse District basin on October 30, 2000. Attended the French Quarter Property Owners Association meeting on May 9, 2001. Attended the French Quarter Business Association meeting on April 17, 2002.

3918 - CBD/FQ Area Sewer Rehabilitation Phase 1 Manhole Rehabilitation

Description

Rehabilitation consisting of approximately 220 sanitary sewer manholes.

Project Location

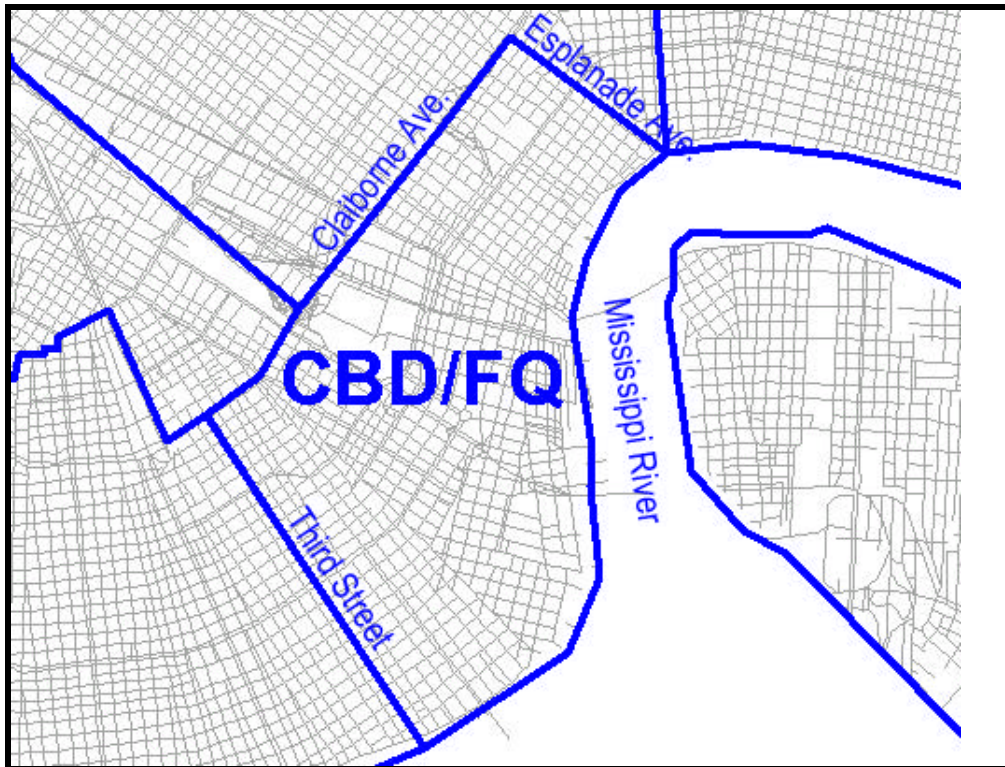

Current Capital Cost \$670,952

| Description | Projected Start | Baseline Start | Projected Finish | Baseline Finish | % | Budgeted Cost | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
|---------------------------------------------------|-----------------|----------------|------------------|-----------------|-----|---------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------|------|------|------|------|------|------|------|------|------|------|------|------|------|------|------|------|------|------|------|------|------|------|------|------|------|------|
| | | | | | | | 1997 | 1998 | 1999 | 2000 | 2001 | 2002 | 2003 | 2004 | 2005 | 2006 | 2007 | 2008 | 2009 | 2010 | 2011 | 2012 | 2013 | 2014 | 2015 | 2016 | 2017 | 2018 | 2019 | 2020 | 2021 | 2022 | 2023 | 2024 |
| 3918 CBD/FQ Phase 1 Manhole Rehabilitation | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Pre-Design | 10OCT98 A | 10OCT98 | 20NOV98 A | 20NOV98 | 100 | 0 | <ul style="list-style-type: none"> Pre-Design <ul style="list-style-type: none"> Preliminary Design Final Design Advertisement Award Construction Field Testing ESDC Inspection Services S&WB Resolution Certification | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Preliminary Design | 08FEB99 A | 08FEB99 | 25MAY99 A | 25MAY99 | 100 | 29,092 | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Final Design | 28JUN99 A | 28JUN99 | 02NOV00 A | 02NOV00 | 100 | 55,823 | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Advertisement | 15NOV00 A | 15NOV00 | 14DEC00 A | 14DEC00 | 100 | 8,425 | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Award | 15DEC00 A | 15DEC00 | 28FEB01 A | 28FEB01 | 100 | 4,637 | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Construction | 26APR01 A | 26APR01 | 19OCT01 A | 19OCT01 | 100 | 479,839 | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Field Testing | 26APR01 A | 26APR01 | 19OCT01 A | 19OCT01 | 100 | 7,198 | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| ESDC | 26APR01 A | 26APR01 | 19OCT01 A | 19OCT01 | 100 | 13,156 | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Inspection Services | 26APR01 A | 26APR01 | 19OCT01 A | 19OCT01 | 100 | 52,782 | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| S&WB Resolution | 20MAR02 A | 20MAR02 | 20MAR02 A | 20MAR02 | 100 | 0 | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Certification | 21DEC02 A | 21DEC02 | 28FEB03 A | 28FEB03 | 100 | 20,000 | | | | | | | | | | | | | | | | | | | | | | | | | | | | |

Data date 01SEP04

© Primavera Systems, Inc.

**Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule**
