

Sewer System Evaluation and Rehabilitation Program

Rehabilitation Project

Contract Number	3914
Name	CBD/FQ Sewer Rehabilitation, Sewer Line Cleaning & CCTV Inspection
Basin	CBD/FQ
Council Districts	B, C
Status:	The Sewerage and Water Board accepted as complete all work performed under this contract at the Board meeting on August 21, 2002. Certification of this project, as required by USEPA Assistance Grant No. XP-996732-01-2, was completed August 21, 2003.

Resources

SSERP Project Engineer MWH

Design Engineer Camp, Dresser, & McKee, Inc.

Contractor Insituform Technologies, Inc.

Comments


A Public Hearing was held for the Central Business District/French Quarter/Warehouse District basin on October 30, 2000. Attended the French Quarter Property Owners Association meeting on May 9, 2001. Attended the French Quarter Business Association meeting on April 17, 2002.

3914 - CBD/FQ Sewer Rehabilitation, Sewer Line Cleaning & CCTV Inspection

Description

Cleaning and CCTV inspection of approximately 346,800 lineal feet of 6"-45" main lines, cleaning of 10,000 feet of 54"-72" main lines, cleaning of 325 service laterals, and CCTV inspection of 145 service laterals.

Project Location

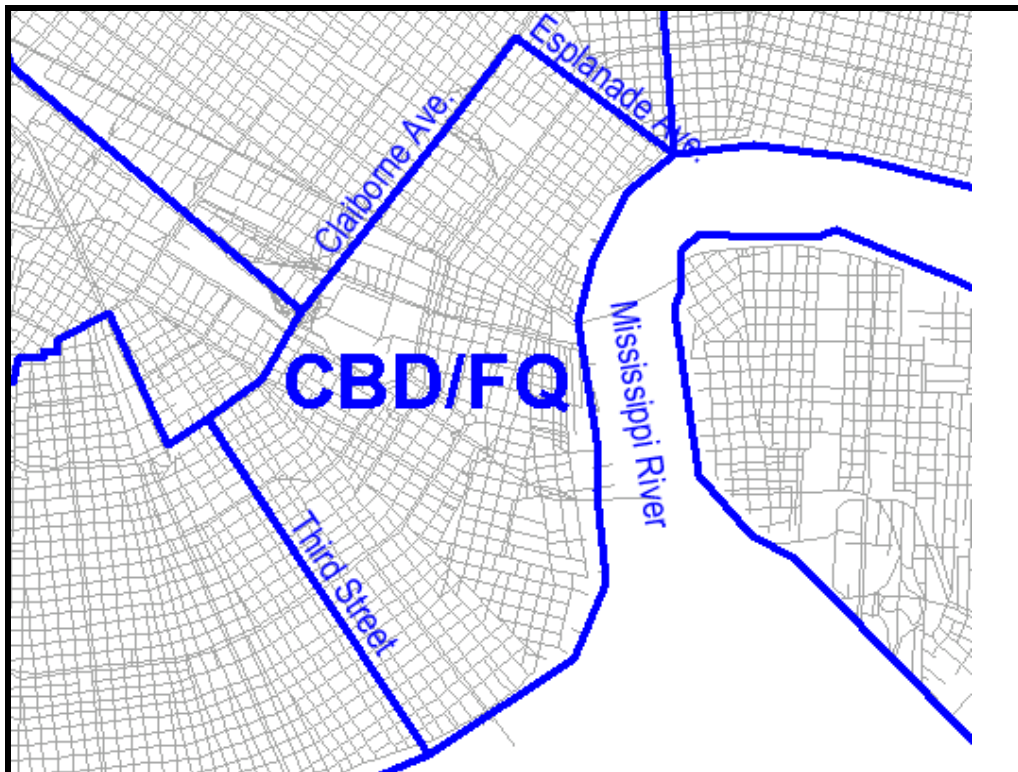

Current Capital Cost \$1,265,881

Description	Projected Start	Baseline Start	Projected Finish	Baseline Finish	%	Budgeted Cost	1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018											
							Gantt chart area with a vertical red line at 2004.											
3914 CBD/FQ Cleaning & CCTV Inspection																		
Pre-Design	10OCT98 A	10OCT98	20NOV98 A	20NOV98	100	0	Pre-Design											
Preliminary Design	08FEB99 A	08FEB99	25MAY99 A	25MAY99	100	29,092	Preliminary Design											
Final Design	28JUN99 A	28JUN99	11APR00 A	11APR00	100	47,158	Final Design											
Advertisement	12APR00 A	12APR00	12MAY00 A	12MAY00	100	8,425	Advertisement											
Award	12MAY00 A	12MAY00	25SEP00 A	25SEP00	100	4,637	Award											
Construction	30OCT00 A	30OCT00	31MAY02 A	31MAY02	100	1,048,120	Construction											
Field Testing	30OCT00 A	30OCT00	31MAY02 A	31MAY02	100	0	Field Testing											
ESDC	30OCT00 A	30OCT00	31MAY02 A	31MAY02	100	13,156	ESDC											
Inspection Services	30OCT00 A	30OCT00	31MAY02 A	31MAY02	100	115,293	Inspection Services											
Construction Final	01JUN02 A	01JUN02	28JUN02 A	28JUN02	100	0	Construction Final Completion											
S&WB Resolution	21AUG02 A	21AUG02	21AUG02 A	21AUG02	100	0	S&WB Resolution											
Certification	21AUG03 A	21AUG03	21AUG03 A	21AUG03	100	0	Certification											

Data date 01NOV04

© Primavera Systems, Inc.

**Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule**

- Early bar
- Target bar
- Progress bar
