

Sewer System Evaluation and Rehabilitation Program

Rehabilitation Project

Contract Number 3933

Name Gentilly Area Sewer Manhole Rehabilitation No. 2

Basin Gentilly

Council Districts D, E

Status: Final Acceptance and Resolution (R-166-2004) was issued by the Board on October 20, 2004.

Resources

SSERP Project Engineer MWH

Design Engineer CH2M Hill

Contractor Boh Bros. Construction Co., L.L.C.


Comments

Attended the Edgewood Park Civic Association meeting of January 20, 2004. Attended the Edgewood Park Civic Association meeting of February 17, 2004. Attended the Edgewood Park Civic Association meeting of April 20, 2004.

Description

Rehabilitation consisting of 328 manhole frame and cover replacements, 138 frame and cover adjustments, 465 isolation pad installations, 155 full depth manhole liners, 279 manhole partial depth liners, 485 frame to corbel seal installations, 5 inflow dish installations, and associated restoration.

Project Location

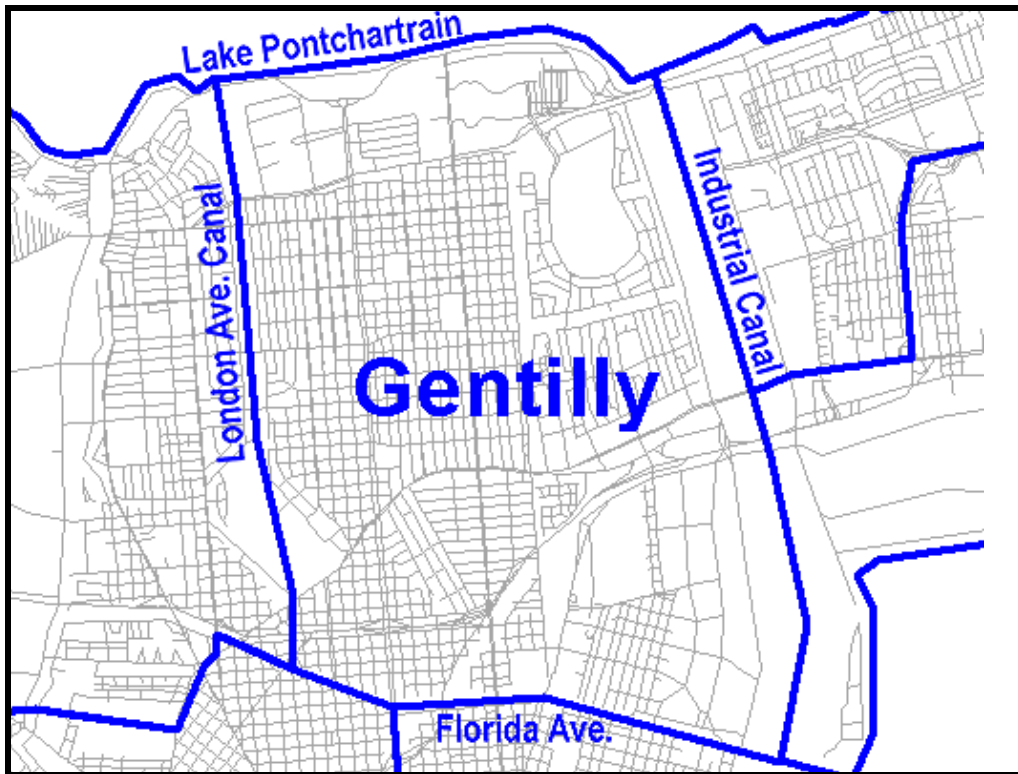

Current Capital Cost \$986,279

Description	Projected Start	Baseline Start	Projected Finish	Baseline Finish	%	Budgeted Cost	1997												1998												1999												2000												2001												2002												2003												2004												2005												2006												2007												2008												2009												2010												2011												2012												2013												2014												2015												2016												2017												2018											
3933 Gentilly Manhole Rehabilitation #2																																																																																																																																																																																																																																																																														
Pre-Design	19NOV99 A	19NOV99	01MAR00 A	01MAR00	100	0																																																																																																																																																																																																																																																																								
Preliminary Design	01MAR00 A	01MAR00	20JUL00 A	20JUL00	100	50,844																																																																																																																																																																																																																																																																								
Final Design	17AUG01 A	17AUG01	21FEB03 A	21FEB03	100	33,792																																																																																																																																																																																																																																																																								
Pre-Advertisement	20AUG02 A	20AUG02	05MAR03 A	05MAR03	100	0																																																																																																																																																																																																																																																																								
Advertisement	12MAR03 A	12MAR03	11APR03 A	11APR03	100	3,613																																																																																																																																																																																																																																																																								
Award	11APR03 A	11APR03	25AUG03 A	25AUG03	100	1,204																																																																																																																																																																																																																																																																								
Construction	25AUG03 A	25AUG03	02APR04 A	02APR04	100	766,376																																																																																																																																																																																																																																																																								
Field Testing	25AUG03 A	25AUG03	07JUN04 A	07JUN04	100	11,496																																																																																																																																																																																																																																																																								
ESDC	25AUG03 A	25AUG03	07JUN04 A	07JUN04	100	24,653																																																																																																																																																																																																																																																																								
Inspection Services	25AUG03 A	25AUG03	07JUN04 A	07JUN04	100	84,301																																																																																																																																																																																																																																																																								
Construction Final	02APR04 A	02APR04	07JUN04 A	07JUN04	100	0																																																																																																																																																																																																																																																																								
S&WB Resolution	20OCT04 A	15SEP04	20OCT04 A	15SEP04	100	0																																																																																																																																																																																																																																																																								
Certification	22JUL05	18JUN05	19OCT05	15SEP05	0	10,000																																																																																																																																																																																																																																																																								

Data date 01NOV04

© Primavera Systems, Inc.

Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule

- Early bar
- Target bar
- Progress bar
