

*Sewer System Evaluation and Rehabilitation Program*

**Rehabilitation Project**

---

**Contract Number** 3927

**Name** Gentilly Sewer Rehab Pipe Replacement Nos. 1 & 2

**Basin** Gentilly

**Council Districts** D, E

**Status:** Final Acceptance and Resolution (R-164-2004) was issued by the Board on October 20, 2004.

**Resources**

**SSERP Project Engineer** MWH

**Design Engineer** CH2M Hill

**Contractor** Boh Bros. Construction Co., L.L.C.


**Comments**

Attended the Edgewood Park Civic Association meeting of January 20, 2004. Attended the Edgewood Park Civic Association meeting of February 17, 2004. Attended the Edgewood Park Civic Association meeting of April 20, 2004.

**Description**

Rehabilitation by replacement of 14 sewer mainlines and associated service connections and approximately 1,700 feet of lateral replacements, including temporary and final restoration.

**Project Location**

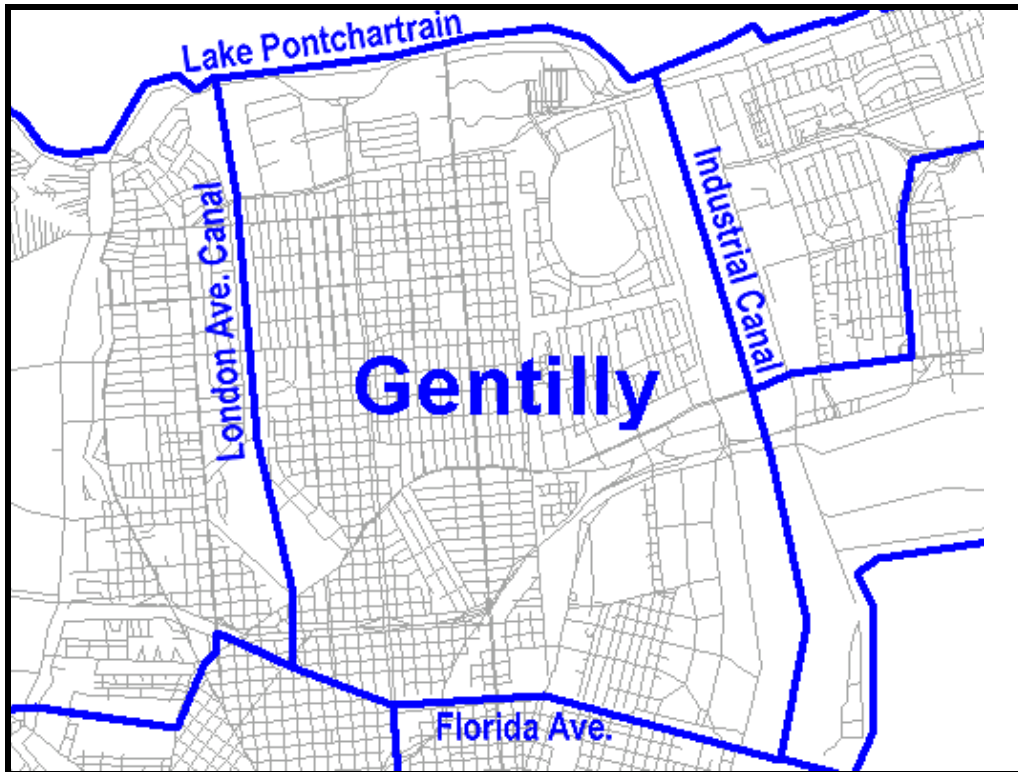

**Current Capital Cost**     \$854,572

Description	Projected Start	Baseline Start	Projected Finish	Baseline Finish	%	Budgeted Cost	1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018											
							Gantt chart area with year markers and task bars.											
<b>3927 Gentilly Sewer Rehab. Pipe Replace #1 &amp; #2</b>																		
Pre-Design	19NOV99 A	19NOV99	01MAR00 A	01MAR00	100	0	Pre-Design											
Preliminary Design	01MAR00 A	01MAR00	20JUL00 A	20JUL00	100	134,916	Preliminary Design											
Final Design	08JUN01 A	08JUN01	05AUG02 A	05AUG02	100	77,126	Final Design											
Pre-Advertisement	02JAN02 A	02JAN02	07AUG02 A	07AUG02	100	0	Pre-Advertisement											
Advertisement	14AUG02 A	14AUG02	20SEP02 A	20SEP02	100	7,225	Advertisement											
Award	20SEP02 A	20SEP02	05MAR03 A	05MAR03	100	2,408	Award											
ESDC	05MAR03 A	05MAR03	30SEP03 A	10SEP03	100	24,552	ESDC											
Construction	05MAR03 A	05MAR03	30SEP03 A	10SEP03	100	522,973	Construction											
Field Testing	05MAR03 A	05MAR03	30SEP03 A	10SEP03	100	7,845	Field Testing											
Inspection Services	05MAR03 A	05MAR03	30SEP03 A	10SEP03	100	57,527	Inspection Services											
Construction Final	10SEP03 A	10SEP03	30SEP03 A	30SEP03	100	0	Construction Final Completion											
S&WB Resolution	20OCT04 A	18AUG04	20OCT04 A	18AUG04	100	0	S&WB Resolution											
Certification	22JUL05	21MAY05	19OCT05	18AUG05	0	20,000	Certification											

Data date 01NOV04

© Primavera Systems, Inc.

**Sewerage and Water Board of New Orleans  
Sewer System Evaluation and Rehabilitation Program  
Master Schedule**

- Early bar
- Target bar
- Progress bar
