

Sewer System Evaluation and Rehabilitation Program

Rehabilitation Project

Contract Number 3932

Name Gentilly Area Sewer Manhole Rehabilitation No. 1

Basin Gentilly

Council Districts D, E

Status: Board Final Acceptance and Resolution (R-097-2004) was issued by the Board on July 21, 2004.

Resources

SSERP Project Engineer MWH

Design Engineer CH2M Hill

Contractor D & O Contractors, Inc.


Comments

Attended the Edgewood Park Civic Association meeting of January 20, 2004. Attended the Edgewood Park Civic Association meeting of February 17, 2004. Attended the Edgewood Park Civic Association meeting of April 20, 2004.

Description

Rehabilitation consisting of manhole rehabilitation, including 405 manhole frame and cover replacements, 93 frame and cover adjustments, 498 isolation pad installation, 253 full depth manhole liners, 243 manhole partial depth liners, 529 frame to corbel seal installation and 5 inflow dish installations.

Project Location

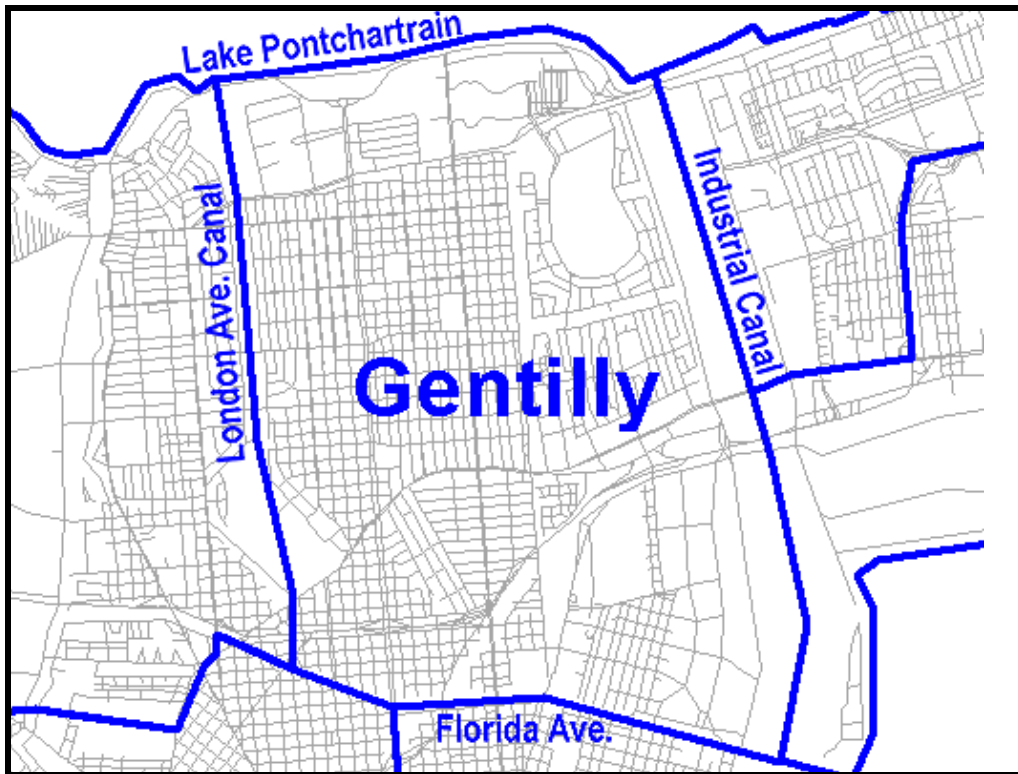

Current Capital Cost \$1,275,100

Description	Projected Start	Baseline Start	Projected Finsh	Baseline Finish	%	Budgeted Cost	1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018											
							Gantt chart area with year markers from 1997 to 2018.											
3932 Gentilly Manhole Rehabilitation #1																		
Pre-Design	19NOV99 A	19NOV99	01MAR00 A	01MAR00	100	0	Pre-Design											
Preliminary Design	01MAR00 A	01MAR00	20JUL00 A	20JUL00	100	50,844	Preliminary Design											
Final Design	08JUN01 A	08JUN01	05FEB02 A	05FEB02	100	33,792	Final Design											
Pre-Advertisement	20AUG02 A	20AUG02	06FEB03 A	06FEB03	100	0	Pre-Advertisement											
Advertisement	12FEB03 A	12FEB03	14MAR03 A	14MAR03	100	3,613	Advertisement											
Award	14MAR03 A	14MAR03	18AUG03 A	18AUG03	100	1,204	Award											
Construction	18AUG03 A	18AUG03	13APR04 A	13APR04	100	1,023,105	Construction											
Field Testing	18AUG03 A	18AUG03	23APR04 A	23APR04	100	15,347	Field Testing											
ESDC	18AUG03 A	18AUG03	23APR04 A	23APR04	100	24,653	ESDC											
Inspection Services	18AUG03 A	18AUG03	23APR04 A	23APR04	100	112,542	Inspection Services											
Construction Final	14APR04 A	14APR04	23APR04 A	23APR04	100	0	Construction Final Completion											
S&WB Resolution	21JUL04 A	21JUL04	21JUL04 A	21JUL04	100	0	S&WB Resolution											
Certification	22APR05	23APR05	20JUL05	21JUL05	0	10,000	Certification											

Data date 01NOV04

© Primavera Systems, Inc.

**Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule**

- Early bar
- Target bar
- Progress bar
