

Sewer System Evaluation and Rehabilitation Program

Rehabilitation Project

Contract Number	3925
Name	Gentilly Area Sewer Rehabilitation Point Repair No. 1
Basin	Gentilly
Council Districts	D, E
Status:	The Sewerage and Water Board accepted as complete all work performed under this contract at the Board meeting on April 16, 2003. Certification of this project, as required by USEPA Assistance Grant No. XP-986258-01-0, is due for completion April 16, 2004. Certification activities began on this project in January 2004.

Resources

SSERP Project Engineer MWH

Design Engineer CH2M Hill

Contractor Wallace C. Drennan

Comments


Attended the St. Gabriel ACT meeting of October 20, 2003. Attended the Edgewood Park Civic Association meeting of November 18, 2003. Attended the Edgewood Park Civic Association meeting of January 20, 2004. Attended the Edgewood Park Civic Association meeting of February 17, 2004.

3925 - Gentilly Area Sewer Rehabilitation Point Repair No. 1

Description

Rehabilitation by 277 external service repairs, 79 main line point repairs and 32 lateral replacements.

Project Location

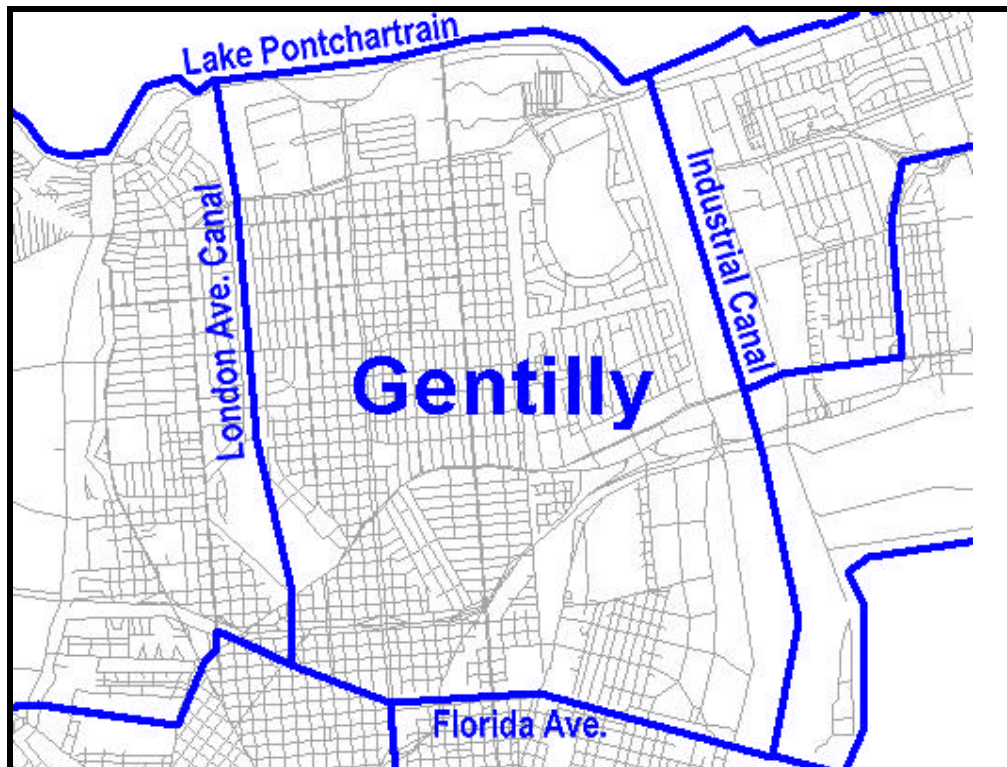

Current Capital Cost \$2,253,944

Description	Projected Start	Baseline Start	Projected Finish	Baseline Finish	%	Budgeted Cost																								
							1997	1998	1999	2000	2001	2002	2003	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015	2016	2017	2018	2019	2020
3925 Gentilly Sewer Rehab. Point Repair #1																														
Pre-Design	19NOV99 A	19NOV99	01MAR00 A	01MAR00	100	0	<ul style="list-style-type: none"> □ Pre-Design 																							
Preliminary Design	01MAR00 A	01MAR00	20JUL00 A	20JUL00	100	37,221	<ul style="list-style-type: none"> □ Preliminary Design 																							
Final Design	07AUG00 A	07AUG00	23JAN01 A	23JAN01	100	33,792	<ul style="list-style-type: none"> □ Final Design 																							
Advertisement	14FEB01 A	14FEB01	23MAR01 A	23MAR01	100	3,613	<ul style="list-style-type: none"> □ Advertisement 																							
Award	23MAR01 A	23MAR01	23JUL01 A	23JUL01	100	1,204	<ul style="list-style-type: none"> □ Award 																							
Construction	23JUL01 A	23JUL01	07MAR02 A	07MAR02	100	1,867,399	<ul style="list-style-type: none"> □ Construction 																							
Field Testing	23JUL01 A	23JUL01	07MAR02 A	07MAR02	100	34,428	<ul style="list-style-type: none"> □ Field Testing 																							
ESDC	23JUL01 A	23JUL01	07MAR02 A	07MAR02	100	50,873	<ul style="list-style-type: none"> □ ESDC 																							
Inspection Services	23JUL01 A	23JUL01	07MAR02 A	07MAR02	100	205,414	<ul style="list-style-type: none"> □ Inspection Services 																							
Construction Final	07MAR02 A	07MAR02	06APR02 A	06APR02	100	0	<ul style="list-style-type: none"> □ Construction Final Completion 																							
S&WB Resolution	16APR03 A	16APR03	16APR03 A	16APR03	100	0	<ul style="list-style-type: none"> □ S&WB Resolution 																							
Certification	16JAN04 A	16JAN04	15APR04 A	15APR04	100	20,000	<ul style="list-style-type: none"> □ Certification 																							

Data date	01SEP04
© Primavera Systems, Inc.	

**Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule**
