

## *Sewer System Evaluation and Rehabilitation Program*

### Rehabilitation Project

---

<b>Contract Number</b>	3903
<b>Name</b>	East Lakeview Area Sewer Rehabilitation Phase 2 Pipe Repairs No. 1
<b>Basin</b>	Lakeview
<b>Council Districts</b>	A, D
<b>Status:</b>	The Sewerage and Water Board certified as complete all the work performed under this contract, as required by USEPA Assistance Grant No. XP-986042-01-0, in February 2002.

#### Resources

**SSERP Project Engineer** Montgomery Watson Harza

**Design Engineer** Evans Graves Engineers, Inc.

**Contractor** Boh Bros. Construction Co., LLC

#### Comments

Attended the Lakeview Civic Improvement Association meeting of March 14, 2001. Attended the Lakeview Civic Improvement Association meeting of May 9, 2001. Attended the Lakeview Civic Improvement Association meeting of July 11, 2001. Attended the Lakeview Civic Improvement Association meeting of November 14, 2001.


## 3903 - East Lakeview Area Sewer Rehabilitation Phase 2 Pipe Repairs No. 1

---

### Description

Rehabilitation by excavation of existing sanitary sewer 8"-18" diameter including 59 external point repairs, 45 external service connection repairs, 2,860 lineal feet of existing sewer service lateral replacements and associated restoration. Point repair length = 12 feet

### Project Location

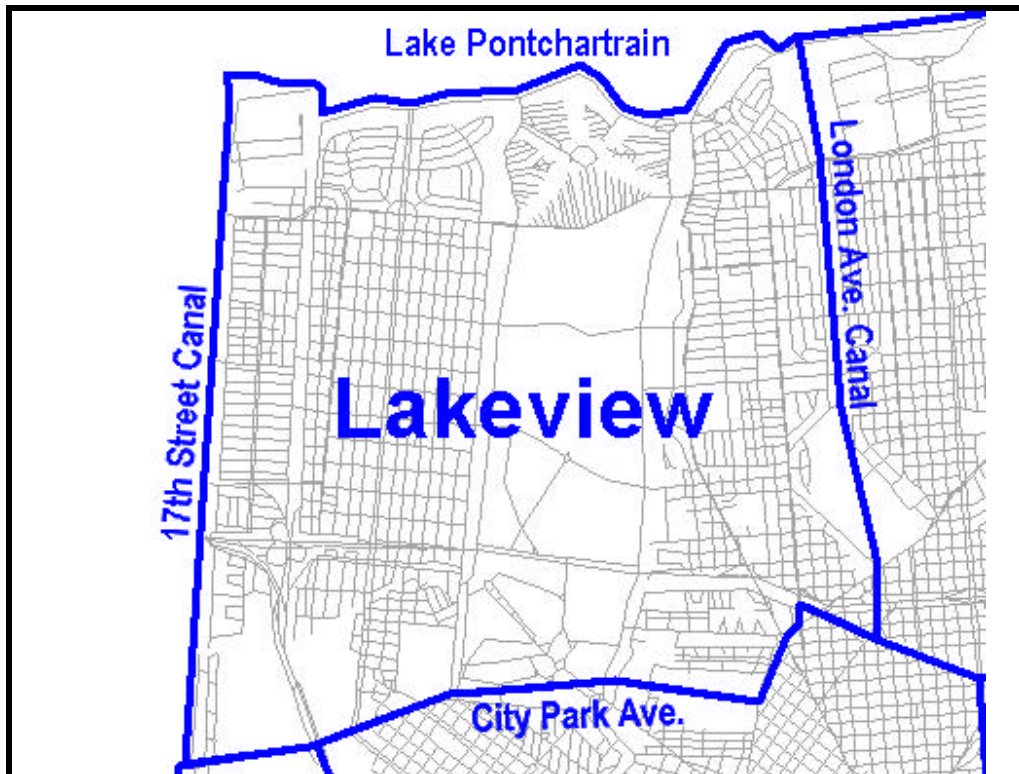

**Current Capital Cost** \$1,764,186

Description	Projected Start	Baseline Start	Projected Finish	Baseline Finish	%	Budgeted Cost	1996 1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019 2020																							
<b>3903 East Lakeview Rehab. Phase 2 Pipe Repair #1</b>																														
Pre-Design	28FEB99 A	28FEB99	05APR99 A	05APR99	100	0	<ul style="list-style-type: none"> <li>■ Pre-Design</li> </ul>																							
Preliminary Design	06APR99 A	06APR99	07JUN99 A	07JUN99	100	30,624	<ul style="list-style-type: none"> <li>■ Preliminary Design</li> </ul>																							
Final Design	07JUN99 A	07JUN99	08DEC99 A	08DEC99	100	57,627	<ul style="list-style-type: none"> <li>■ Final Design</li> </ul>																							
Advertisement	15DEC99 A	15DEC99	14JAN00 A	14JAN00	100	2,841	<ul style="list-style-type: none"> <li>■ Advertisement</li> </ul>																							
Award	19JAN00 A	19JAN00	19APR00 A	19APR00	100	2,200	<ul style="list-style-type: none"> <li>■ Award</li> </ul>																							
Construction	20APR00 A	20APR00	23MAR01 A	23MAR01	100	1,437,161	<ul style="list-style-type: none"> <li>■ Construction</li> </ul>																							
Field Testing	20APR00 A	20APR00	23MAR01 A	23MAR01	100	31,216	<ul style="list-style-type: none"> <li>■ Field Testing</li> </ul>																							
ESDC	20APR00 A	20APR00	23MAR01 A	23MAR01	100	7,217	<ul style="list-style-type: none"> <li>■ ESDC</li> </ul>																							
Inspection Services	20APR00 A	20APR00	23MAR01 A	23MAR01	100	175,300	<ul style="list-style-type: none"> <li>■ Inspection Services</li> </ul>																							
S&WB Resolution	05APR01 A	05APR01	05APR01 A	05APR01	100	0	<ul style="list-style-type: none"> <li>■ S&amp;WB Resolution</li> </ul>																							
Certification	26OCT01 A	26OCT01	05APR02 A	05APR02	100	20,000	<ul style="list-style-type: none"> <li>■ Certification</li> </ul>																							

Data date 01SEP03

© Primavera Systems, Inc.

**Sewerage and Water Board of New Orleans  
Sewer System Evaluation and Rehabilitation Program  
Master Schedule**

- Early bar
- Target bar
- Progress bar
