

## *Sewer System Evaluation and Rehabilitation Program*

### Rehabilitation Project

---

<b>Contract Number</b>	3924
<b>Name</b>	East Lakeview Area Sewer Rehabilitation Phase 2 Pipe Lining and Repairs
<b>Basin</b>	Lakeview
<b>Council Districts</b>	A, D
<b>Status:</b>	The Sewerage and Water Board accepted as complete all work performed under this contract at the Board meeting on October 10, 2001. Certification of this project, as required by USEPA Assistance Grant No. XP-996732-01-2, was completed October 10, 2002.

#### Resources

**SSERP Project Engineer** MWH

**Design Engineer** Evans Graves Engineers, Inc.

**Contractor** Insituform Technologies, Inc.

#### Comments

Attended the Lakeview Civic Improvement Association meeting of March 14, 2001. Attended the Lakeview Civic Improvement Association meeting of May 9, 2001. Attended the Lakeview Civic Improvement Association meeting of July 11, 2001. Attended the Lakeview Civic Improvement Association meeting of November 14, 2001.


## 3924 - East Lakeview Area Sewer Rehabilitation Phase 2 Pipe Lining and Repairs

---

### Description

Rehabilitation by cured-in-place lining of approximately 26,720 lineal feet of existing sanitary sewer 8"-18" diameter; 1,080 lineal feet of existing sewer service lateral replacements; 33 internal point repairs; 166 service connection repairs by short length service lateral lining or excavation; and restoration.

### Project Location

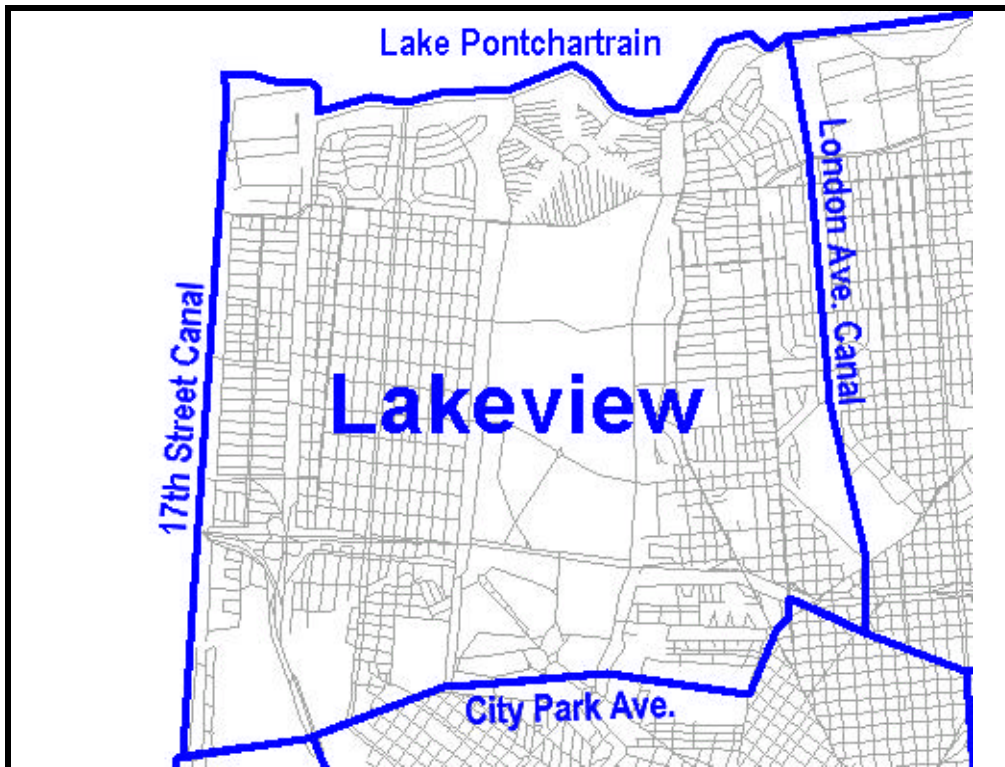

**Current Capital Cost**    \$1,661,989

Description	Projected Start	Baseline Start	Projected Finish	Baseline Finish	%	Budgeted Cost																												
							1997	1998	1999	2000	2001	2002	2003	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	2023	2024
<b>3924 East Lakeview Phase 2 Pipe Lining &amp; Repairs</b>																																		
Pre-Design	28FEB99 A	28FEB99	05APR99 A	05APR99	100	0	Pre-Design																											
Preliminary Design	06APR99 A	06APR99	07JUN99 A	07JUN99	100	30,624	Preliminary Design																											
Final Design	07JUN99 A	07JUN99	08DEC99 A	08DEC99	100	34,708	Final Design																											
Advertisement	15DEC99 A	15DEC99	10MAR00 A	10MAR00	100	3,669	Advertisement																											
Award	15MAR00 A	15MAR00	12APR00 A	12APR00	100	2,200	Award																											
Construction	24JUL00 A	24JUL00	15JUN01 A	15JUN01	100	1,356,339	Construction																											
Field Testing	24JUL00 A	24JUL00	15JUN01 A	15JUN01	100	30,545	Field Testing																											
ESDC	24JUL00 A	24JUL00	15JUN01 A	15JUN01	100	8,604	ESDC																											
Inspection Services	24JUL00 A	24JUL00	15JUN01 A	15JUN01	100	175,300	Inspection Services																											
S&WB Resolution	10OCT01 A	10OCT01	10OCT01 A	10OCT01	100	0	S&WB Resolution																											
Certification	13JUL02 A	13JUL02	10OCT02 A	10OCT02	100	20,000	Certification																											

Data date	01SEP04
© Primavera Systems, Inc.	

**Sewerage and Water Board of New Orleans**  
**Sewer System Evaluation and Rehabilitation Program**  
**Master Schedule**
