

Sewer System Evaluation and Rehabilitation Program

Rehabilitation Project

Contract Number	3954
Name	Mid-City Area Sewer Rehabilitation Sewer Main Replacement No. 1
Basin	Mid-City
Council Districts	A, B, C, D
Status:	This project is currently in the Construction phase.

Resources

SSERP Project Engineer MWH

Design Engineer Weston Solutions, Inc.

Contractor Boh Bros. Construction Co., LLC


Comments

3954 - Mid-City Area Sewer Rehabilitation Sewer Main Replacement No. 1

Description

The proposed work generally consists of sewer mainline replacements, associated service connections and laterals. The project is located in the Mid-City basin of Orleans Parish and is bounded by City Park Avenue, Canal Street, Carrollton Avenue, and Interstate 10.

Project Location

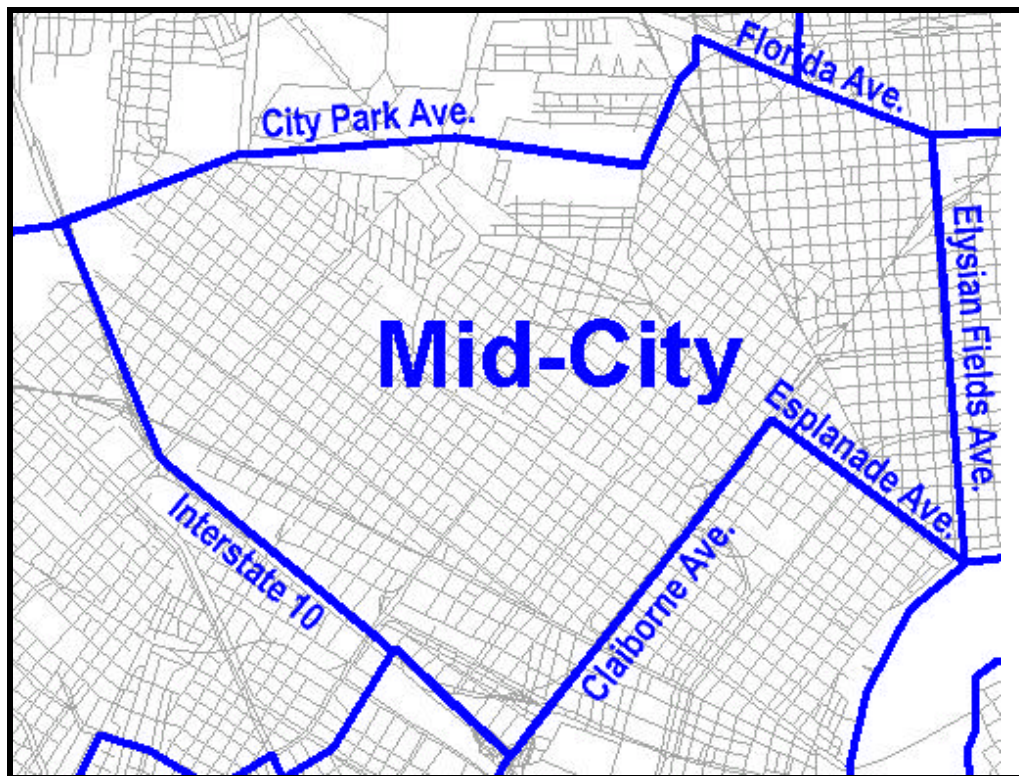

Current Capital Cost \$902,681

Description	Projected Start	Target Start	Projected Finish	Target Finish	%	Budgeted Cost	1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019																							
							Gantt Chart Timeline																							
3954 Mid-City Sewer Main Replacement No. 1																														
Pre-Design	21MAR02 A	21MAR02	21FEB03 A	21FEB03	100	0																								
Preliminary Design	10MAR03 A	10MAR03	27OCT03 A	27OCT03	100	21,967																								
Pre-Advertisement	24SEP03 A	24SEP03	03DEC03 A	03DEC03	100	0																								
Final Design	26SEP03 A	26SEP03	17NOV03 A	17NOV03	100	33,166																								
Advertisement	10DEC03 A	10DEC03	23JAN04 A	23JAN04	100	3,147																								
Award	23JAN04 A	23JAN04	01JUN04 A	01JUN04	100	1,049																								
Construction	01JUN04 A	01JUN04	11MAR05	28SEP04	92	727,676																								
Field Testing	01JUN04 A	01JUN04	10APR05	28OCT04	92	10,915																								
ESDC	01JUN04 A	01JUN04	10APR05	28OCT04	92	4,717																								
Inspection Services	01JUN04 A	01JUN04	10APR05	28OCT04	92	80,044																								
Construction Final	12MAR05	29SEP04	10APR05	28OCT04	0	0																								
S&WB Acceptance	02AUG05	27JAN05	02AUG05	27JAN05	0	0																								
Certification	04MAY06	30OCT05	01AUG06	27JAN06	0	20,000																								

Data date 01FEB05

© Primavera Systems, Inc.

**Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule**

- Early bar
- Target bar
- Progress bar
