

*Sewer System Evaluation and Rehabilitation Program*

**Rehabilitation Project**

---

**Contract Number**            3959

**Name**                            Mid-City Area Sewer Rehabilitation No. 3

**Basin**                            Mid-City

**Council Districts**            A, B, C, D

**Status:**                        This project is in the Construction phase.

**Resources**

**SSERP Project Engineer** MWH

**Design Engineer**            Weston Solutions, Inc.

**Contractor**                    D & O Construction


**Comments**

---

**Description**

This project includes the rehabilitation of existing main line sanitary sewers and sanitary sewer service connections. The project is located in the area bounded by Canal Street, Carrollton Avenue, Conti Street, and North Claiborne Avenue.

**Project Location**

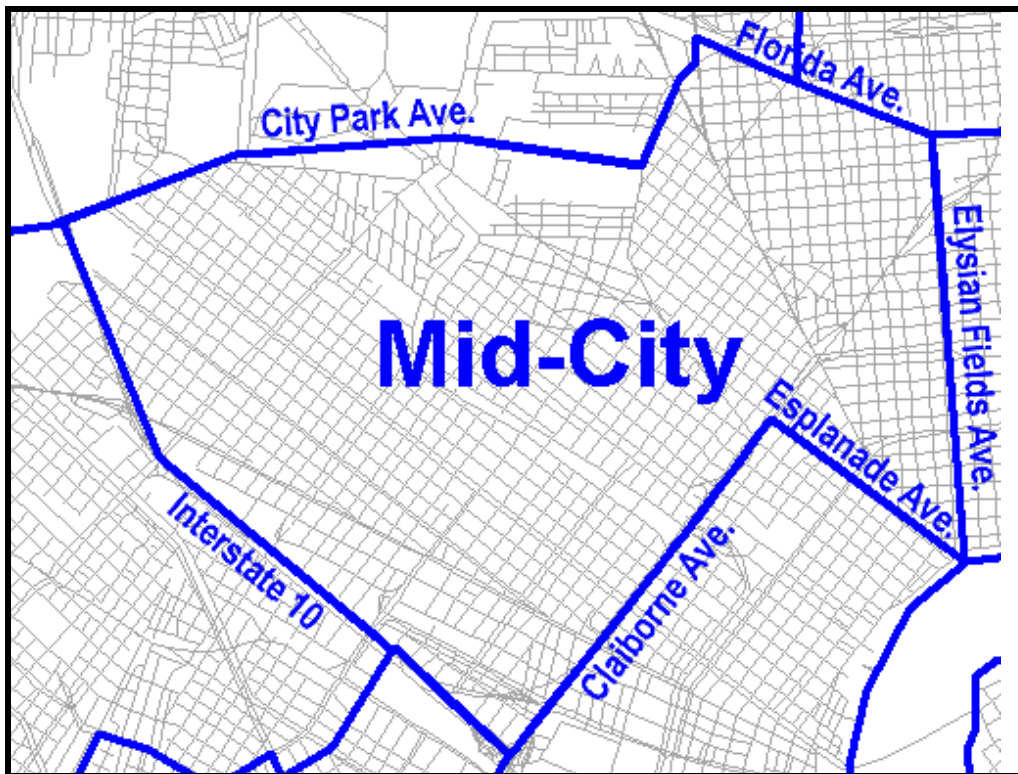

**Current Capital Cost** \$2,712,478

Description	Projected Start	Target Start	Projected Finish	Target Finish	%	Budgeted Cost	1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019																							
							Gantt Chart Timeline																							
<b>3959 Mid-City Sewer Rehabilitation No. 3</b>																														
Pre-Design	21MAR02 A	21MAR02	21FEB03 A	21FEB03	100	0	[Gantt bar: Pre-Design, 21MAR02 to 21FEB03, 100% complete]																							
Preliminary Design	10MAR03 A	10MAR03	27OCT03 A	27OCT03	100	21,967	[Gantt bar: Preliminary Design, 10MAR03 to 27OCT03, 100% complete]																							
Final Design	22JAN04 A	22JAN04	21JUN04 A	21JUN04	100	33,166	[Gantt bar: Final Design, 22JAN04 to 21JUN04, 100% complete]																							
Pre-Advertisement	11FEB04 A	11FEB04	30JUN04 A	30JUN04	100	0	[Gantt bar: Pre-Advertisement, 11FEB04 to 30JUN04, 100% complete]																							
Advertisement	07JUL04 A	07JUL04	20AUG04 A	05AUG04	100	3,147	[Gantt bar: Advertisement, 07JUL04 to 20AUG04, 100% complete]																							
Award	20AUG04 A	06AUG04	15NOV04 A	21JAN05	100	1,049	[Gantt bar: Award, 20AUG04 to 15NOV04, 100% complete]																							
Construction	15NOV04 A	22JAN05	12JUN05	19AUG05	66	2,336,384	[Gantt bar: Construction, 15NOV04 to 12JUN05, 66% complete]																							
Field Testing	15NOV04 A	22JAN05	12JUL05	18SEP05	66	35,046	[Gantt bar: Field Testing, 15NOV04 to 12JUL05, 66% complete]																							
ESDC	15NOV04 A	22JAN05	12JUL05	18SEP05	66	4,717	[Gantt bar: ESDC, 15NOV04 to 12JUL05, 66% complete]																							
Inspection Services	15NOV04 A	22JAN05	12JUL05	18SEP05	66	257,002	[Gantt bar: Inspection Services, 15NOV04 to 12JUL05, 66% complete]																							
Construction Final	13JUN05	20AUG05	12JUL05	18SEP05	0	0	[Gantt bar: Construction Final, 13JUN05 to 20AUG05, 0% complete]																							
S&WB Acceptance	19OCT05	18DEC05	19OCT05	18DEC05	0	0	[Gantt bar: S&WB Acceptance, 19OCT05 to 18DEC05, 0% complete]																							
Certification	21JUL06	20SEP06	18OCT06	18DEC06	0	20,000	[Gantt bar: Certification, 21JUL06 to 18OCT06, 0% complete]																							

Data date 01FEB05

**Sewerage and Water Board of New Orleans  
Sewer System Evaluation and Rehabilitation Program  
Master Schedule**

- Early bar
- Target bar
- Progress bar
