

Sewer System Evaluation and Rehabilitation Program

Rehabilitation Project

Contract Number 3967

Name Mid-City Sewer Rehabilitation No. 9

Basin Mid-City

Council Districts A, B, C, D

Status: This project is currently in the Advertisement phase.

Resources

SSERP Project Engineer MWH

Design Engineer Weston Solutions, Inc.

Contractor


Comments

Description

The proposed work generally consists of sewer main replacements, associated service connections and laterals, manhole rehabilitation, CIPP lining and point repairs; including temporary and final restoration, sewer flow control, traffic maintenance and control, labor, equipment, tools and materials as necessary to perform the work as specified in the Contract Documents.

The project is generally located in the Mid-City Area of Orleans Parish. The project work area is bounded by Esplanade Avenue, N. Dorgenois Street, St. Bernard Avenue, Paul Morphy Street, LaHarp Street and Gentilly Boulevard.

Project Location

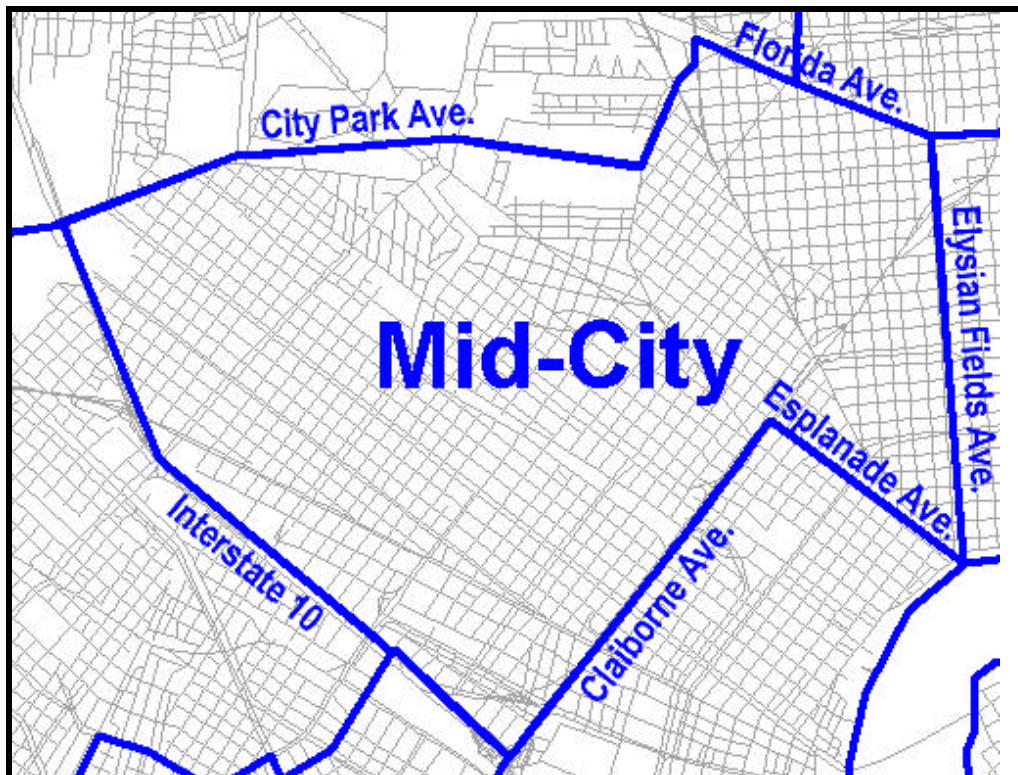

Current Capital Cost \$2,604,049

Description	Projected Start	Target Start	Projected Finish	Target Finish	%	Budgeted Cost	1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019																							
							Gantt Chart Timeline																							
3967 Mid-City Sewer Rehabilitation No. 9																														
Pre-Design	21MAR02 A	21MAR02	21FEB03 A	21FEB03	100	0																								
Preliminary Design	10MAR03 A	10MAR03	27OCT03 A	27OCT03	100	21,968																								
Final Design	18SEP04 A	17SEP04	21DEC04 A	15DEC04	100	33,167																								
Pre-Advertisement	29SEP04 A	20OCT04	06JAN05 A	11JAN05	100	0																								
Advertisement	12JAN05 A	12JAN05	18FEB05	10FEB05	71	3,147																								
Award	18FEB05	11FEB05	16AUG05	01AUG05	0	1,050																								
Construction	16AUG05	02AUG05	11FEB06	29MAR06	0	2,240,000																								
Field Testing	16AUG05	02AUG05	13MAR06	28APR06	0	33,600																								
ESDC	16AUG05	02AUG05	13MAR06	28APR06	0	4,717																								
Inspection Services	16AUG05	02AUG05	13MAR06	28APR06	0	246,400																								
Construction Final	12FEB06	30MAR06	13MAR06	28APR06	0	0																								
S&WB Acceptance	21JUN06	28JUL06	21JUN06	28JUL06	0	0																								
Certification	23MAR07	30APR07	20JUN07	28JUL07	0	20,000																								

Data date 01FEB05

Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule

- Early bar
- Target bar
- Progress bar
