

Sewer System Evaluation and Rehabilitation Program

Rehabilitation Project

Contract Number 3972

Name Mid-City Sewer Rehabilitation No. 14

Basin Mid-City

Council Districts A, B, C, D

Status: This project is currently in the Final Design / Pre-Advertisement phase.

Resources

SSERP Project Engineer MWH

Design Engineer Weston Solutions, Inc.


Contractor

Comments

Description

Rehabilitation of sewer lines as recommended by the RMAP.

Project Location

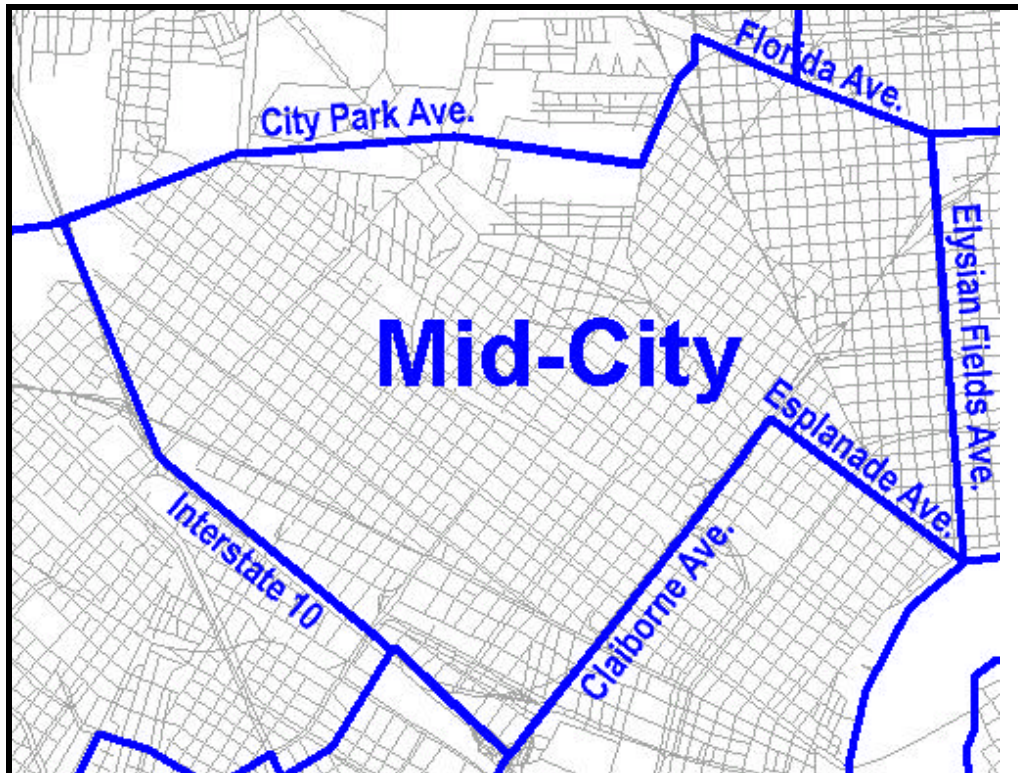

Current Capital Cost \$2,100,051

Description	Projected Start	Target Start	Projected Finish	Target Finish	%	Budgeted Cost	1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019											
							Gantt chart area with a vertical red line at 2005.											
3972 Mid-City Sewer Rehabilitation No. 14																		
Pre-Design	21MAR02 A	21MAR02	21FEB03 A	21FEB03	100	0	Pre-Design											
Preliminary Design	10MAR03 A	10MAR03	27OCT03 A	27OCT03	100	21,968	Preliminary Design											
Final Design	17DEC04 A	17DEC04	25FEB05	16MAR05	45	33,167	Final Design											
Pre-Advertisement	21DEC04 A	19JAN05	06APR05	12APR05	40	0	Pre-Advertisement											
Advertisement	13APR05	13APR05	20MAY05	12MAY05	0	3,148	Advertisement											
Award	20MAY05	13MAY05	07NOV05	31OCT05	0	1,050	Award											
Construction	07NOV05	01NOV05	04JUN06	29MAY06	0	1,792,000	Construction											
Field Testing	07NOV05	01NOV05	04JUL06	28JUN06	0	26,880	Field Testing											
ESDC	07NOV05	01NOV05	04JUL06	28JUN06	0	4,718	ESDC											
Inspection Services	07NOV05	01NOV05	04JUL06	28JUN06	0	197,120	Inspection Services											
Construction Final	05JUN06	30MAY06	04JUL06	28JUN06	0	0	Construction Final Completion											
S&WB Acceptance	18OCT06	27SEP06	18OCT06	27SEP06	0	0	IS&WB Acceptance											
Certification	20JUL07	30JUN07	17OCT07	27SEP07	0	20,000	Certification											

Data date 01FEB05

© Primavera Systems, Inc.

**Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule**

- Early bar
- Target bar
- Progress bar
