

Sewer System Evaluation and Rehabilitation Program

Rehabilitation Project

Contract Number 3956

Name Mid-City Area Sewer Rehabilitation Excavated Point Repair No. 2

Basin Mid-City

Council Districts A, B, C, D

Status: This project is in the Construction phase.

Resources

SSERP Project Engineer MWH

Design Engineer Weston Solutions, Inc.

Contractor Wallace C. Drennan


Comments

3956 - Mid-City Area Sewer Rehabilitation Excavated Point Repair No. 2

Description

The proposed work generally consists of mainline point repairs, and lateral replacements. The project is generally located in the Mid-City basin of Orleans Parish, bounded by City Park Ave., Lelong Ave., Carrollton Ave., and St. Peter St.

Project Location

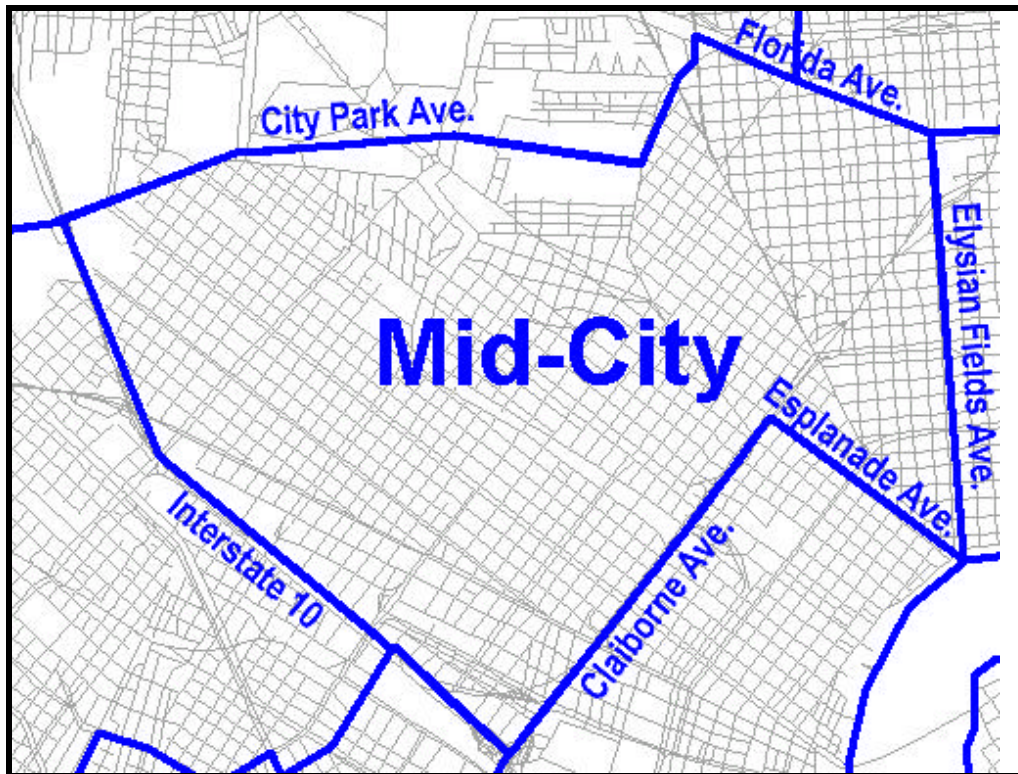

Current Capital Cost \$394,741

Description	Projected Start	Target Start	Projected Finish	Target Finish	%	Budgeted Cost	1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019																							
							Gantt Chart Timeline																							
3956 Mid-City Excavated Point Repair No. 2																														
Pre-Design	21MAR02 A	21MAR02	21FEB03 A	21FEB03	100	0																								
Preliminary Design	10MAR03 A	10MAR03	27OCT03 A	27OCT03	100	21,967																								
Final Design	13NOV03 A	13NOV03	30JAN04 A	30JAN04	100	33,166																								
Pre-Advertisement	14NOV03 A	14NOV03	04FEB04 A	04FEB04	100	0																								
Advertisement	11FEB04 A	11FEB04	12MAR04 A	12MAR04	100	3,147																								
Award	12MAR04 A	12MAR04	19JUL04 A	18JUL04	100	1,049																								
Construction	19JUL04 A	19JUL04	22FEB05	15DEC04	71	276,173																								
Field Testing	19JUL04 A	19JUL04	24MAR05	14JAN05	71	4,143																								
ESDC	19JUL04 A	19JUL04	24MAR05	14JAN05	71	4,717																								
Inspection Services	19JUL04 A	19JUL04	24MAR05	14JAN05	71	30,379																								
Construction Final	23FEB05	16DEC04	24MAR05	14JAN05	0	0																								
S&WB Acceptance	20JUL05	15APR05	20JUL05	15APR05	0	0																								
Certification	21APR06	16JAN06	19JUL06	15APR06	0	20,000																								

Data date 01FEB05

Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule

- Early bar
- Target bar
- Progress bar
