

Sewer System Evaluation and Rehabilitation Program

Rehabilitation Project

Contract Number 3965

Name Mid-City Sewer Rehabilitation No. 8

Basin Mid-City

Council Districts A, B, C, D

Status: This project is currently in the Award phase.

Resources

SSERP Project Engineer MWH

Design Engineer Weston Solutions, Inc.

Contractor


Comments

Description

The proposed work generally consists of manholes, mainline pipe replacement, CIPP lining, partial lining, mainline point repairs, and lateral replacements; including temporary and final restoration, sewer flow control, traffic maintenance and control, labor, equipment, tools and materials as necessary to perform the work as specified in the Contract Documents.

The project is generally located in the Mid-City Area of Orleans Parish. The project work area is bounded by St. Bernard Avenue, N. Broad Street, Florida Avenue, New Orleans Street, Duels Street, Allen Street and Pontchartrain Expressway.

Project Location

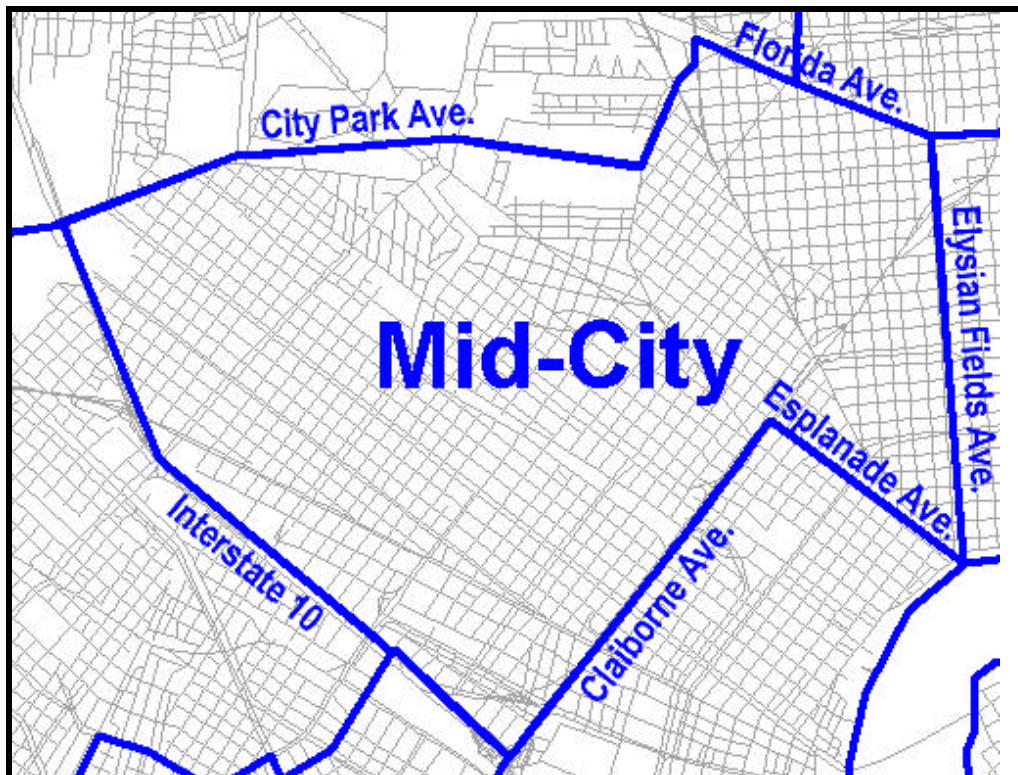

Current Capital Cost \$1,774,921

Description	Projected Start	Target Start	Projected Finish	Target Finish	%	Budgeted Cost	1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019																							
							Gantt Chart Timeline																							
3965 Mid-City Sewer Rehabilitation No. 8																														
Pre-Design	21MAR02 A	21MAR02	21FEB03 A	21FEB03	100	0																								
Preliminary Design	10MAR03 A	10MAR03	27OCT03 A	27OCT03	100	21,967																								
Final Design	13AUG04 A	13AUG04	01NOV04 A	10NOV04	100	33,166																								
Pre-Advertisement	31AUG04 A	15SEP04	24NOV04 A	07DEC04	100	0																								
Advertisement	01DEC04 A	08DEC04	14JAN05 A	06JAN05	100	3,147																								
Award	14JAN05 A	07JAN05	18JUL05	24JUN05	7	1,049																								
Construction	18JUL05	25JUN05	14DEC05	21DEC05	0	1,503,000																								
Field Testing	18JUL05	25JUN05	13JAN06	20JAN06	0	22,545																								
ESDC	18JUL05	25JUN05	13JAN06	20JAN06	0	4,717																								
Inspection Services	18JUL05	25JUN05	13JAN06	20JAN06	0	165,330																								
Construction Final	15DEC05	22DEC05	13JAN06	20JAN06	0	0																								
S&WB Acceptance	21APR06	21APR06	21APR06	21APR06	0	0																								
Certification	21JAN07	22JAN07	20APR07	21APR07	0	20,000																								

Data date 01FEB05

Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule

- Early bar
- Target bar
- Progress bar
