

Sewer System Evaluation and Rehabilitation Program

Rehabilitation Project

Contract Number 3961

Name Mid-City Area Sewer Rehabilitation No. 5

Basin Mid-City

Council Districts A, B, C, D

Status: This project is in the Construction phase.

Resources

SSERP Project Engineer MWH

Design Engineer Weston Solutions, Inc.

Contractor D & O Construction


Comments

Description

The proposed work generally consists of manholes, mainline pipe replacement, CIPP lining, partial lining, mainline point repairs, and lateral replacements; including temporary and final restoration, sewer flow control, traffic maintenance and control, labor, equipment, tools and materials as necessary to perform the work as specified in the Contract Documents.

The project is generally located in the Mid-City Basin of Orleans Parish. The project work area is bounded by Broad Street, Canal Street, S. Claiborne Avenue and Pontchartrain Expressway.

Project Location

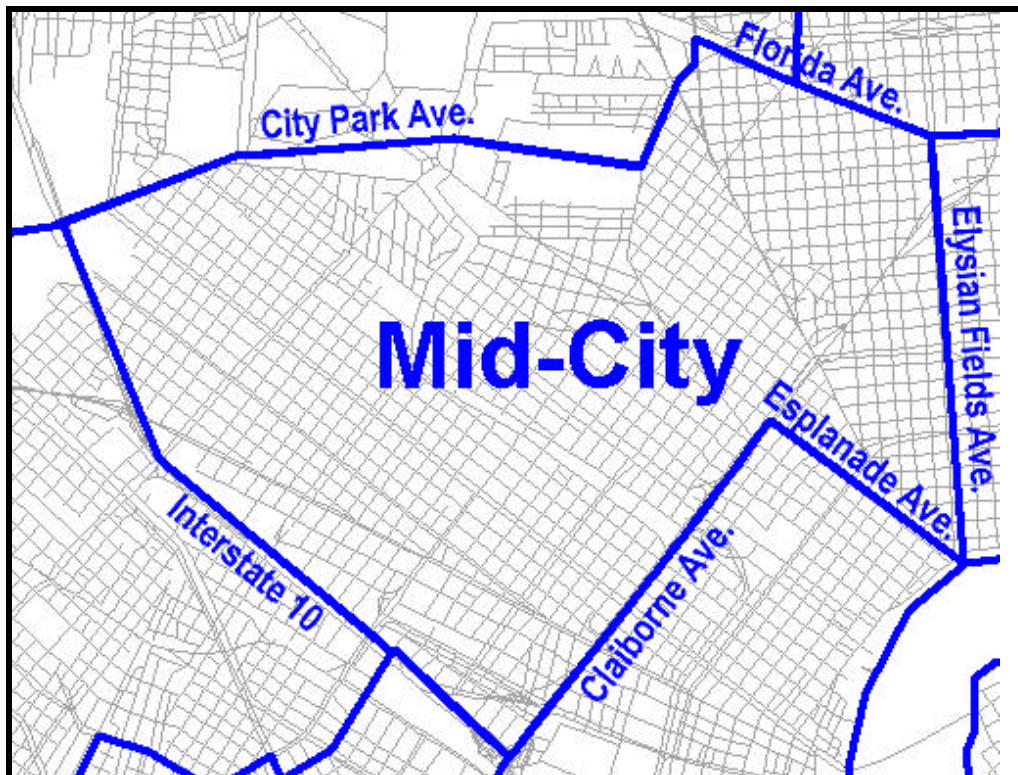

Current Capital Cost \$3,323,312

Description	Projected Start	Target Start	Projected Finish	Target Finish	%	Budgeted Cost	1996 1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019																							
							Gantt Chart Timeline																							
3961 Mid-City Sewer Rehabilitation No. 5																														
Pre-Design	21MAR02 A	21MAR02	21FEB03 A	21FEB03	100	0																								
Preliminary Design	10MAR03 A	10MAR03	27OCT03 A	27OCT03	100	21,967																								
Final Design	10APR04 A	10APR04	14JUL04 A	14JUL04	100	33,166																								
Pre-Advertisement	28APR04 A	28APR04	06AUG04 A	10AUG04	100	0																								
Advertisement	11AUG04 A	11AUG04	24SEP04 A	09SEP04	100	3,147																								
Award	24SEP04 A	10SEP04	24JAN05 A	25FEB05	100	1,049																								
Construction	24JAN05 A	26FEB05	19NOV05	21JAN06	2	2,879,348																								
Field Testing	24JAN05 A	26FEB05	19DEC05	20FEB06	2	43,190																								
ESDC	24JAN05 A	26FEB05	19DEC05	20FEB06	2	4,717																								
Inspection Services	24JAN05 A	26FEB05	19DEC05	20FEB06	2	316,728																								
Construction Final	20NOV05	22JAN06	19DEC05	20FEB06	0	0																								
S&WB Acceptance	23MAR06	22MAY06	23MAR06	22MAY06	0	0																								
Certification	23DEC06	22FEB07	22MAR07	22MAY07	0	20,000																								

Data date 01FEB05

Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule

- Early bar
- Target bar
- Progress bar
