

Sewer System Evaluation and Rehabilitation Program

Rehabilitation Project

Contract Number 3975

Name Lower Ninth Ward Point Repairs No. 2

Basin Lower Ninth Ward

Council Districts C, D, E

Status: This project is in the Final Design/Pre-Advertisement phase.

Resources

SSERP Project Engineer MWH

Design Engineer CH2MHill


Contractor

Comments

Description

Rehabilitation of sewer lines as recommended by the RMAP.

Project Location

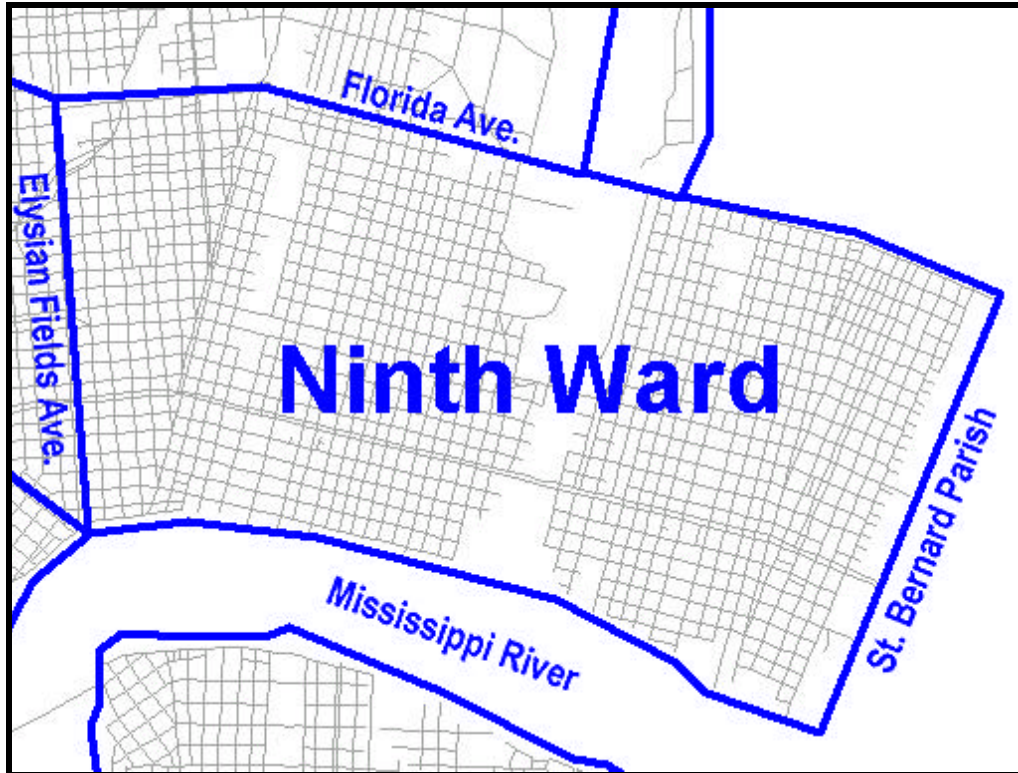

Current Capital Cost \$669,296

Description	Projected Start	Target Start	Projected Finish	Target Finish	%	Budgeted Cost	1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018											
							Gantt Chart Timeline											
3975 Ninth Ward Point Repairs No. 2																		
Pre-Design	18JUN03 A	18JUN03	06OCT03 A	06OCT03	100	0	Pre-Design											
Preliminary Design	13JAN04 A	13JAN04	19JAN05 A	12OCT04	100	25,007	Preliminary Design											
Pre-Advertisement	27DEC04 A	16FEB05	04MAY05	11MAY05	48	0	Pre-Advertisement											
Final Design	20JAN05 A	11NOV04	25MAR05	11FEB05	40	33,292	Final Design											
Advertisement	11MAY05	11MAY05	17JUN05	10JUN05	0	2,322	Advertisement											
Award	17JUN05	10JUN05	08NOV05	29NOV05	0	774	Award											
Construction	08NOV05	29NOV05	03OCT06	25OCT06	0	576,384	Construction											
Field Testing	08NOV05	29NOV05	02NOV06	24NOV06	0	8,646	Field Testing											
ESDC	08NOV05	29NOV05	02NOV06	24NOV06	0	4,079	ESDC											
Inspection Services	08NOV05	29NOV05	02NOV06	24NOV06	0	63,402	Inspection Services											
Construction Final	04OCT06	25OCT06	02NOV06	24NOV06	0	0	Construction Final Completion											
S&WB Acceptance	21FEB07	22FEB07	21FEB07	23FEB07	0	0	S&WB Acceptance											
Certification	24NOV07	25NOV07	21FEB08	23FEB08	0	20,000	Certification											

Data date 01MAR05

**Sewerage & Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule**

- Early bar
- Target bar
- Progress bar
