

*Sewer System Evaluation and Rehabilitation Program*

**Rehabilitation Project**

---

**Contract Number**            3988

**Name**                            Lower Ninth Ward Sewer Rehabilitation No. 7.

**Basin**                            Lower Ninth Ward

**Council Districts**            C, D, E

**Status:**

**Resources**

**SSERP Project Engineer** MWH

**Design Engineer**            CH2MHILL


**Contractor**

**Comments**

**Description**

Rehabilitation of sewer lines as recommended by the RMAP.

**Project Location**

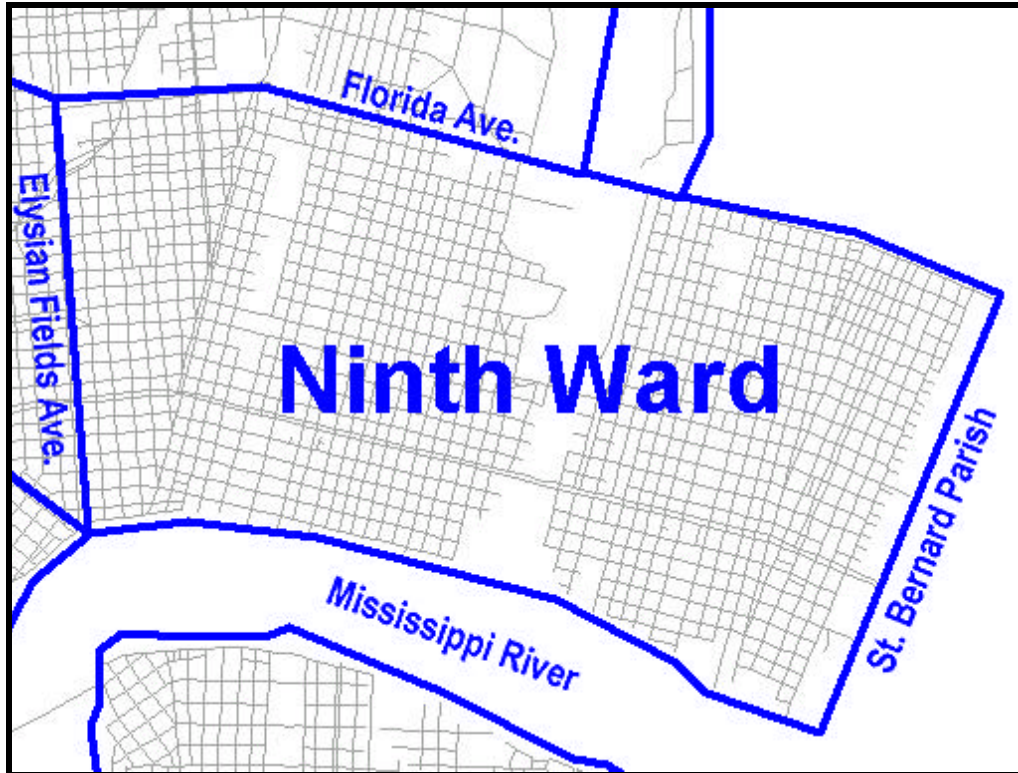

**Current Capital Cost**    \$3,830,041

| Description                                       | Projected Start | Target Start | Projected Finish | Target Finish | %   | Budgeted Cost | 1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019 |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|---|-----------------|--------------|------------------|---------------|-----|---------------|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|
|   |                 |              |                  |               |     |               | Gantt chart area with a vertical red line at 2005.   |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| <b>3988 Ninth Ward Sewer Rehabilitation No. 7</b> |                 |              |                  |               |     |               |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| Pre-Design  | 18JUN03 A       |              | 06OCT03 A        |               | 100 | 0             | ■ Pre-Design   |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| Preliminary Design                                | 13JAN04 A       |              | 19JAN05 A        |               | 100 | 25,007        | ■ Preliminary Design   |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| Final Design                                      | 15JUL05         |              | 12SEP05          |               | 0   | 33,292        | ■ Final Design   |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| Pre-Advertisement                                 | 27JUL05         |              | 02NOV05          |               | 0   | 0             | ■ Pre-Advertisement  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| Advertisement                                     | 09NOV05         |              | 16DEC05          |               | 0   | 2,322         | ■ Advertisement  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| Award   | 16DEC05         |              | 04MAY06          |               | 0   | 774           | ■ Award  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| Construction                                      | 04MAY06         |              | 29MAR07          |               | 0   | 3,328,504     | ■ Construction   |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| Field Testing                                     | 04MAY06         |              | 28APR07          |               | 0   | 49,928        | ■ Field Testing  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| ESDC  | 04MAY06         |              | 28APR07          |               | 0   | 4,079         | ■ ESDC   |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| Inspection Services                               | 04MAY06         |              | 28APR07          |               | 0   | 366,135       | ■ Inspection Services  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| Construction Final                                | 30MAR07         |              | 28APR07          |               | 0   | 0             | ■ Construction Final Completion  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| S&WB Acceptance                                   | 15AUG07         |              | 15AUG07          |               | 0   | 0             | ■ S&WB Acceptance  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| Certification                                     | 17MAY08         |              | 14AUG08          |               | 0   | 20,000        | ■ Certification  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |

Data date 01FEB05

© Primavera Systems, Inc.

**Sewerage and Water Board of New Orleans  
Sewer System Evaluation and Rehabilitation Program  
Master Schedule**

- Early bar
- Target bar
- Progress bar
