

Sewer System Evaluation and Rehabilitation Program

Rehabilitation Project

Contract Number 3989

Name Lower Ninth Ward Sewer Rehabilitation No. 8.

Basin Lower Ninth Ward

Council Districts C, D, E

Status:

Resources

SSERP Project Engineer MWH

Design Engineer CH2MHILL


Contractor

Comments

Description

Rehabilitation of sewer lines as recommended by the RMAP.

Project Location

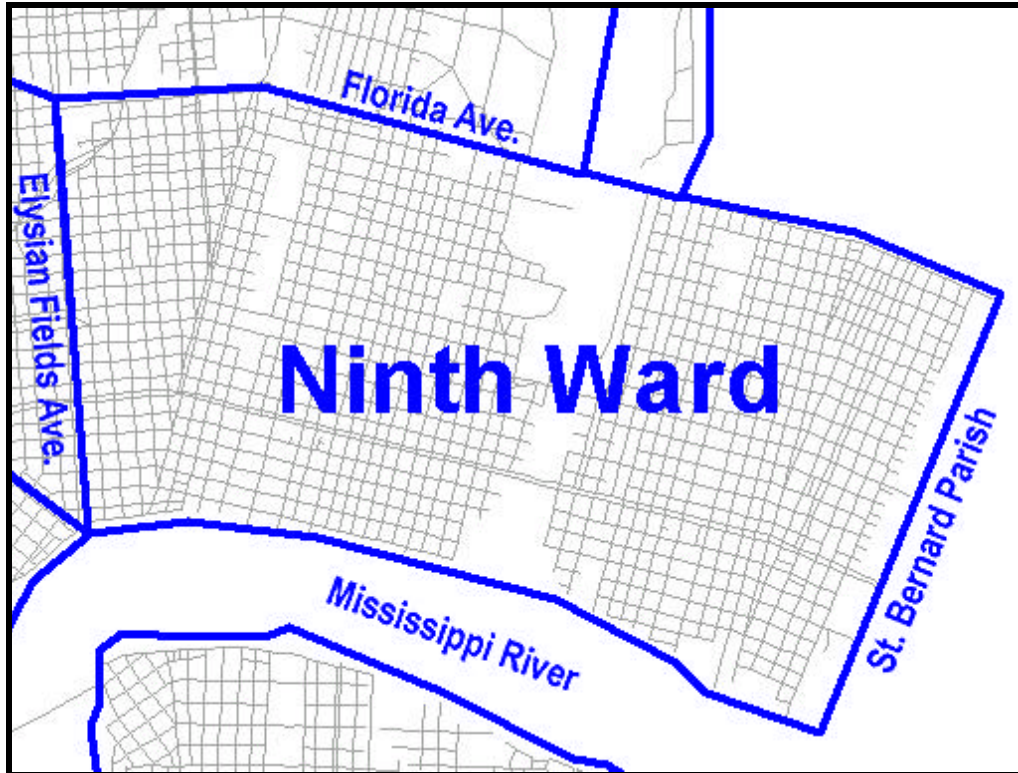

Current Capital Cost \$3,295,003

Description	Projected Start	Target Start	Projected Finish	Target Finish	%	Budgeted Cost	1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019																							
							Gantt chart area with a vertical red line at 2005.																							
3989 Ninth Ward Sewer Rehabilitation No. 8																														
Pre-Design	18JUN03 A		06OCT03 A		100	0	■ Pre-Design																							
Preliminary Design	13JAN04 A		19JAN05 A		100	25,007	■ Preliminary Design																							
Final Design	15JUL05		12SEP05		0	33,292	■ Final Design																							
Pre-Advertisement	31AUG05		07DEC05		0	0	■ Pre-Advertisement																							
Advertisement	14DEC05		20JAN06		0	2,322	■ Advertisement																							
Award	20JAN06		01JUN06		0	774	■ Award																							
Construction	01JUN06		26APR07		0	2,852,914	■ Construction																							
Field Testing	01JUN06		26MAY07		0	42,794	■ Field Testing																							
ESDC	01JUN06		26MAY07		0	4,079	■ ESDC																							
Inspection Services	01JUN06		26MAY07		0	313,821	■ Inspection Services																							
Construction Final	27APR07		26MAY07		0	0	■ Construction Final Completion																							
S&WB Acceptance	19SEP07		19SEP07		0	0	■ S&WB Acceptance																							
Certification	21JUN08		18SEP08		0	20,000	■ Certification																							

Data date 01FEB05

© Primavera Systems, Inc.

**Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule**

- Early bar
- Target bar
- Progress bar
