

Sewer System Evaluation and Rehabilitation Program

Rehabilitation Project

Contract Number 3986

Name Lower Ninth Ward Sewer Rehabilitation No. 5.

Basin Lower Ninth Ward

Council Districts C, D, E

Status:

Resources

SSERP Project Engineer MWH

Design Engineer CH2MHILL


Contractor

Comments

Description

Rehabilitation of sewer lines as recommended by the RMAP.

Project Location

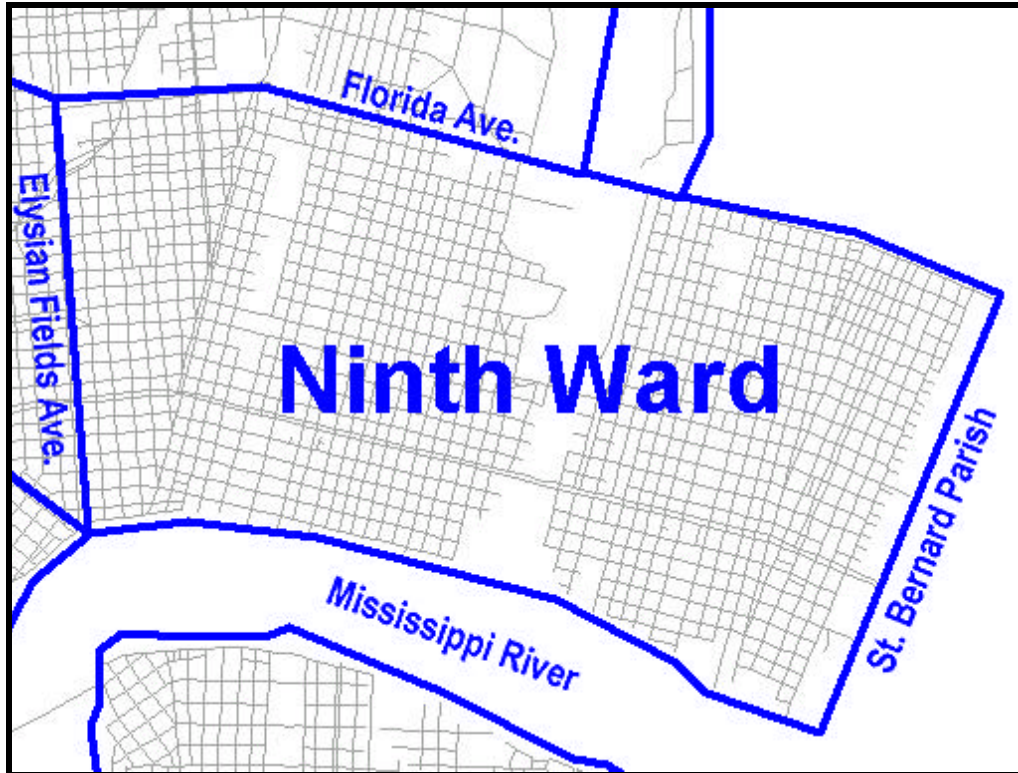

Current Capital Cost \$3,830,918

Description	Projected Start	Target Start	Projected Finish	Target Finish	%	Budgeted Cost	1996 1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019																							
							Gantt chart area with a vertical red line at 2005.																							
3986 Ninth Ward Sewer Rehabilitation No. 5																														
Pre-Design	18JUN03 A		06OCT03 A		100	0	■ Pre-Design																							
Preliminary Design	13JAN04 A		19JAN05 A		100	25,007	■ Preliminary Design																							
Final Design	16JUN05		12AUG05		0	33,292	■ Final Design																							
Pre-Advertisement	29JUN05		05OCT05		0	0	■ Pre-Advertisement																							
Advertisement	12OCT05		18NOV05		0	2,322	■ Advertisement																							
Award	18NOV05		06APR06		0	774	■ Award																							
Construction	06APR06		01MAR07		0	3,329,284	■ Construction																							
Field Testing	06APR06		31MAR07		0	49,939	■ Field Testing																							
ESDC	06APR06		31MAR07		0	4,079	■ ESDC																							
Inspection Services	06APR06		31MAR07		0	366,221	■ Inspection Services																							
Construction Final	02MAR07		31MAR07		0	0	■ Construction Final Completion																							
S&WB Acceptance	18JUL07		18JUL07		0	0	■ S&WB Acceptance																							
Certification	19APR08		17JUL08		0	20,000	■ Certification																							

Data date 01FEB05

© Primavera Systems, Inc.

**Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule**

- Early bar
- Target bar
- Progress bar
