

*Sewer System Evaluation and Rehabilitation Program*

**Rehabilitation Project**

---

**Contract Number**            3976

**Name**                            Lower Ninth Ward Point Repairs No. 3

**Basin**                            Lower Ninth Ward

**Council Districts**            C, D, E

**Status:**                        This project is in the Final Design / Pre-Advertisement phase.

**Resources**

**SSERP Project Engineer** MWH

**Design Engineer**            CH2MHill


**Contractor**

**Comments**

**Description**

Rehabilitation of sewer lines as recommended by the RMAP.

**Project Location**

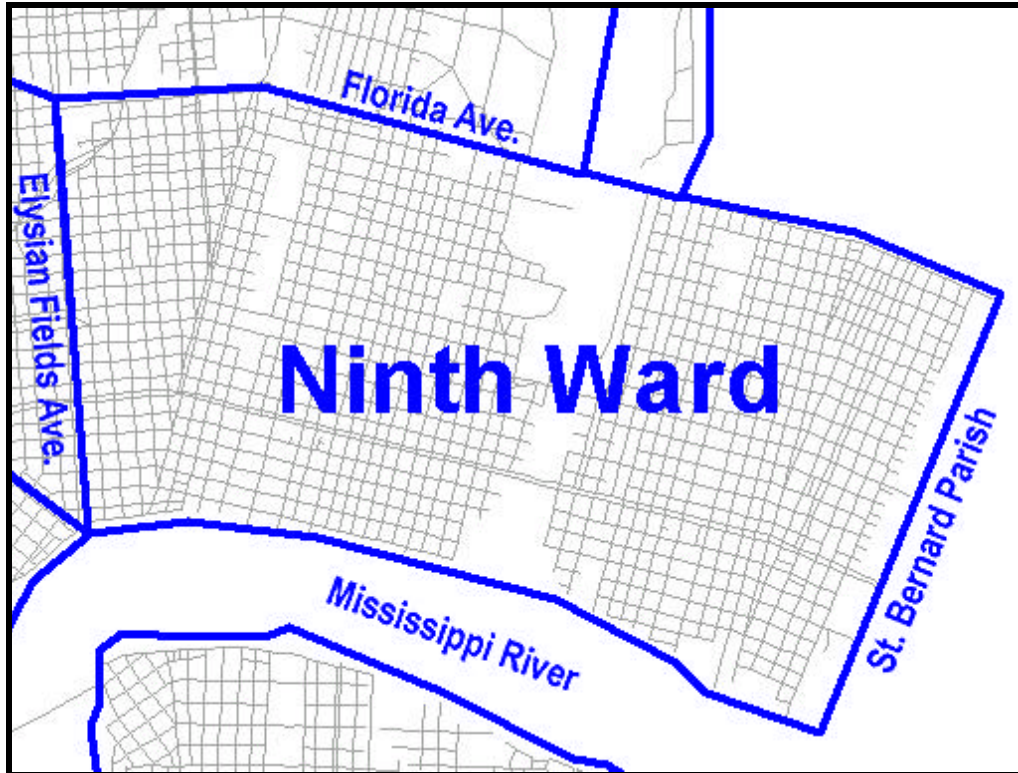

**Current Capital Cost**     \$774,421

Description	Projected Start	Target Start	Projected Finish	Target Finish	%	Budgeted Cost	1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018											
							Gantt Chart Timeline											
<b>3976 Ninth Ward Point Repairs No. 3</b>																		
Pre-Design	18JUN03 A	18JUN03	06OCT03 A	06OCT03	100	0												
Preliminary Design	13JAN04 A	13JAN04	19JAN05 A	12OCT04	100	25,007												
Final Design	20JAN05 A	13DEC04	25MAR05	15MAR05	40	33,292												
Pre-Advertisement	23FEB05 A	16MAR05	01JUN05	08JUN05	0	0												
Advertisement	08JUN05	08JUN05	15JUL05	11JUL05	0	2,322												
Award	15JUL05	11JUL05	06DEC05	27DEC05	0	774												
Construction	06DEC05	27DEC05	31OCT06	22NOV06	0	612,399												
Field Testing	06DEC05	27DEC05	30NOV06	22DEC06	0	9,185												
ESDC	06DEC05	27DEC05	30NOV06	22DEC06	0	4,079												
Inspection Services	06DEC05	27DEC05	30NOV06	22DEC06	0	67,363												
Construction Final	01NOV06	22NOV06	30NOV06	22DEC06	0	0												
S&WB Acceptance	21MAR07	22MAR07	21MAR07	23MAR07	0	0												
Certification	22DEC07	23DEC07	20MAR08	22MAR08	0	20,000												

Data date 01MAR05

**Sewerage & Water Board of New Orleans  
Sewer System Evaluation and Rehabilitation Program  
Master Schedule**

- Early bar
- Target bar
- Progress bar
