

Sewer System Evaluation and Rehabilitation Program

Rehabilitation Project

Contract Number	3945
Name	Uptown Area Sewer Excavated Point Repair No. 3
Basin	Uptown
Council Districts	A, B
Status:	Final Acceptance and Resolution (R-202-2004) was issued by the Board for this contract on November 17, 2004.

Resources

SSERP Project Engineer MWH

Design Engineer Evans Graves Engineers, Inc.

Contractor Roland Pugh Construction, Inc.


Comments

Attended the Magazine Street Merchants Association Board meeting on February 4, 2004. Met with President and Vice President of the Magazine Street Merchants Association on April 5, 2004. Met with residents of the 600 block of Patton Street on April 6, 2004. Attended the Board of Directors meeting of the Magazine Street Merchants Association on April 14, 2004. Attended the monthly meeting of the Magazine Street Merchants Association on April 21, 2004.

Description

Rehabilitation of sewer lines as recommended by the RMAP.

Project Location

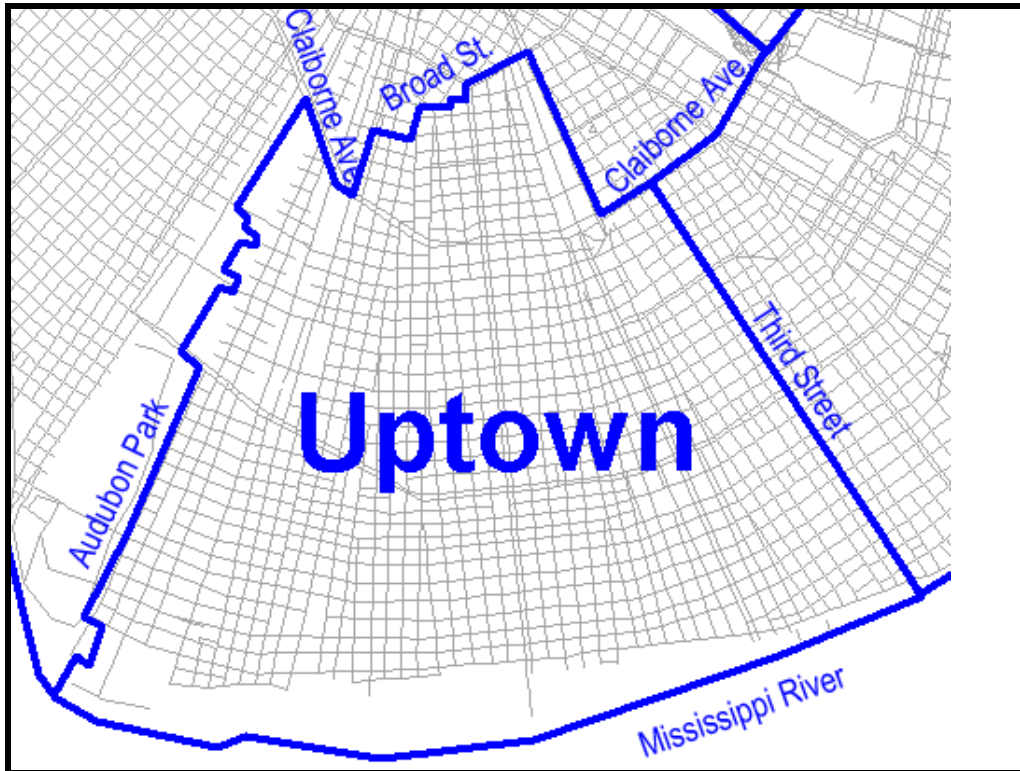

Current Capital Cost \$1,071,462

Description	Projected Start	Baseline Start	Projected Finsh	Baseline Finish	%	Budgeted Cost	1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019																							
							Gantt chart showing project progress from 1997 to 2019. A vertical red line indicates the current date (01DEC04). The chart uses color-coded bars: yellow for target bars, blue for progress bars, and green for early bars.																							
3945 Uptown Excavated Point Repair #3																														
Pre-Design	11MAY01 A	11MAY01	28DEC01 A	28DEC01	100	0	Pre-Design (Progress bar)																							
Preliminary Design	28DEC01 A	28DEC01	19FEB03 A	19FEB03	100	27,541	Preliminary Design (Progress bar)																							
Final Design	02DEC02 A	02DEC02	15APR03 A	15APR03	100	17,501	Final Design (Progress bar)																							
Pre-Advertisement	24FEB03 A	24FEB03	27JUN03 A	27JUN03	100	0	Pre-Advertisement (Progress bar)																							
Advertisement	11JUN03 A	11JUN03	11JUL03 A	11JUL03	100	2,917	Advertisement (Progress bar)																							
Award	11JUL03 A	11JUL03	03NOV03 A	03NOV03	100	2,201	Award (Progress bar)																							
Construction	03NOV03 A	03NOV03	16JUL04 A	16JUL04	100	887,473	Construction (Progress bar)																							
Field Testing	03NOV03 A	03NOV03	13AUG04 A	15AUG04	100	13,312	Field Testing (Progress bar)																							
ESDC	03NOV03 A	03NOV03	13AUG04 A	15AUG04	100	2,895	ESDC (Progress bar)																							
Inspection Services	03NOV03 A	03NOV03	13AUG04 A	15AUG04	100	97,622	Inspection Services (Progress bar)																							
Construction Final Completion	17JUL04 A	17JUL04	13AUG04 A	15AUG04	100	0	Construction Final Completion (Target bar)																							
S&WB Acceptance	17NOV04 A	14NOV04	17NOV04 A	14NOV04	100	0	S&WB Acceptance (Target bar)																							
Certification	19AUG05	17AUG05	16NOV05	14NOV05	0	20,000	Certification (Target bar)																							

Data date 01DEC04

© Primavera Systems, Inc.

**Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule**

- Early bar
- Target bar
- Progress bar
