

Sewer System Evaluation and Rehabilitation Program

Rehabilitation Project

Contract Number 3948

Name Uptown Area Sewer Main Replacement No. 3

Basin Uptown

Council Districts A, B

Status: This project is in the Construction phase.

Resources

SSERP Project Engineer MWH

Design Engineer Evans Graves Engineers, Inc.

Contractor Wallace C. Drennan, Inc.


Comments

Attended the Magazine Street Merchants Association Board meeting on February 4, 2004. Met with President and Vice President of the Magazine Street Merchants Association on April 5, 2004. Met with residents of the 600 block of Patton Street on April 6, 2004. Attended the Board of Directors meeting of the Magazine Street Merchants Association on April 14, 2004. Attended the montly meeting of the Magazine Street Merchants Association on April 21, 2004.

Description

The proposed work generally consists of mainline replacements, associated service connections and laterals, pipebursting and associated service connections and laterals; including temporary and final restoration, sewer flow control, traffic maintenance and control, labor, equipment, tools and materials as necessary to perform the work as specified in the contract documents.

Project Location

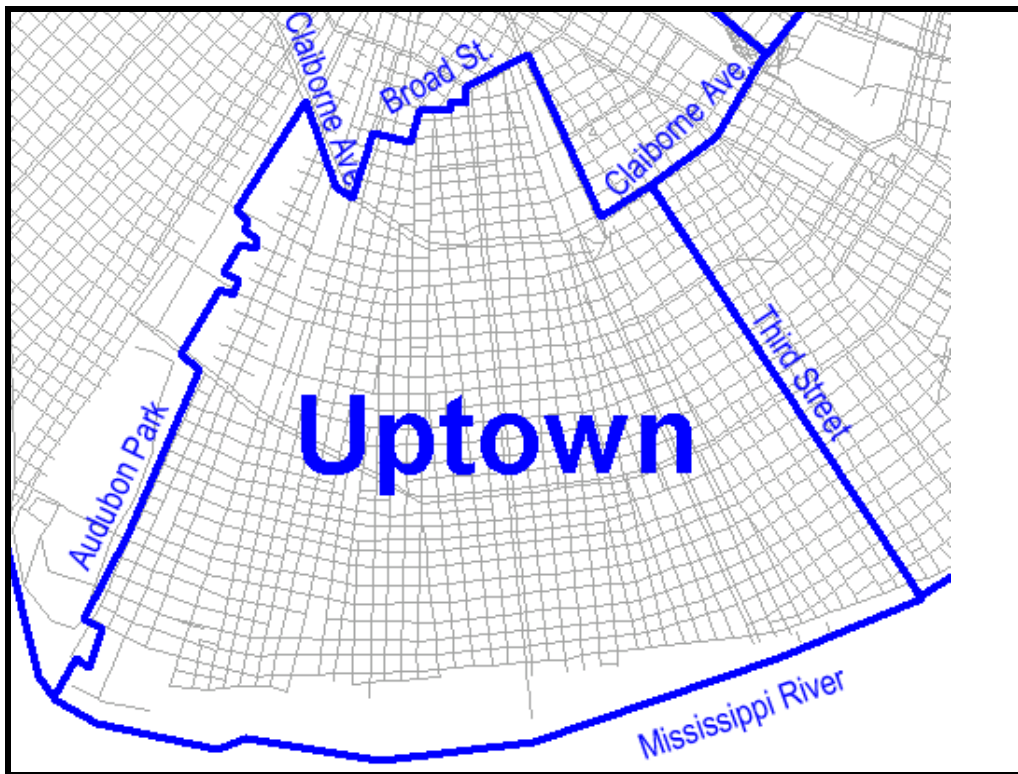

Current Capital Cost \$2,705,087

Description	Projected Start	Target Start	Projected Finish	Target Finish	%	Budgeted Cost	1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018											
							Gantt Chart Timeline											
3948 Uptown Sewer Main Replacement #3																		
Pre-Design	11MAY01 A	11MAY01	28DEC01 A	28DEC01	100	0	Pre-Design											
Preliminary Design	28DEC01 A	28DEC01	19FEB03 A	19FEB03	100	27,541	Preliminary Design											
Final Design	02DEC02 A	02DEC02	02JUN03 A	02JUN03	100	77,259	Final Design											
Pre-Advertisement	27MAR03 A	27MAR03	03JUL03 A	03JUL03	100	0	Pre-Advertisement											
Advertisement	09JUL03 A	09JUL03	15AUG03 A	15AUG03	100	2,917	Advertisement											
Award	15AUG03 A	15AUG03	12JUL04 A	11JUL04	100	2,201	Award											
Construction	12JUL04 A	12JUL04	07MAY05	07APR05	75	2,284,688	Construction											
Field Testing	12JUL04 A	12JUL04	07MAY05	07MAY05	75	34,270	Field Testing											
ESDC	12JUL04 A	12JUL04	07MAY05	07MAY05	75	4,895	ESDC											
Inspection Services	12JUL04 A	12JUL04	07MAY05	07MAY05	75	251,316	Inspection Services											
Construction Final	07MAY05	08APR05	07MAY05	07MAY05	0	0	Construction Final Completion											
S&WB Acceptance	17AUG05	06AUG05	17AUG05	06AUG05	0	0	S&WB Acceptance											
Certification	19MAY06	09MAY06	16AUG06	06AUG06	0	20,000	Certification											

Data date 01MAR05

**Sewerage & Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule**

- Early bar
- Target bar
- Progress bar
