

Sewer System Evaluation and Rehabilitation Program

Rehabilitation Project

Contract Number 3950

Name Uptown Area Sewer Rehabilitation Pipe Lining and Repair No. 2

Basin Uptown

Council Districts A, B

Status: Notice to Proceed with Construction was issued on this contract on March 29, 2004.

Resources

SSERP Project Engineer MWH

Design Engineer Evans Graves Engineers, Inc.

Contractor D & O Contractors, Inc.

Comments


Attended the Magazine Street Merchants Association Executive Board meeting on January 6, 2004.
Attended the Magazine Street Merchants Association Board meeting on January 14, 2004. Attended the Magazine Street Merchants Association Board meeting on February 4, 2004.

3950 - Uptown Area Sewer Rehabilitation Pipe Lining and Repair No. 2

Description

The proposed work consists of full-length and partial cured-in-place lining, excavated main line point repairs, excavated service laterals, internal manhole repairs including installation of cementitious liner, installation of frame to corbel seals, and installation of flow pans, external manhole repairs including replacement of frame and cover, and horizontal and vertical adjustment of frame and cover, and temporary and final restoration. The project is bounded by Third St., Claiborne Ave., Audubon Park, and the Mississippi River.

Project Location

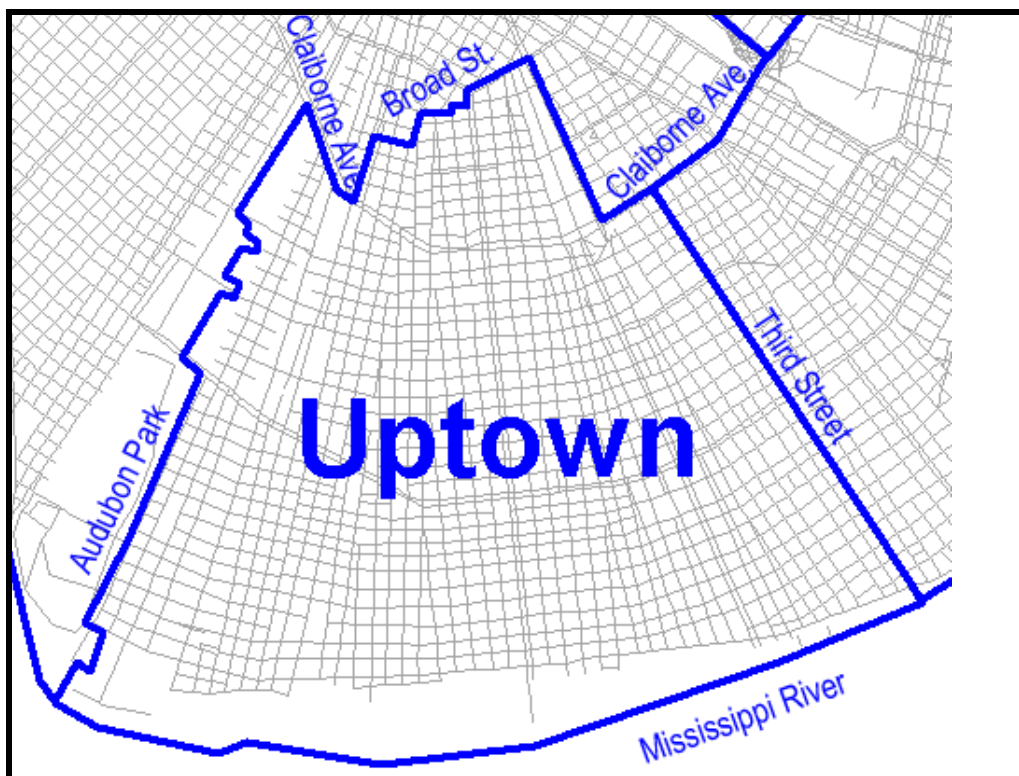

Current Capital Cost \$3,993,754

Description	Projected Start	Target Start	Projected Finish	Target Finish	%	Budgeted Cost	1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018											
							Gantt chart area with year markers from 1997 to 2018.											
3950 Uptown Pipe & Lining Repair #2																		
Pre-Design	11MAY01 A	11MAY01	28DEC01 A	28DEC01	100	0	Pre-Design											
Preliminary Design	28DEC01 A	28DEC01	19FEB03 A	19FEB03	100	27,541	Preliminary Design											
Final Design	02DEC02 A	02DEC02	23JUL03 A	23JUL03	100	17,501	Final Design											
Pre-Advertisement	28MAY03 A	28MAY03	10OCT03 A	10OCT03	100	0	Pre-Advertisement											
Advertisement	15OCT03 A	15OCT03	21NOV03 A	21NOV03	100	2,917	Advertisement											
Award	21NOV03 A	21NOV03	29MAR04 A	29MAR04	100	2,201	Award											
Construction	29MAR04 A	29MAR04	22FEB05 A	21FEB05	100	3,483,288	Construction											
Field Testing	29MAR04 A	29MAR04	23MAR05	23MAR05	88	52,249	Field Testing											
ESDC	29MAR04 A	29MAR04	23MAR05	23MAR05	88	4,895	ESDC											
Inspection Services	29MAR04 A	29MAR04	23MAR05	23MAR05	88	383,162	Inspection Services											
Construction Final	23FEB05 A	22FEB05	23MAR05	23MAR05	88	0	Construction Final Completion											
S&WB Acceptance	18JUL05	22JUN05	18JUL05	22JUN05	0	0	S&WB Acceptance											
Certification	19APR06	25MAR06	17JUL06	22JUN06	0	20,000	Certification											

Data date 01MAR05

**Sewerage & Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule**

- Early bar
- Target bar
- Progress bar
