

Sewer System Evaluation and Rehabilitation Program

Rehabilitation Project

Contract Number	3942
Name	Uptown Area Sewer Excavated Point Repair No. 1
Basin	Uptown
Council Districts	A, B
Status:	Final Acceptance and Resolution(R-201-2004) was issued by the Board for this contract on November 17, 2004.

Resources

SSERP Project Engineer MWH

Design Engineer Evans Graves Engineers, Inc.

Contractor Wallace C. Drennan, Inc.


Comments

Attended the Magazine Street Merchants Association Board meeting on February 4, 2004. Met with President and Vice President of the Magazine Street Merchants Association on April 5, 2004. Met with residents of the 600 block of Patton Street on April 6, 2004. Attended the Board of Directors meeting of the Magazine Street Merchants Association on April 14, 2004. Attended the monthly meeting of the Magazine Street Merchants Association on April 21, 2004.

Description

Rehabilitation of approximately 340 external point repairs, including temporary and final restoration. The project is located in the area bounded by Third Street, Claiborne Avenue, Audubon Park, and the Mississippi River.

Project Location

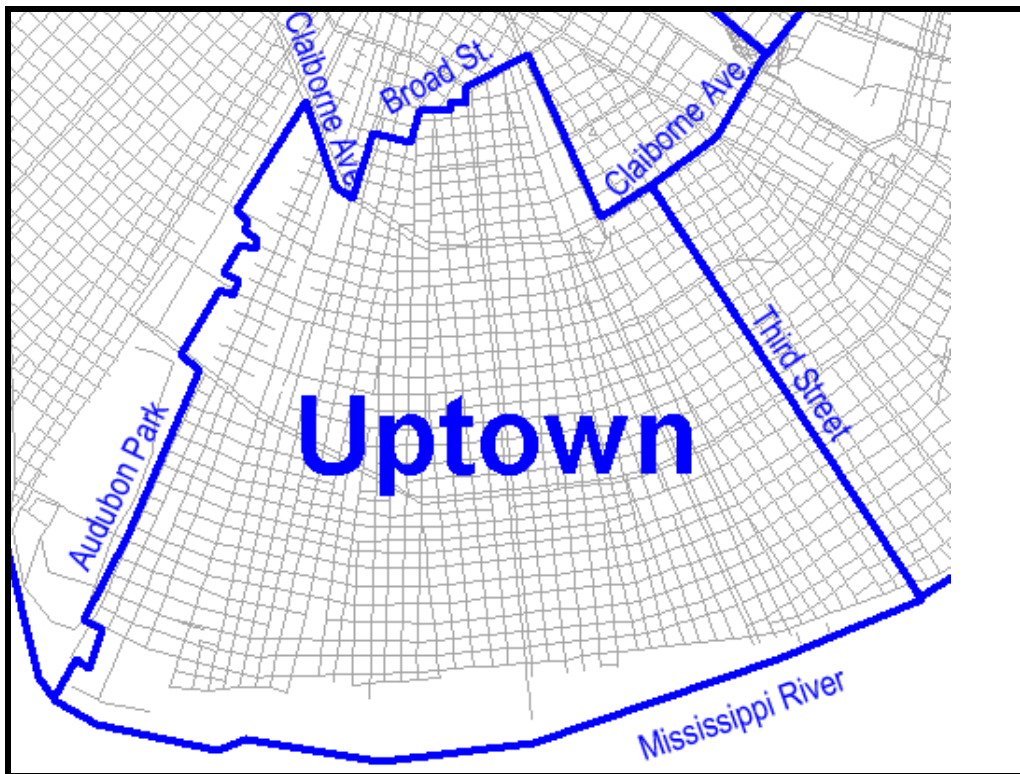

Current Capital Cost \$1,702,154

Description	Projected Start	Baseline Start	Projected Finish	Baseline Finish	%	Budgeted Cost	1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019																							
							Gantt Chart Timeline																							
3942 Uptown Excavated Point Repair #1																														
Pre-Design	11MAY01 A	11MAY01	28DEC01 A	28DEC01	100	0																								
Preliminary Design	28DEC01 A	28DEC01	19FEB03 A	19FEB03	100	27,541																								
Final Design	02DEC02 A	02DEC02	18FEB03 A	18FEB03	100	17,501																								
Pre-Advertisement	16JAN03 A	16JAN03	01APR03 A	01APR03	100	0																								
Advertisement	09APR03 A	09APR03	09MAY03 A	09MAY03	100	2,917																								
Award	09MAY03 A	09MAY03	02SEP03 A	02SEP03	100	2,201																								
Construction	02SEP03 A	02SEP03	01MAY04 A	01MAY04	100	1,448,088																								
Field Testing	02SEP03 A	02SEP03	02JUN04 A	02JUN04	100	21,721																								
ESDC	02SEP03 A	02SEP03	02JUN04 A	02JUN04	100	2,895																								
Inspection Services	02SEP03 A	02SEP03	02JUN04 A	02JUN04	100	159,290																								
Construction Final Completion	02MAY04 A	02MAY04	02JUN04 A	02JUN04	100	0																								
S&WB Acceptance	17NOV04 A	15SEP04	17NOV04 A	15SEP04	100	0																								
Certification	19AUG05	18JUN05	16NOV05	15SEP05	0	20,000																								

Data date 01DEC04
© Primavera Systems, Inc.

Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule

- Early bar
- Target bar
- Progress bar
