

Sewer System Evaluation and Rehabilitation Program

Planning Task

Name Carrollton CSES
Basin Carrollton
Council Districts A, B

Progress

Percent Complete 100 %

Resources

SSERP Project Engineer MWH
Consultant CH2MHill


Comments

The final report was submitted to the USEPA on March 27, 2003, ahead of the Consent Decree milestone due date.

Description

Description of proposed remedial measures to be implemented for the Carrollton basin, which is designed to address defects identified in the Carrollton CSES. The RMAP addresses and resolves issues related to pump station and force main capacity, and addresses measures intended to eliminate unauthorized discharges.

Project

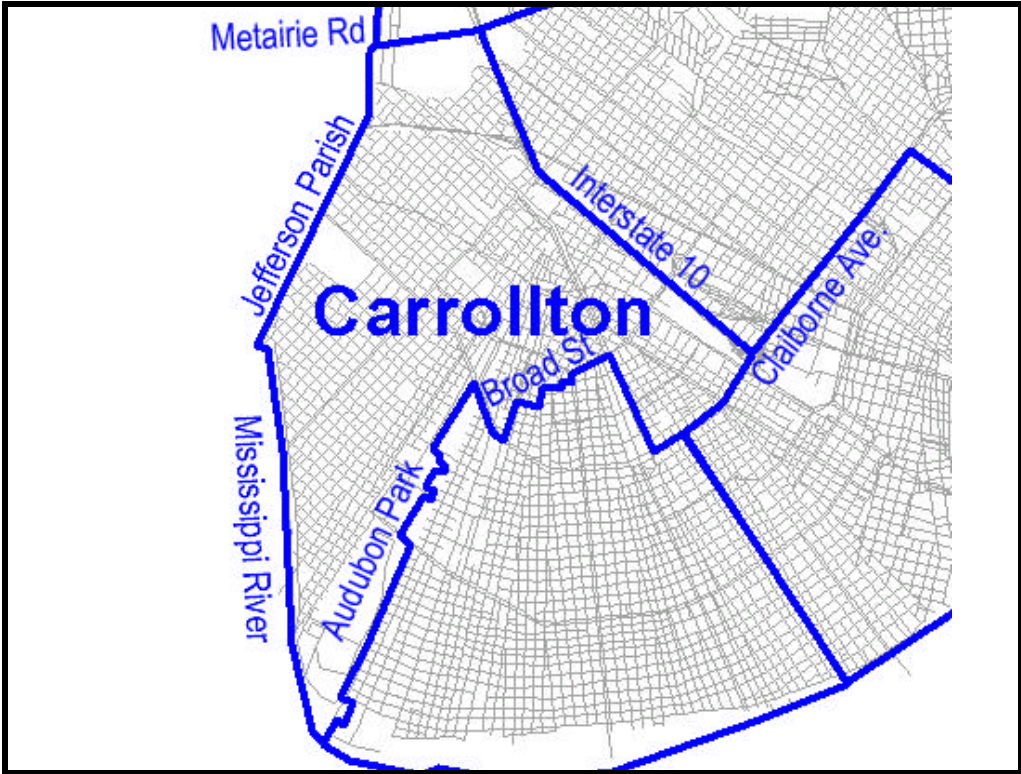

Current Capital Cost \$0

Description	Projected Start	Baseline Start	Projected Finish	Baseline Finish	%	Budgeted Cost																												
							1997	1998	1999	2000	2001	2002	2003	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	2023	2024
Carrollton CSES																																		
CSES	27FEB02 A	27FEB02	27MAR03 A	27MAR03	100	2,899,388																												

Data date	01SEP04
© Primavera Systems, Inc.	

Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule
