

## *Sewer System Evaluation and Rehabilitation Program*

### **Planning Task**

---

<b>Name</b>	CBD/FQ CSES
<b>Basin</b>	CBD/FQ
<b>Council Districts</b>	B, C

### **Progress**

<b>Percent Complete</b>	100 %
-------------------------	-------

### **Resources**

<b>SSERP Project Engineer</b>	MWH
<b>Consultant</b>	CH2M Hill


### **Comments**

A Public Hearing was held for the Central Business District/French Quarter/Warehouse District basin on October 30, 2000. Attended the French Quarter Property Owners Association meeting on May 9, 2001. Attended the French Quarter Business Association meeting on April 17, 2002.

**Description**

Study performed to evaluate the condition and capacity of the collection system in the CBD/FQ basin, including all pump stations in order to determine if the condition and capacity of the collection system are sufficient to prevent unauthorized discharges.

**Project**

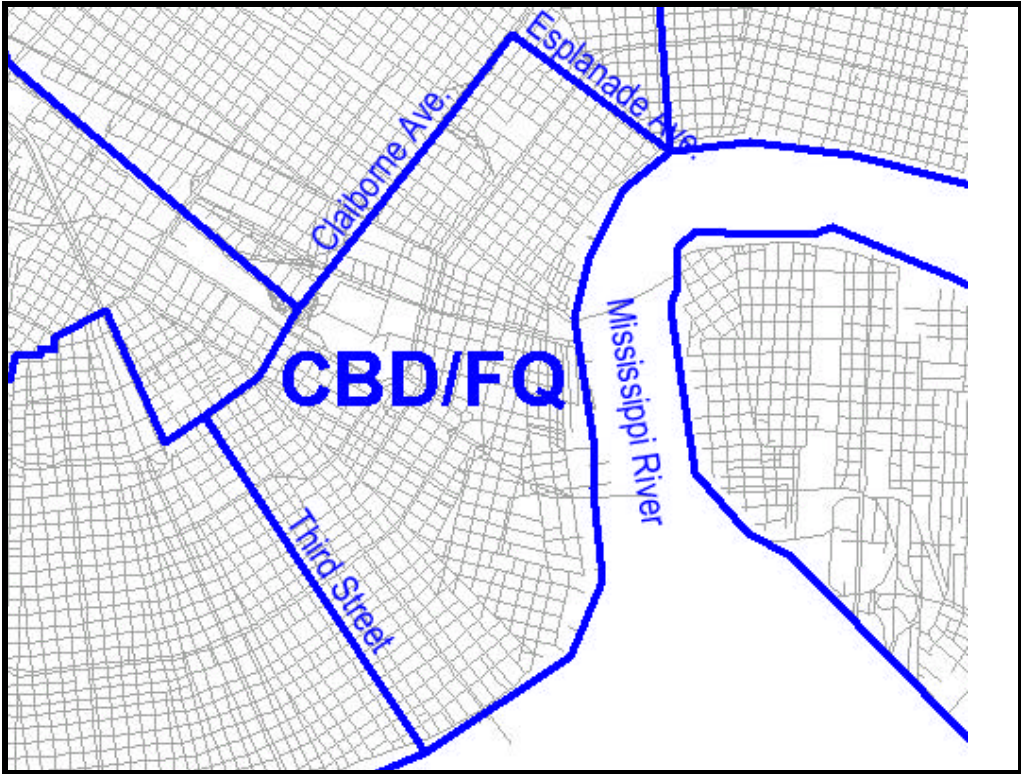

**Current Capital Cost** \$1,532,716

Description	Projected Start	Baseline Start	Projected Finish	Baseline Finish	%	Budgeted Cost	1996 1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019																							
CBD/FQ CSES																														
CSES	01MAY97 A	01MAY97	27MAR98 A	27MAR98	100	1,532,716																								

Start date	01JAN95
Finish date	03MAR18
© Primavera Systems, Inc.	

**Sewerage and Water Board of New Orleans**  
**Sewer System Evaluation and Rehabilitation Program**  
**Master Schedule**

- Early bar
- Target bar
- Progress bar
