

Sewer System Evaluation and Rehabilitation Program

Planning Task

Name Gentilly CSES

Basin Gentilly

Council Districts D, E

Progress

Percent Complete 100 %

Resources

SSERP Project Engineer MWH

Consultant Consoer Townsend Envirodyne Engineers


Comments

Attended the St. Gabriel ACT meeting of October 20, 2003. Attended the Edgewood Park Civic Association meeting of November 18, 2003. Attended the Edgewood Park Civic Association meeting of January 20, 2004.

Description

Study performed to evaluate the condition and capacity of the collection system in the Gentilly basin, including all pump stations in order to determine if the condition and capacity of the collection system are sufficient to prevent unauthorized discharges.

Project

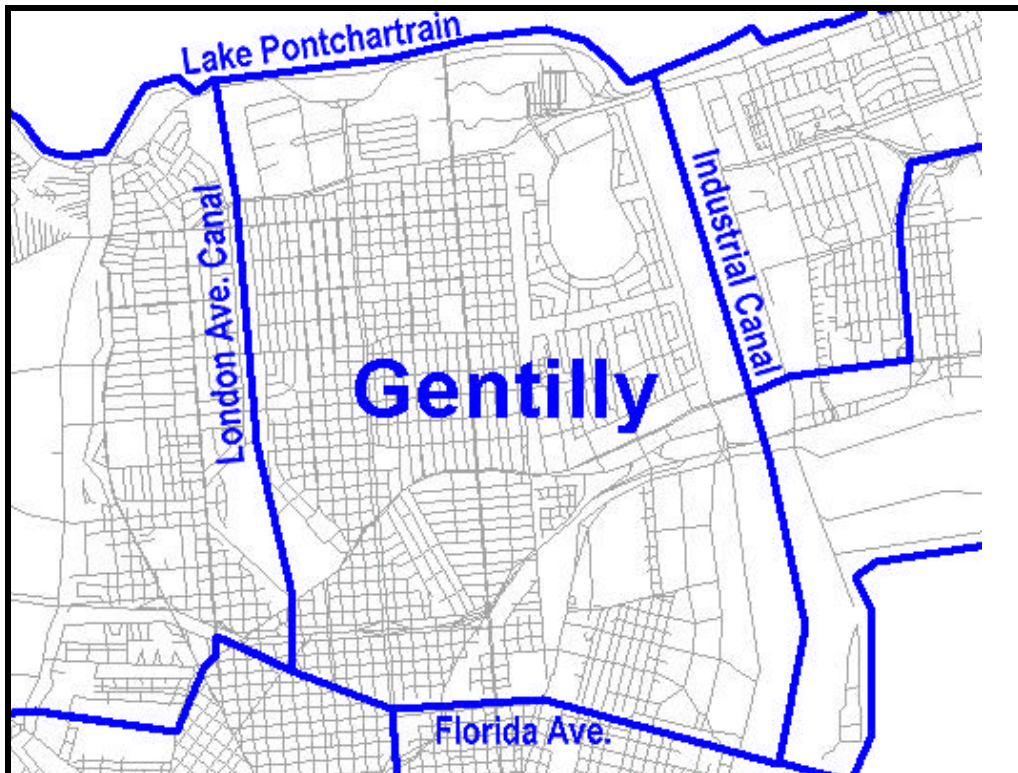

Current Capital Cost \$2,434,040

Description	Projected Start	Baseline Start	Projected Finish	Baseline Finish	%	Budgeted Cost	1996 1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019																							
Gentilly CSES																														
CSES	05JUN98 A	05JUN98	30MAR99 A	30MAR99	100	2,434,040																								

Start date	01JAN95
Finish date	03MAR18
© Primavera Systems, Inc.	

Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule

- Early bar
- Target bar
- Progress bar
