

## *Sewer System Evaluation and Rehabilitation Program*

### **Planning Task**

---

<b>Name</b>	Lakeview CSES
<b>Basin</b>	Lakeview
<b>Council Districts</b>	A, D

### **Progress**

<b>Percent Complete</b>	100 %
-------------------------	-------

### **Resources**

<b>SSERP Project Engineer</b>	N/A
<b>Consultant</b>	RJN Group, Inc.


### **Comments**

Attended the Lakeview Civic Improvement Association meeting of March 14, 2001. Attended the Lakeview Civic Improvement Association meeting of May 9, 2001. Attended the Lakeview Civic Improvement Association meeting of July 11, 2001. Attended the Lakeview Civic Improvement Association meeting of November 14, 2001.

**Description**

Study performed to evaluate the condition and capacity of the collection system in the Lakeview basin, including all pump stations in order to determine if the condition and capacity of the collection system are sufficient to prevent unauthorized discharges.

**Project**

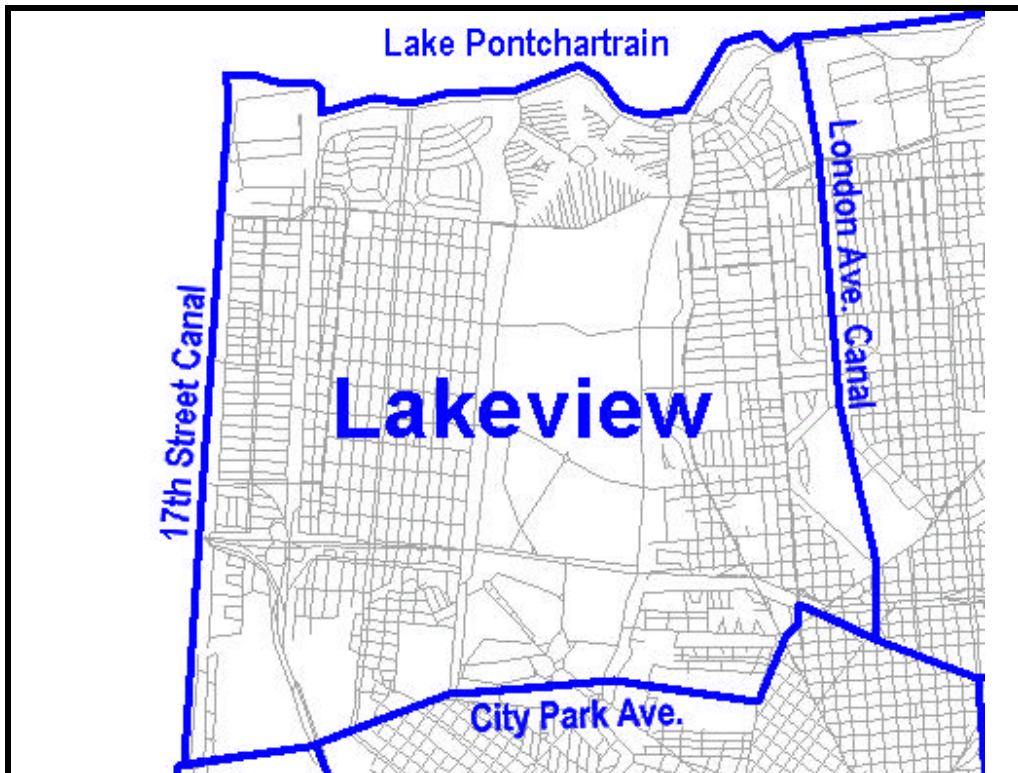

**Current Capital Cost** \$1,000,000

Description	Projected Start	Baseline Start	Projected Finish	Baseline Finish	%	Budgeted Cost	1996 1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019																							
Lakeview CSES																														
CSES	01JUL95 A	01JUL95	15AUG96 A	15AUG96	100	1,000,000																								

Start date	01JAN95
Finish date	03MAR18
© Primavera Systems, Inc.	

**Sewerage and Water Board of New Orleans**  
**Sewer System Evaluation and Rehabilitation Program**  
**Master Schedule**

- Early bar
- Target bar
- Progress bar
