

Sewer System Evaluation and Rehabilitation Program

Planning Task

Name Mid-City RMAP
Basin Mid-City
Council Districts A, B, C, D

Progress

Percent Complete 100 %

Resources


SSERP Project Engineer MWH
Consultant MWH

Comments

Description

Description of proposed remedial measures to be implemented for the Mid-City basin, which is designed to address defects identified in the Mid-City CSES. The RMAP addresses and resolves issues related to pump station and force main capacity, and addresses measures intended to eliminate unauthorized discharges.

Project

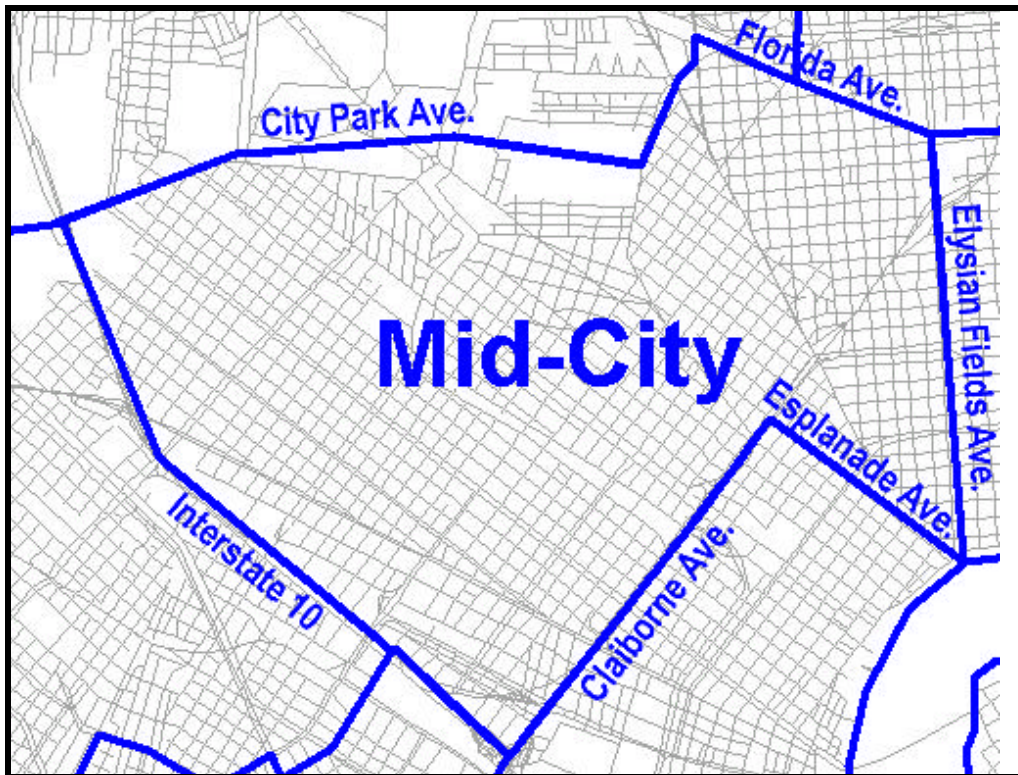

Current Capital Cost \$0

Description	Projected Start	Baseline Start	Projected Finish	Baseline Finish	%	Budgeted Cost	1996 1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019																							
Mid-City RMAP																														
RMAP	16APR01 A	16APR01	15AUG01 A	15AUG01	100	0	<div style="display: flex; align-items: center;"> <div style="width: 10px; height: 10px; border: 1px solid black; margin-right: 5px;"></div> RMAP </div>																							

Start date	01JAN95
Finish date	03MAR18
© Primavera Systems, Inc.	

Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule

- Early bar
- Target bar
- Progress bar
