

*Sewer System Evaluation and Rehabilitation Program*

**Planning Task**

---

**Name** Lower Ninth Ward CSES  
**Basin** Lower Ninth Ward  
**Council Districts** C, D, E

**Progress**

**Percent Complete** 100 %

**Resources**

**SSERP Project Engineer** MWH  
**Consultant** Roy F. Weston, Inc.


**Comments**

The Lower Ninth Ward CSES was submitted to the USEPA on March 27, 2002.

**Description**

Study to be performed to evaluate the condition and capacity of the collection system in the 9th Ward basin, including all pump stations in order to determine if the condition and capacity of the collection system are sufficient to prevent unauthorized discharges.

**Project Location**

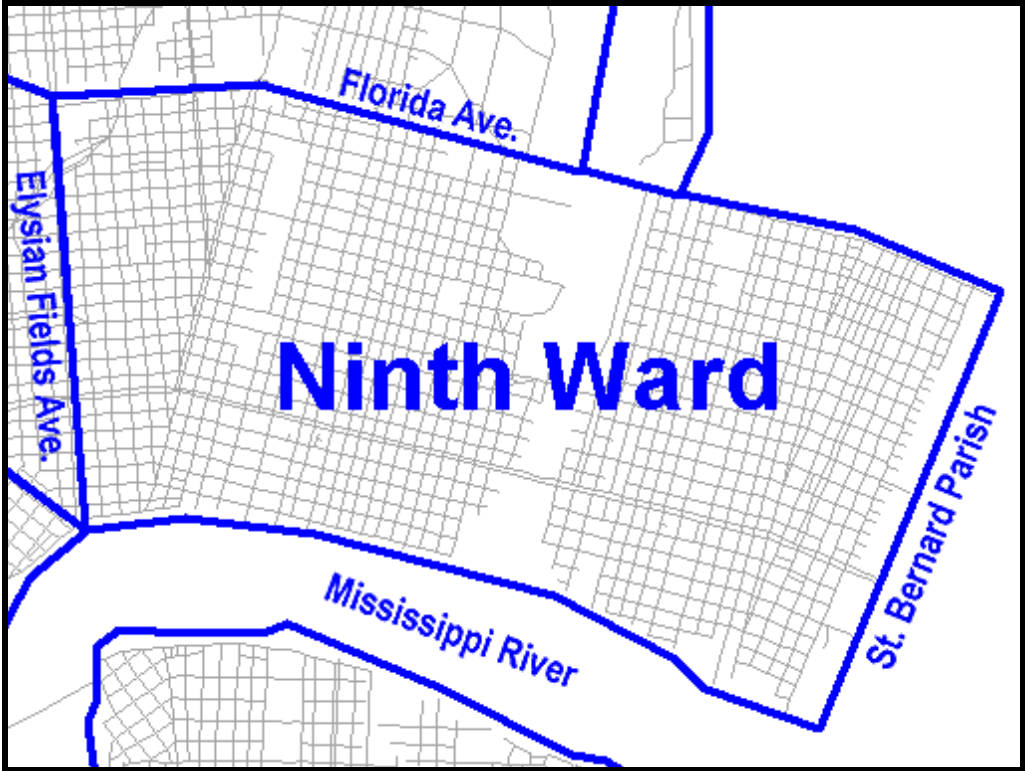

**Current Capital Cost** \$2,775,411

| Description     | Projected Start | Baseline Start | Projected Finish | Baseline Finish | %   | Budgeted Cost | 1996 1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019 |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|-----------------|-----------------|----------------|------------------|-----------------|-----|---------------|-------------------------------------------------------------------------------------------------------------------------|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|
|                 |                 |                |                  |                 |     |               |                                                                                                                         |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| Ninth Ward CSES |                 |                |                  |                 |     |               |                                                                                                                         |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| CSES            | 16MAY01 A       | 16MAY01        | 27MAR02 A        | 27MAR02         | 100 | 2,775,411     |                                                                                                                         |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |

|                           |         |
|---------------------------|---------|
| Start date                | 01JAN95 |
| Finish date               | 03MAR18 |
|                           |         |
| © Primavera Systems, Inc. |         |

**Sewerage and Water Board of New Orleans**  
**Sewer System Evaluation and Rehabilitation Program**  
**Master Schedule**

- Early bar
- Target bar
- Progress bar
