

Sewer System Evaluation and Rehabilitation Program

Rehabilitation Project

Contract Number	3909
Name	West Lakeview Manhole Rehabilitation
Basin	Lakeview
Council Districts	A, D
Status:	The Sewerage and Water Board certified as complete all the work performed under this contract, as required by USEPA Assistance Grant No. XP-996667-01-3, in October 2001.

Resources

SSERP Project Engineer MWH

Design Engineer Consoer Townsend Envirodyne Engineers

Contractor E.B. Feucht & Sons, Inc.


Comments

Attended the Lakeview Civic Improvement Association meeting of March 14, 2001. Attended the Lakeview Civic Improvement Association meeting of May 9, 2001. Attended the Lakeview Civic Improvement Association meeting of July 11, 2001. Attended the Lakeview Civic Improvement Association meeting of November 14, 2001.

Description

Rehabilitation of approximately 1,100 existing sanitary sewer manholes including frame and cover replacements, resetting frames, frame and cover adjustments, elastomeric corbel seals, lightweight cementitious manhole lining, and inflow dish inserts.

Project Location

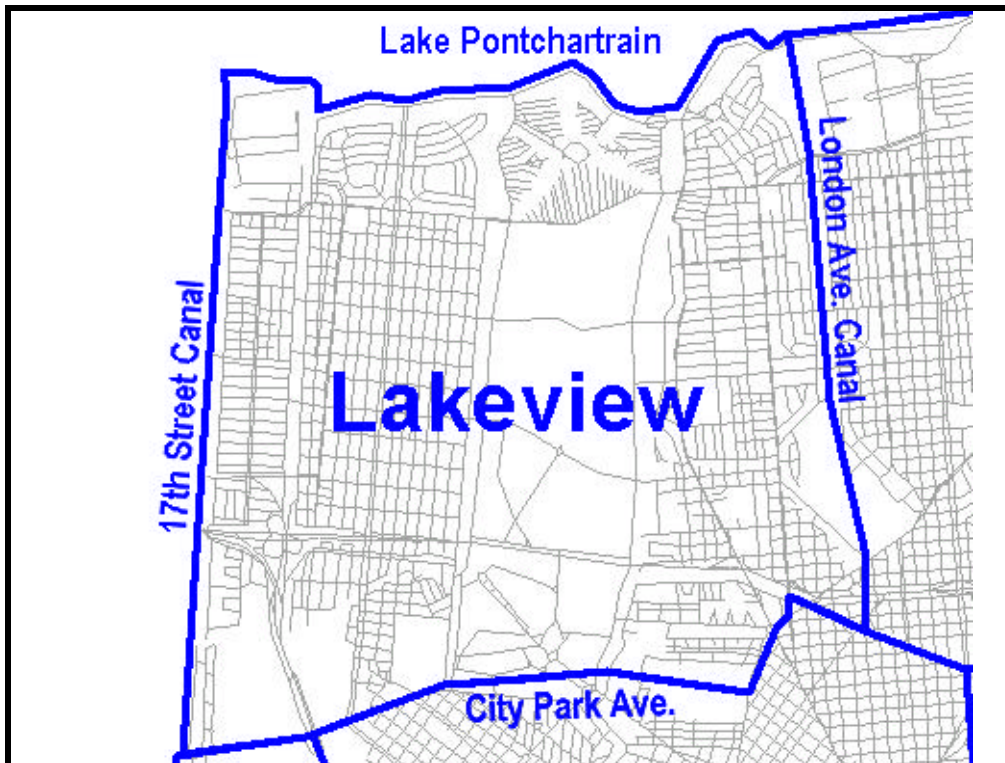

Current Capital Cost \$1,902,571

Description	Projected Start	Baseline Start	Projected Finish	Baseline Finish	%	Budgeted Cost																								
							1997	1998	1999	2000	2001	2002	2003	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015	2016	2017	2018	2019	2020
3909 West Lakeview Manhole Rehabilitation																														
Pre-Design	13SEP97 A	13SEP97	28SEP97 A	28SEP97	100	0	Pre-Design																							
Preliminary Design	29SEP97 A	29SEP97	10FEB98 A	10FEB98	100	32,370	Preliminary Design																							
Final Design	10FEB98 A	10FEB98	04JUN98 A	04JUN98	100	51,810	Final Design																							
Advertisement	11JUN98 A	11JUN98	12FEB99 A	12FEB99	100	10,869	Advertisement																							
Award	17FEB99 A	17FEB99	23APR99 A	23APR99	100	2,200	Award																							
Construction	02AUG99 A	02AUG99	13JUN00 A	13JUN00	100	1,598,277	Construction																							
Field Testing	02AUG99 A	02AUG99	13JUN00 A	13JUN00	100	2,745	Field Testing																							
ESDC	02AUG99 A	02AUG99	13JUN00 A	13JUN00	100	9,000	ESDC																							
Inspection Services	02AUG99 A	02AUG99	13JUN00 A	13JUN00	100	175,300	Inspection Services																							
S&WB Resolution	08OCT00 A	08OCT00	08OCT00 A	08OCT00	100	0	S&WB Resolution																							
Certification	16JUL01 A	16JUL01	08OCT01 A	08OCT01	100	20,000	Certification																							

Data date	01SEP04
© Primavera Systems, Inc.	

Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule
