

Sewer System Evaluation and Rehabilitation Program

Rehabilitation Project

Contract Number 3983
Name Lower Ninth Ward Sewer Rehabilitation No. 2.
Basin Lower Ninth Ward
Council Districts C, D, E
Status:

Resources

SSERP Project Engineer MWH

Design Engineer CH2MHill


Contractor

Comments

Description

Rehabilitation of sewer lines as recommended by the RMAP.

Project Location

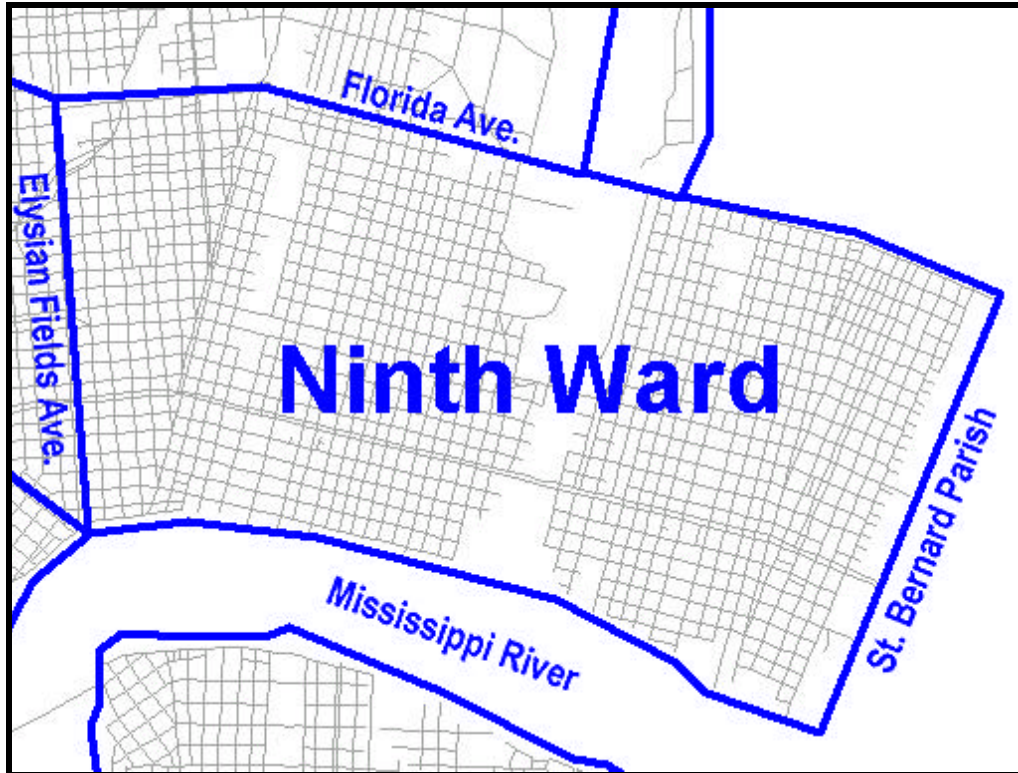

Current Capital Cost \$3,788,610

Description	Projected Start	Target Start	Projected Finish	Target Finish	%	Budgeted Cost	1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019																							
							Gantt Chart Area																							
3983 Ninth Ward Sewer Rehabilitation No. 2																														
Pre-Design	18JUN03 A	18JUN03	06OCT03 A	06OCT03	100	0	■ Pre-Design																							
Preliminary Design	13JAN04 A	13JAN04	19JAN05 A	12OCT04	100	25,007	■ Preliminary Design																							
Final Design	19APR05	15MAR05	15JUN05	15JUN05	0	33,292	■ Final Design																							
Pre-Advertisement	25MAY05	21JUN05	07SEP05	14SEP05	0	0	■ Pre-Advertisement																							
Advertisement	14SEP05	14SEP05	21OCT05	14OCT05	0	2,322	■ Advertisement																							
Award	21OCT05	14OCT05	22FEB06	03APR06	0	774	■ Award																							
Construction	22FEB06	03APR06	17JAN07	27FEB07	0	3,291,677	■ Construction																							
Field Testing	22FEB06	03APR06	16FEB07	29MAR07	0	49,375	■ Field Testing																							
ESDC	22FEB06	03APR06	16FEB07	29MAR07	0	4,079	■ ESDC																							
Inspection Services	22FEB06	03APR06	16FEB07	29MAR07	0	362,084	■ Inspection Services																							
Construction Final	18JAN07	27FEB07	16FEB07	29MAR07	0	0	■ Construction Final Completion																							
S&WB Acceptance	16MAY07	27JUN07	16MAY07	28JUN07	0	0	■ S&WB Acceptance																							
Certification	16FEB08	29MAR08	15MAY08	27JUN08	0	20,000	■ Certification																							

Data date 01FEB05

© Primavera Systems, Inc.

**Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule**

■ Early bar

■ Target bar

■ Progress bar
