

Sewer System Evaluation and Rehabilitation Program

Rehabilitation Project

Contract Number 3981
Name Lower Ninth Ward Line Replacement No. 2
Basin Lower Ninth Ward
Council Districts C, D, E
Status:

Resources

SSERP Project Engineer MWH

Design Engineer CH2MHill


Contractor

Comments

Description

Rehabilitation of sewer lines as recommended by the RMAP.

Project Location

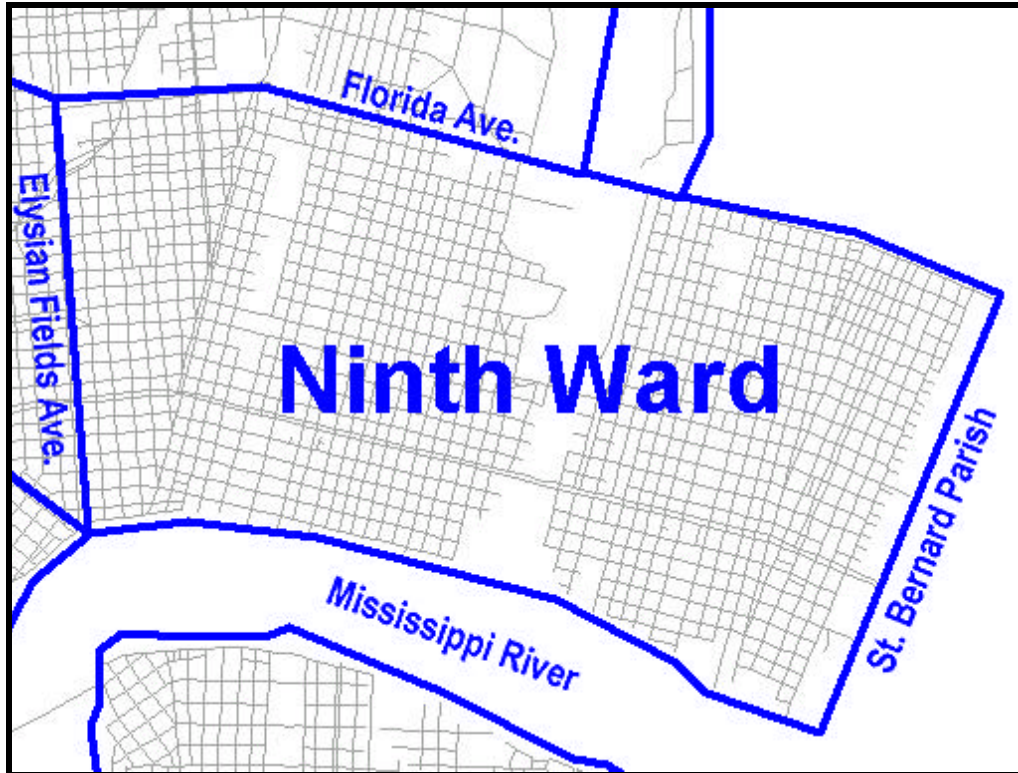

Current Capital Cost \$994,785

Description	Projected Start	Target Start	Projected Finish	Target Finish	%	Budgeted Cost	1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019																							
							Gantt Chart Timeline																							
3981 Ninth Ward Line Replacement No. 2																														
Pre-Design	18JUN03 A	18JUN03	06OCT03 A	06OCT03	100	0																								
Preliminary Design	13JAN04 A	13JAN04	19JAN05 A	12OCT04	100	25,007																								
Final Design	21MAR05	15MAR05	17MAY05	15JUN05	0	33,292																								
Pre-Advertisement	27APR05	21JUN05	03AUG05	14SEP05	0	0																								
Advertisement	10AUG05	14SEP05	16SEP05	14OCT05	0	2,322																								
Award	16SEP05	14OCT05	07FEB06	03APR06	0	774																								
Construction	07FEB06	03APR06	02JAN07	27FEB07	0	808,277																								
Field Testing	07FEB06	03APR06	01FEB07	29MAR07	0	12,124																								
ESDC	07FEB06	03APR06	01FEB07	29MAR07	0	4,079																								
Inspection Services	07FEB06	03APR06	01FEB07	29MAR07	0	88,910																								
Construction Final	03JAN07	27FEB07	01FEB07	29MAR07	0	0																								
S&WB Acceptance	16MAY07	27JUN07	16MAY07	28JUN07	0	0																								
Certification	16FEB08	29MAR08	15MAY08	27JUN08	0	20,000																								

Data date 01FEB05

**Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule**

- Early bar
- Target bar
- Progress bar
