

Sewer System Evaluation and Rehabilitation Program

Rehabilitation Project

Contract Number 3982
Name Lower Ninth Ward Sewer Rehabilitation No. 1
Basin Lower Ninth Ward
Council Districts C, D, E
Status:

Resources

SSERP Project Engineer MWH

Design Engineer CH2MHill


Contractor

Comments

Description

Rehabilitation of sewer lines as recommended by the RMAP.

Project Location

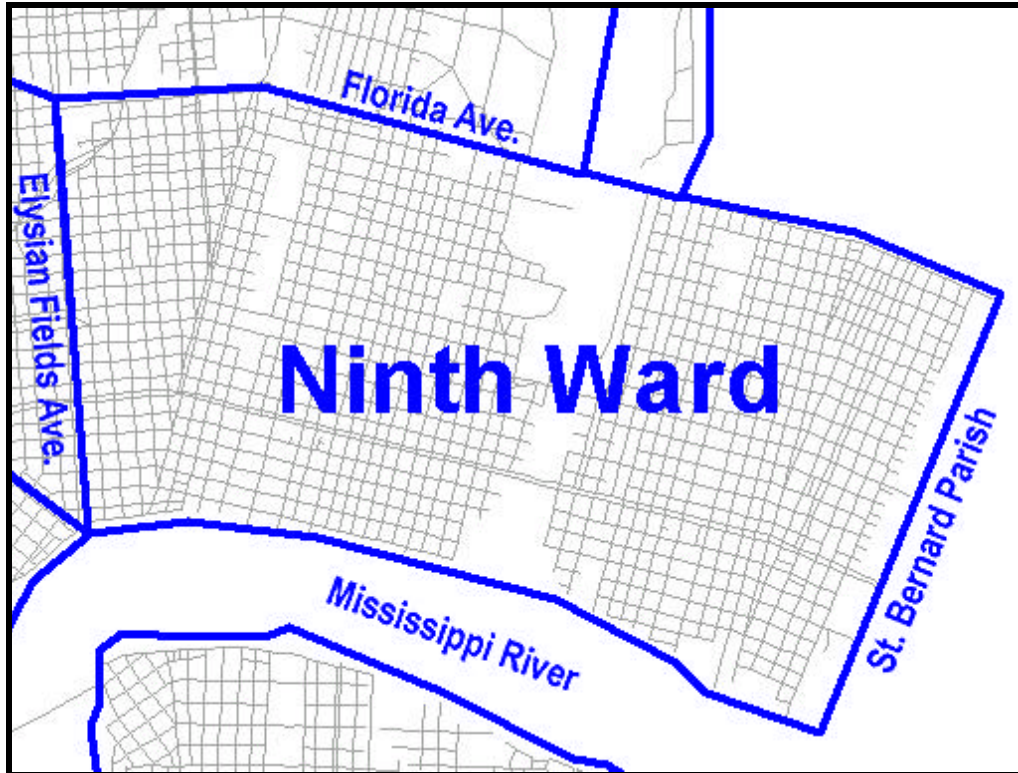

Current Capital Cost \$3,926,499

Description	Projected Start	Target Start	Projected Finish	Target Finish	%	Budgeted Cost	1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019																							
							Gantt Chart Timeline																							
3982 Ninth Ward Sewer Rehabilitation No. 1																														
Pre-Design	18JUN03 A	18JUN03	06OCT03 A	06OCT03	100	0																								
Preliminary Design	13JAN04 A	13JAN04	19JAN05 A	12OCT04	100	25,007																								
Final Design	19APR05	14APR05	15JUN05	18JUL05	0	33,292																								
Pre-Advertisement	25MAY05	20JUL05	07SEP05	12OCT05	0	0																								
Advertisement	14SEP05	12OCT05	21OCT05	11NOV05	0	2,322																								
Award	21OCT05	11NOV05	22FEB06	01MAY06	0	774																								
Construction	22FEB06	01MAY06	17JAN07	27MAR07	0	3,414,244																								
Field Testing	22FEB06	01MAY06	16FEB07	26APR07	0	51,214																								
ESDC	22FEB06	01MAY06	16FEB07	26APR07	0	4,079																								
Inspection Services	22FEB06	01MAY06	16FEB07	26APR07	0	375,567																								
Construction Final	18JAN07	27MAR07	16FEB07	26APR07	0	0																								
S&WB Acceptance	16MAY07	25JUL07	16MAY07	26JUL07	0	0																								
Certification	16FEB08	26APR08	15MAY08	25JUL08	0	20,000																								

Data date 01FEB05

Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule

- Early bar
- Target bar
- Progress bar
