

*Sewer System Evaluation and Rehabilitation Program*

**Rehabilitation Project**

---

**Contract Number**            3984

**Name**                            Lower Ninth Ward Sewer Rehabilitation No. 3.

**Basin**                            Lower Ninth Ward

**Council Districts**            C, D, E

**Status:**

**Resources**

**SSERP Project Engineer** MWH

**Design Engineer**            CH2MHill


**Contractor**

**Comments**

**Description**

Rehabilitation of sewer lines as recommended by the RMAP.

**Project Location**

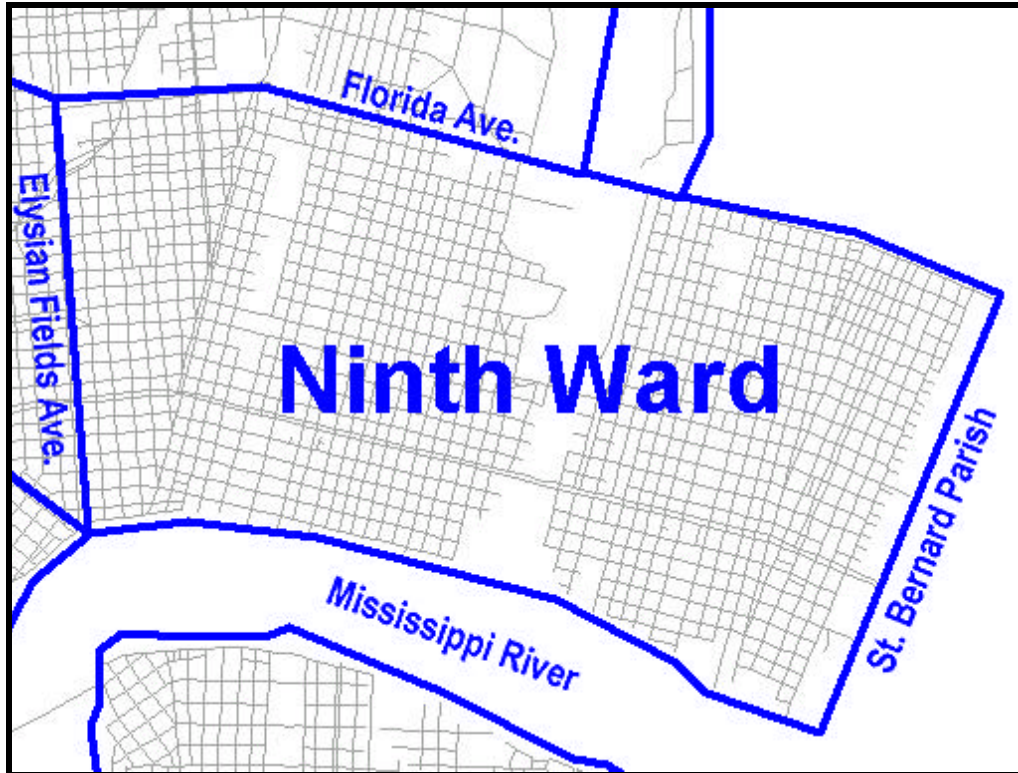

**Current Capital Cost**    \$3,797,452

Description	Projected Start	Target Start	Projected Finish	Target Finish	%	Budgeted Cost	1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019																							
							Gantt Chart Timeline																							
<b>3984 Ninth Ward Sewer Rehabilitation No. 3</b>																														
Pre-Design	18JUN03 A	18JUN03	06OCT03 A	06OCT03	100	0																								
Preliminary Design	13JAN04 A	13JAN04	19JAN05 A	12OCT04	100	25,007																								
Final Design	18MAY05	14APR05	14JUL05	18JUL05	0	33,292																								
Pre-Advertisement	29JUN05	20JUL05	05OCT05	12OCT05	0	0																								
Advertisement	12OCT05	12OCT05	18NOV05	11NOV05	0	2,322																								
Award	18NOV05	11NOV05	06APR06	01MAY06	0	774																								
Construction	06APR06	01MAY06	01MAR07	27MAR07	0	3,299,979																								
Field Testing	06APR06	01MAY06	31MAR07	26APR07	0	49,500																								
ESDC	06APR06	01MAY06	31MAR07	26APR07	0	4,079																								
Inspection Services	06APR06	01MAY06	31MAR07	26APR07	0	362,998																								
Construction Final	02MAR07	27MAR07	31MAR07	26APR07	0	0																								
S&WB Acceptance	18JUL07	25JUL07	18JUL07	26JUL07	0	0																								
Certification	19APR08	26APR08	17JUL08	25JUL08	0	20,000																								

Data date 01FEB05

**Sewerage and Water Board of New Orleans**  
**Sewer System Evaluation and Rehabilitation Program**  
**Master Schedule**

- Early bar
- Target bar
- Progress bar
