

Sewer System Evaluation and Rehabilitation Program

Rehabilitation Project

Contract Number 3943
Name Uptown Area Sewer Excavated Point Repair No. 2
Basin Uptown
Council Districts A, B

Status:

Final Acceptance and Resolution (R-099-2004) was issued by the Board for this contract on July 21, 2004.

Resources

SSERP Project Engineer MWH

Design Engineer Evans Graves Engineers, Inc.

Contractor D & O Contractors, Inc.


Comments

Attended the Magazine Street Merchants Association Board meeting on February 4, 2004. Met with President and Vice President of the Magazine Street Merchants Association on April 5, 2004. Met with residents of the 600 block of Patton Street on April 6, 2004. Attended the Board of Directors meeting of the Magazine Street Merchants Association on April 14, 2004. Attended the monthly meeting of the Magazine Street Merchants Association on April 21, 2004.

Description


Rehabilitation of sewer lines as recommended by the RMAP.

Project Location

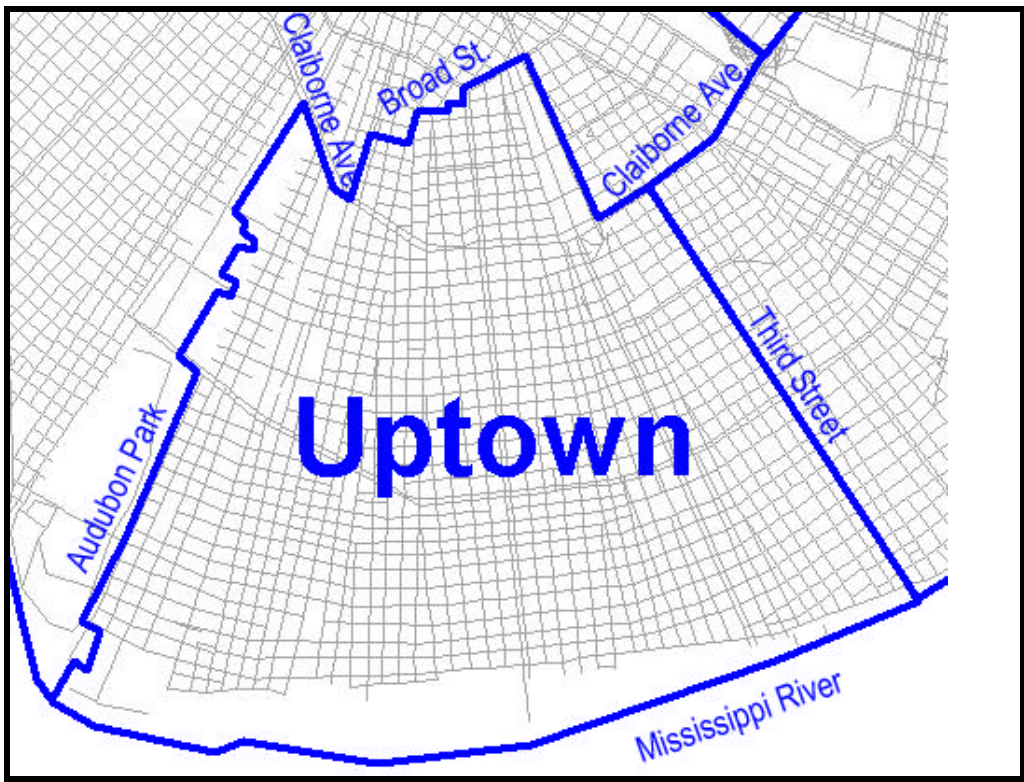

Current Capital Cost \$1,308,322

Description	Projected Start	Baseline Start	Projected Finish	Baseline Finish	%	Budgeted Cost																								
							1997	1998	1999	2000	2001	2002	2003	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015	2016	2017	2018	2019	2020
3943 Uptown Excavated Point Repair #2																														
Pre-Design	11MAY01 A	11MAY01	28DEC01 A	28DEC01	100	0																								
Preliminary Design	28DEC01 A	28DEC01	19FEB03 A	19FEB03	100	27,541																								
Final Design	02DEC02 A	02DEC02	01APR03 A	01APR03	100	17,501																								
Pre-Advertisement	13FEB03 A	13FEB03	16MAY03 A	16MAY03	100	0																								
Advertisement	19MAY03 A	19MAY03	20JUN03 A	20JUN03	100	2,917																								
Award	20JUN03 A	20JUN03	13OCT03 A	13OCT03	100	2,201																								
Construction	13OCT03 A	13OCT03	21APR04 A	21APR04	100	1,234,502																								
Field Testing	13OCT03 A	13OCT03	30APR04 A	30APR04	100	18,518																								
ESDC	13OCT03 A	13OCT03	30APR04 A	30APR04	100	5,996																								
Inspection Services	13OCT03 A	13OCT03	30APR04 A	30APR04	100	135,795																								
Construction Final	22APR04 A	22APR04	30APR04 A	30APR04	100	0																								
S&WB Resolution	21JUL04 A	21JUL04	21JUL04 A	21JUL04	100	0																								
Certification	22APR05	23APR05	20JUL05	21JUL05	0	20,000																								

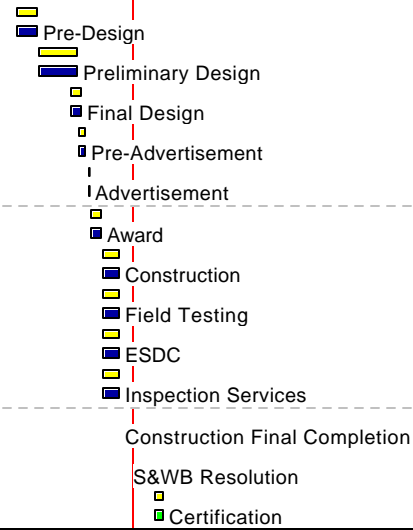

Data date	01SEP04
© Primavera Systems, Inc.	

Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule
