

## *Sewer System Evaluation and Rehabilitation Program*

### **Planning Task**

---

<b>Name</b>	CBD/FQ RMAP
<b>Basin</b>	CBD/FQ
<b>Council Districts</b>	B, C

### **Progress**

<b>Percent Complete</b>	100 %
-------------------------	-------

### **Resources**

<b>SSERP Project Engineer</b>	MWH
<b>Consultant</b>	MWH


### **Comments**

A Public Hearing was held for the Central Business District/French Quarter/Warehouse District basin on October 30, 2000. Attended the French Quarter Property Owners Association meeting on May 9, 2001. Attended the French Quarter Business Association meeting on April 17, 2002.

**Description**

Description of proposed remedial measures to be implemented for the CBD/FQ basin, which is designed to address defects identified in the CBD/FQ CSES. The RMAP addresses and resolves issues related to pump station and force main capacity, and addresses measures intended to eliminate unauthorized discharges.

**Project**

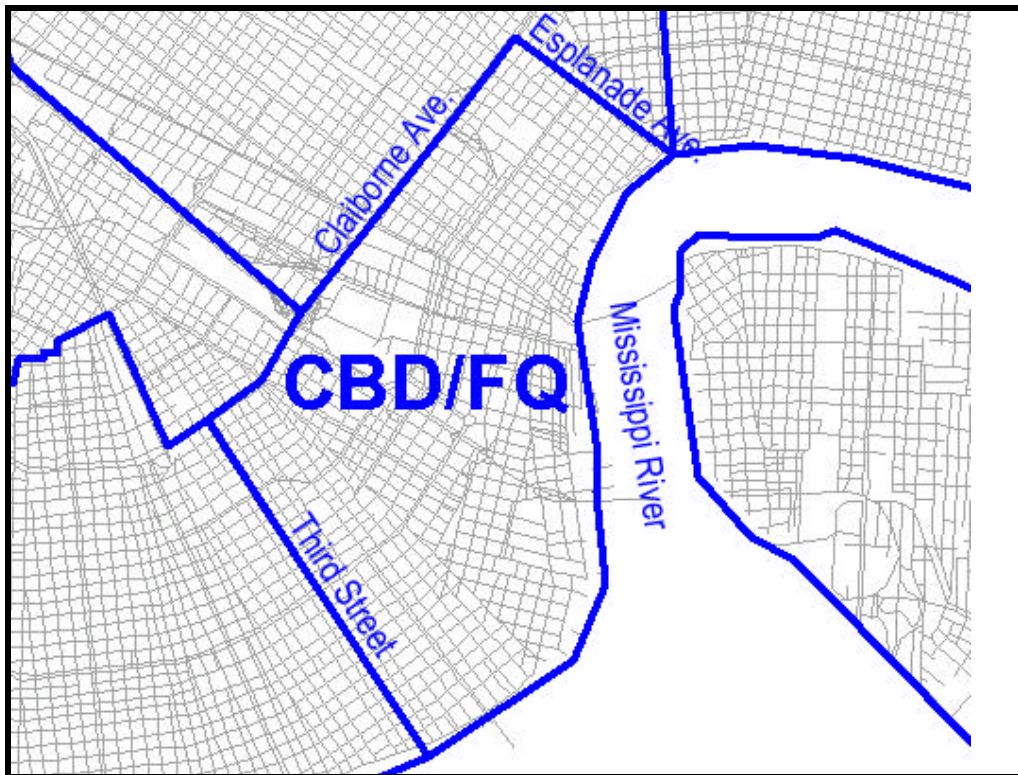

**Current Capital Cost**            \$0

Description	Projected Start	Baseline Start	Projected Finish	Baseline Finish	%	Budgeted Cost	1996 1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019																							
CBD/FQ RMAP																														
RMAP	15APR98 A	15APR98	07AUG98 A	07AUG98	100	0																								

Start date	01JAN95
Finish date	03MAR18
© Primavera Systems, Inc.	

**Sewerage and Water Board of New Orleans**  
**Sewer System Evaluation and Rehabilitation Program**  
**Master Schedule**

- Early bar
- Target bar
- Progress bar
