

Sewer System Evaluation and Rehabilitation Program

Planning Task

Name	Lakeview RMAP
Basin	Lakeview
Council Districts	A, D

Progress

Percent Complete	100 %
-------------------------	-------

Resources

SSERP Project Engineer	MWH
Consultant	MWH


Comments

Attended the Lakeview Civic Improvement Association meeting of March 14, 2001. Attended the Lakeview Civic Improvement Association meeting of May 9, 2001. Attended the Lakeview Civic Improvement Association meeting of July 11, 2001. Attended the Lakeview Civic Improvement Association meeting of November 14, 2001.

Description

Description of proposed remedial measures to be implemented for the Lakeview basin, which is designed to address defects identified in the Lakeview CSES. The RMAP addresses and resolves issues related to pump station and force main capacity, and addresses measures intended to eliminate unauthorized discharges.

Project

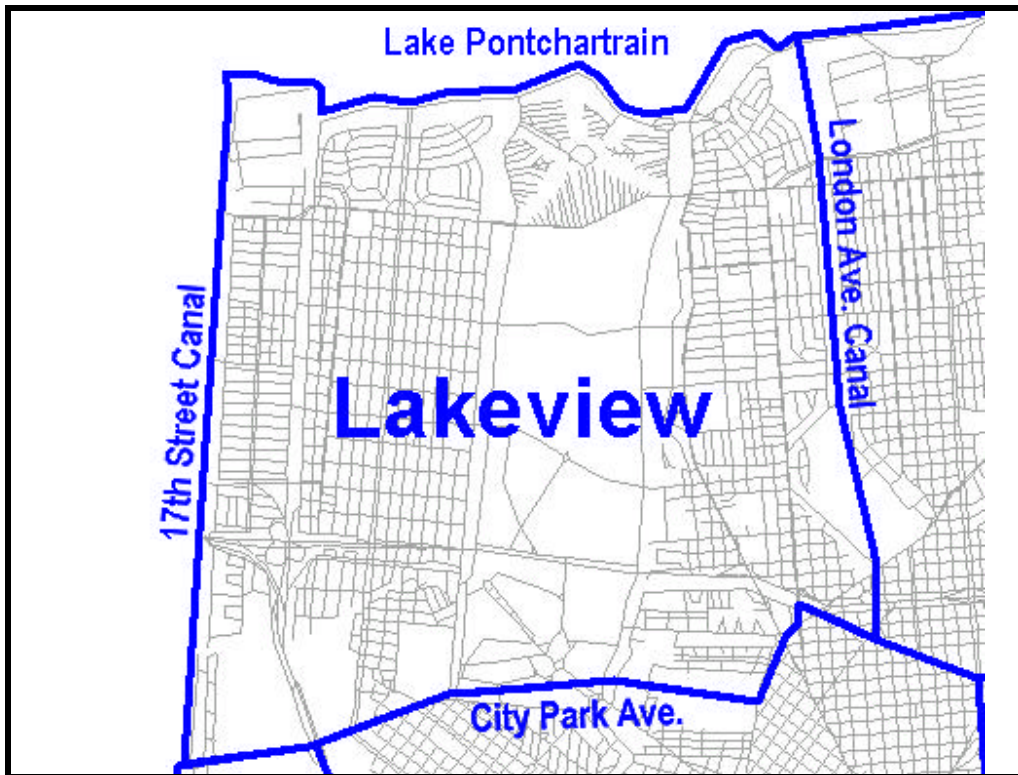

Current Capital Cost \$0

Description	Projected Start	Baseline Start	Projected Finish	Baseline Finish	%	Budgeted Cost	1996 1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019																							
Lakeview RMAP																														
RMAP	01NOV96 A	01NOV96	02JAN97 A	02JAN97	100	0																								

Start date	01JAN95
Finish date	03MAR18
© Primavera Systems, Inc.	

Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule

- Early bar
- Target bar
- Progress bar
