

Sewer System Evaluation and Rehabilitation Program

Planning Task

Name New Orleans East CSES
Basin New Orleans East
Council Districts D, E

Progress

Percent Complete 100 %

Resources

SSERP Project Engineer MWH
Consultant Consoer Townsend Envirodyne Engineers


Comments

The New Orleans East CSES was submitted to the USEPA on March 24, 2004, ahead of the Consent Decree milestone due date of April 1, 2004.

Description

Study to be performed to evaluate the condition and capacity of the collection system in the New Orleans basin, including all pump stations in order to determine if the condition and capacity of the collection system are sufficient to prevent unauthorized discharges.

Project

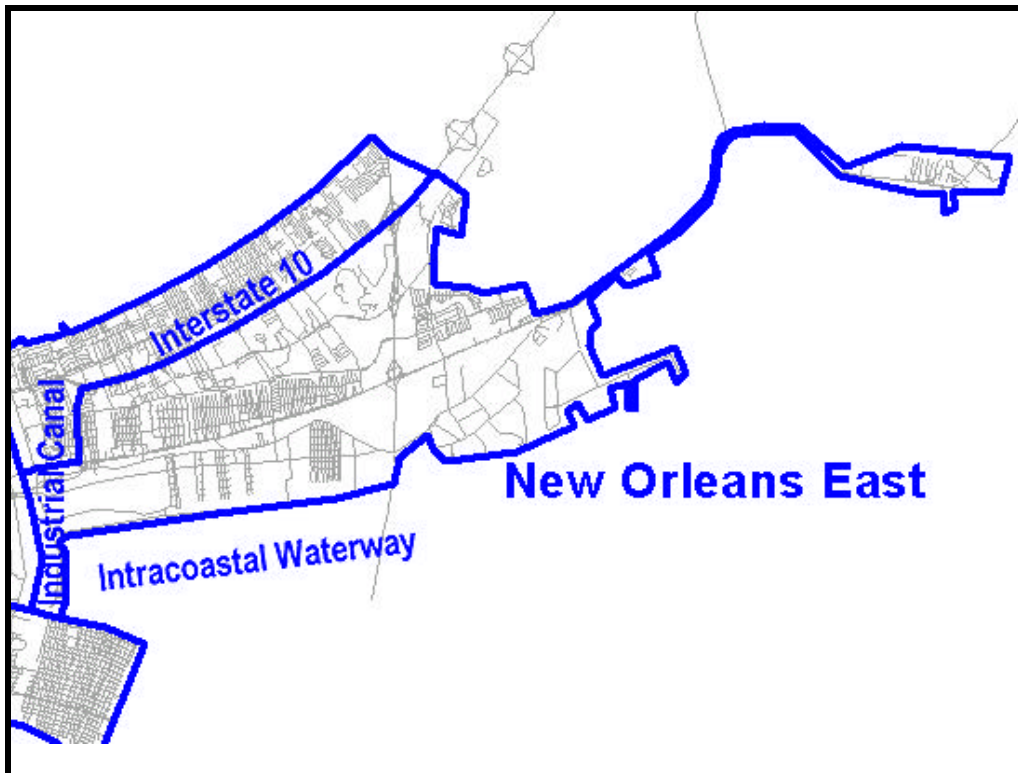

Current Capital Cost \$3,000,000

Description	Projected Start	Baseline Start	Projected Finish	Baseline Finish	%	Budgeted Cost	1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019 20																							

New Orleans East CSES																														
CSES	10JAN03 A	10JAN03	24MAR04 A	30APR04	100	3,000,000																								

Data date 01APR04
© Primavera Systems, Inc.

Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule

- Early bar
- Target bar
- Progress bar
