

## *Sewer System Evaluation and Rehabilitation Program*

### **Planning Task**

---

<b>Name</b>	Lower Ninth Ward RMAP
<b>Basin</b>	Lower Ninth Ward
<b>Council Districts</b>	C, D, E

### **Progress**

<b>Percent Complete</b>	100 %
-------------------------	-------

### **Resources**

<b>SSERP Project Engineer</b>	MWH
<b>Consultant</b>	MWH


### **Comments**

The Lower Ninth Ward RMAP was submitted to the USEPA on July 30, 2002. The USEPA accepted the Lower Ninth Ward RMAP on January 31, 2003.

**Description**

Description of proposed remedial measures to be implemented for the 9th Ward basin, which is designed to address defects identified in the 9th Ward CSES. The RMAP addresses and resolves issues related to pump station and force main capacity, and addresses measures intended to eliminate unauthorized discharges.

**Project Location**

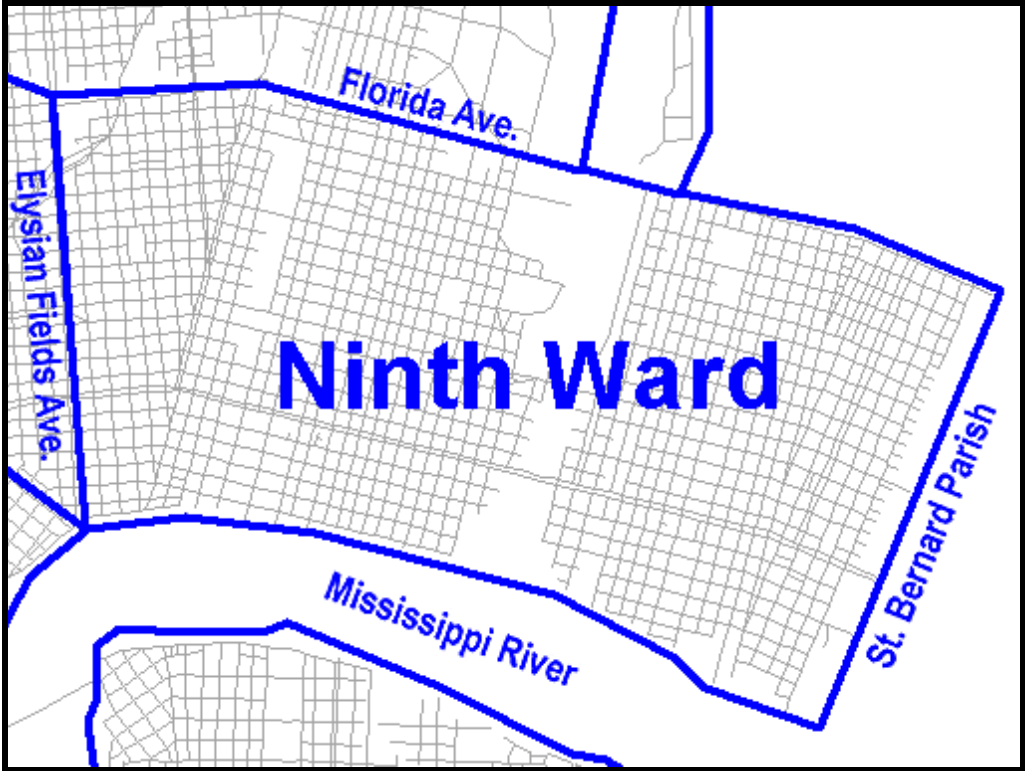

**Current Capital Cost**                      \$0

Description	Projected Start	Baseline Start	Projected Finish	Baseline Finish	%	Budgeted Cost	1996 1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019																							
Ninth Ward RMAP																														
RMAP	11APR02 A	11APR02	30JUL02 A	30JUL02	100	0																								

Start date	01JAN95
Finish date	03MAR18
© Primavera Systems, Inc.	

**Sewerage and Water Board of New Orleans**  
**Sewer System Evaluation and Rehabilitation Program**  
**Master Schedule**

-  Early bar
-  Target bar
-  Progress bar
