

Sewer System Evaluation and Rehabilitation Program

Planning Task

Name Uptown CSES
Basin Uptown
Council Districts A, B

Progress

Percent Complete 100 %

Resources

SSERP Project Engineer MWH
Consultant Roy F. Weston, Inc.


Comments

Attended the Magazine Street Merchants Association Executive Board meeting on January 6, 2004. Attended the Magazine Street Merchants Association Board meeting on January 14, 2004.

Description

Study performed to evaluate the condition and capacity of the collection system in the Uptown basin, including all pump stations in order to determine if the condition and capacity of the collection system are sufficient to prevent unauthorized discharges.

Project

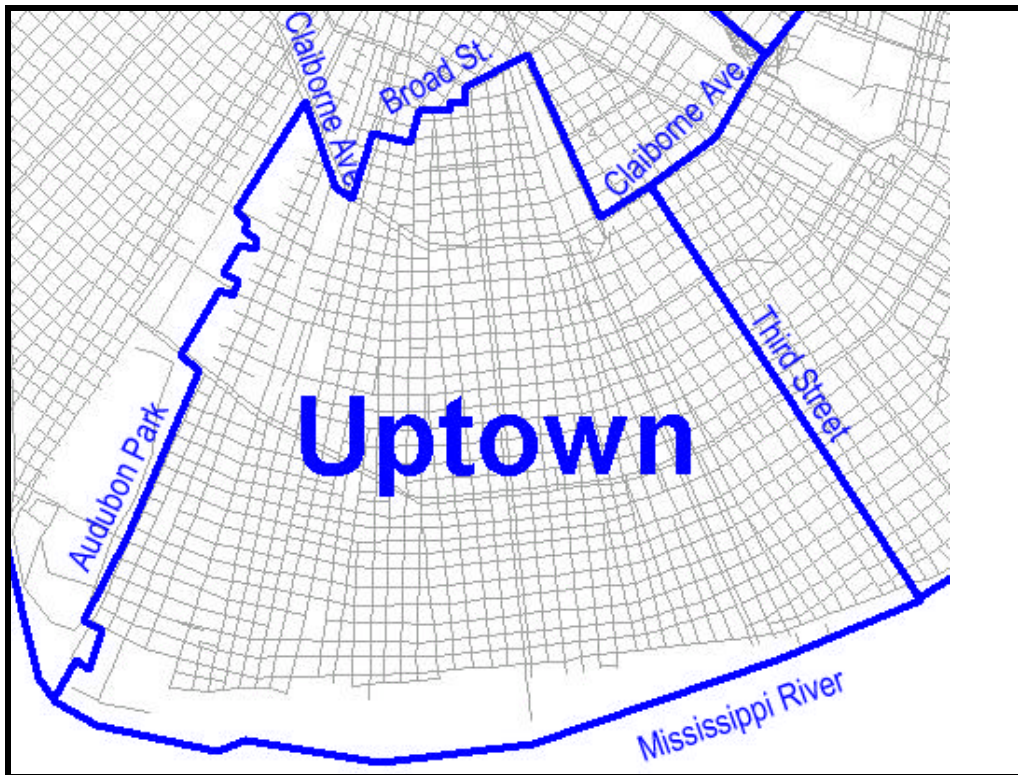

Current Capital Cost \$2,894,006

Description	Projected Start	Baseline Start	Projected Finish	Baseline Finish	%	Budgeted Cost	1996 1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019																							
Uptown CSES																														
CSES	18MAY99 A	18MAY99	30MAR00 A	30MAR00	100	2,894,006																								

Start date	01JAN95
Finish date	03MAR18
© Primavera Systems, Inc.	

Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule

- Early bar
- Target bar
- Progress bar
