

Sewer System Evaluation and Rehabilitation Program

Rehabilitation Project

Contract Number	3901
Name	Lakeview Area Sewer Rehabilitation Cleaning and CCTV Inspection
Basin	Lakeview
Council Districts	A, D
Status:	The Sewerage and Water Board certified as complete all the work performed under this contract, as required by USEPA Assistance Grant No. XP-996667-01-3, in October 2000.

Resources

SSERP Project Engineer Montgomery Watson Harza

Design Engineer Consoer Townsend Envirodyne Engineers

Contractor D&O Contractors, Inc.

Comments


Attended the Lakeview Civic Improvement Association meeting of March 14, 2001. Attended the Lakeview Civic Improvement Association meeting of May 9, 2001. Attended the Lakeview Civic Improvement Association meeting of July 11, 2001. Attended the Lakeview Civic Improvement Association meeting of November 14, 2001.

3901 - Lakeview Area Sewer Rehabilitation Cleaning and CCTV Inspection

Description


Cleaning, dye water flooding and CCTV inspection of approximately 177,660 lineal feet of primarily 8" and up to 36" sanitary sewer. The contract includes cleaning, dye water flooding, and flow control.

Project Location

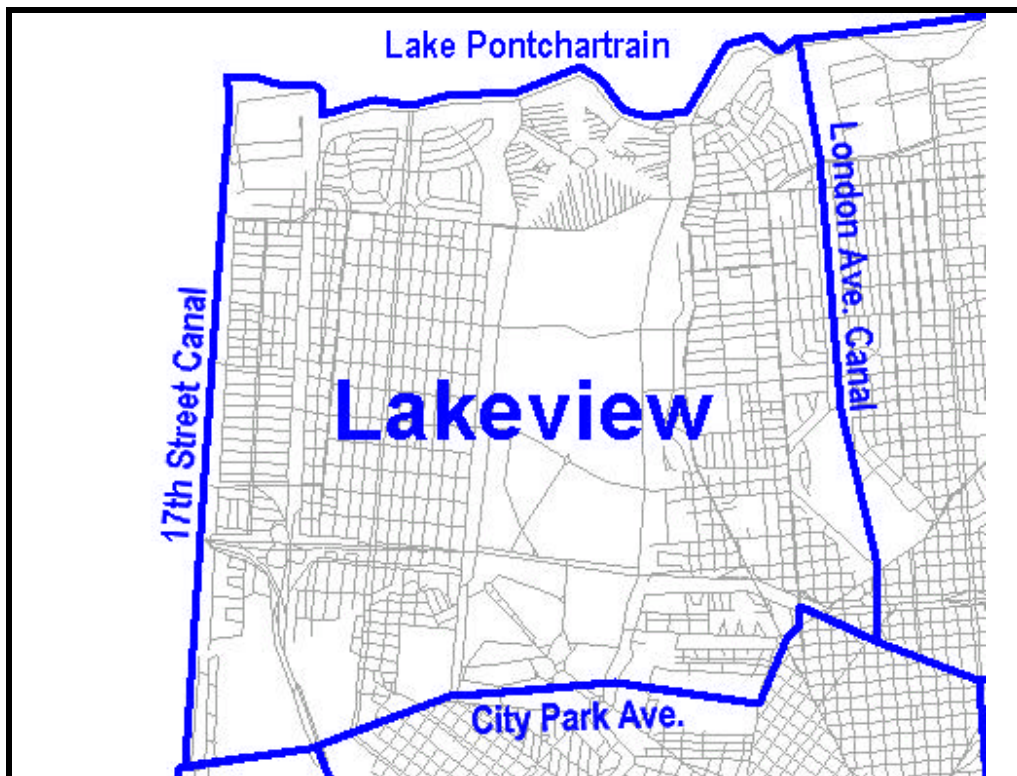

Current Capital Cost \$733,634

Description	Projected Start	Baseline Start	Projected Finish	Baseline Finish	%	Budgeted Cost	1996 1997 1998 1999 2000 2001 2002 2003 2004 2005 2006 2007 2008 2009 2010 2011 2012 2013 2014 2015 2016 2017 2018 2019																				
3901 Lakeview Cleaning & CCTV Inspection																											
Pre-Design	13JUN97 A	13JUN97	29SEP97 A	29SEP97	100	0																					
Preliminary Design	29SEP97 A	29SEP97	10FEB98 A	10FEB98	100	23,620																					
Final Design	10FEB98 A	10FEB98	09APR98 A	09APR98	100	46,124																					
Advertisement	16APR98 A	16APR98	12JUN98 A	12JUN98	100	8,368																					
Award	17JUN98 A	17JUN98	14SEP98 A	14SEP98	100	2,200																					
Construction	19OCT98 A	19OCT98	16AUG99 A	16AUG99	100	478,022																					
Field Testing	19OCT98 A	19OCT98	16AUG99 A	16AUG99	100	0																					
ESDC	19OCT98 A	19OCT98	16AUG99 A	16AUG99	100	0																					
Inspection Services	19OCT98 A	19OCT98	16AUG99 A	16AUG99	100	175,300																					
S&WB Resolution	17OCT99 A	17OCT99	17OCT99 A	17OCT99	100	0																					
Certification	23AUG00 A	23AUG00	17OCT00 A	17OCT00	100	0																					

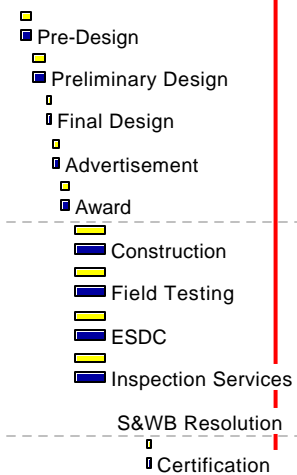

Start date	01JAN95
Finish date	03MAR18
© Primavera Systems, Inc.	

Sewerage and Water Board of New Orleans
Sewer System Evaluation and Rehabilitation Program
Master Schedule

